



North Carolina Department of Public Safety

Office of Recovery and Resiliency

Roy Cooper, Governor
Eddie M. Buffaloe Jr., Secretary

Laura H. Hogshead, Director

MEMORANDUM

TO: State Budget Director
House Appropriations Committee
Senate Appropriations Committee
Fiscal Research Division

FROM: Eddie M. Buffaloe Jr., Secretary *EMB*
Laura H. Hogshead, Director *LHH*

RE: State Funding Update for North Carolina's Hurricane Recovery (Q4)

DATE: April 28, 2022

Pursuant to Session Law 2019-250, Section 3.5(c), the Office of Recovery and Resiliency shall provide separate quarterly reports to the Director of the Budget, the standing Appropriations Committees of the Senate and the House of Representatives, and the Fiscal Research Division on the use of disaster recovery and assistance funds expended from the Hurricane Florence Recovery Fund, the State Emergency Response and Disaster Relief Fund for Hurricane Matthew, and funds appropriated for disaster relief for Hurricane Dorian.

Please find attached the quarterly report for the October – December 2021 period.

Mailing Address:
Post Office Box 110465
Durham, NC 27709



Telephone: 984.833.5350
www.ncdps.gov
www.rebuild.nc.gov

Quarterly Report: State Funding Update for North Carolina's Hurricane Recovery

October – December 2021

Submitted by: North Carolina Office of Recovery and Resiliency



Contents

Executive Summary	3
State Funding Summary Tables	8
Department of Public Safety.....	10
Department of Agriculture and Consumer Services.....	45
Department of Commerce.....	70
Department of Environmental Quality.....	72
Department of Health and Human Services	116
Department of Insurance.....	119
Department of Public Instruction	120
Elizabeth City State University	123
Fayetteville State University	125
Golden Leaf Foundation	127
Lumber River Council of Governments	130
North Carolina Community College System	132
Department of Natural and Cultural Resources	138
North Carolina Housing Finance Agency.....	140
Office of State Budget and Management	142
North Carolina State Education Assistance Authority.....	154
UNC Pembroke	157
UNC Wilmington.....	160
North Carolina Wildlife Resources Commission	162
Appendices	164

This space intentionally left blank.

Executive Summary

On October 29, 2018, SL 2018-136 created the North Carolina Office of Recovery and Resiliency (NCORR) and charged the Office with providing quarterly and annual reports on the state's recovery progress. This quarterly report outlines state-funded recovery activities from October 1, 2021 – December 31, 2021. The report is organized into three sections, which include:

1. **Executive Summary.** A brief overview of current recovery needs and activities.
2. **Summary of State Funding for Disaster Relief.** Summary reports of state-funded programs, by state agencies and departments, and the progress made to support the state's recovery from recent events.
3. **Appendix.** A detailed expenditure report (Excel spreadsheet) summarizing the status of funds for each state-appropriated program, by agency.

Access to state funds for long-term recovery is critical for the ability of state and local responding entities to meet not only the immediate recovery needs of hurricane survivors, but also make it possible for individuals and communities to participate in federal programs. These funded programs are also demonstrating enhanced abilities for state and local partners to respond to immediate needs.

For example, in this reporting period, the **Office of Budget and Management – Disaster Recovery Section (OSBM-DR)** completed 29 home repairs and/or reconstructions. Also 31 projects were 80% complete by the end of this reporting period. An example of one of these reconstructions was recently completed in New Bern using Hurricane Florence state recovery funding. This was a partnership between OSBM-DR and the Baptist on Mission (BOM) organization. BOM provided labor and the state supported \$125,000 in building materials and for demolition costs. Before (left) and after (right) reconstruction photos below:



Also, this quarter, the **Department of Agriculture** engaged in Forest Service Activities with **Agriculture Recovery Funding appropriated in SL 2018-136, Section 6.1.(23)** to reimburse 42 landowners for completing 49 practices on 1,096 acres of farmland. The Department has also allocated debris removal funds to 76 local sponsors and reports 68 contracts are fully executed and are prepared to begin work. For 38 of the 76 local sponsors, NCDA&CS funds are matching USDA Emergency Watershed Protection Program funding. In addition, three road repair projects have been completed this quarter. State funds were also used to restore 185 acres of pastureland in Duplin and Jones Counties.

In addition to communities continuing their long-term recovery from four federally declared disasters in recent years, 2020-2021 also brought unprecedented changes as the world responded to the COVID-19 pandemic. The importance of state funds to support the activities outlined in this report have proven again how crucial this support is to the state's recovery and resiliency.

Figure 1. Hurricane Matthew Declared Counties

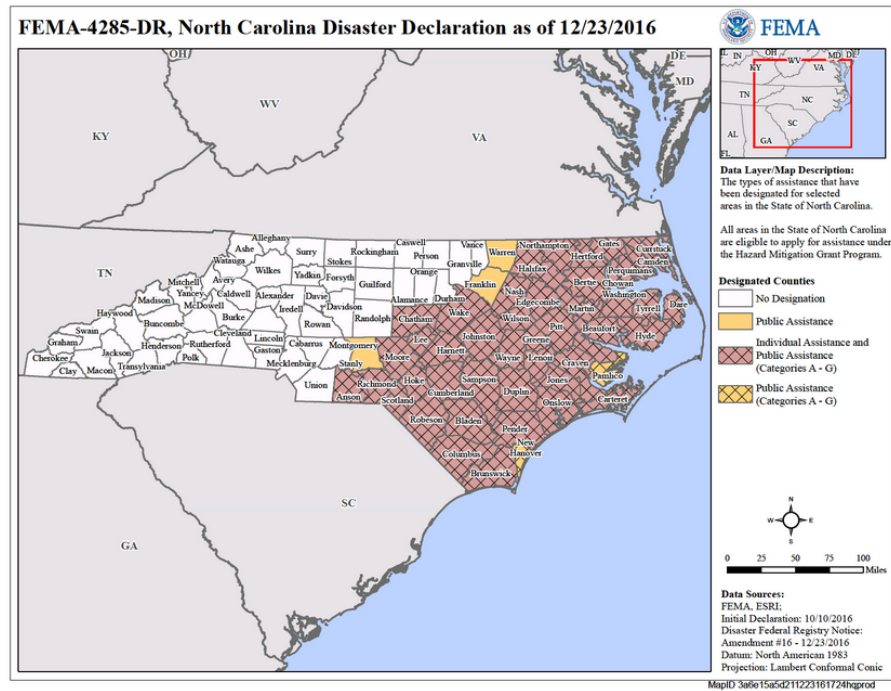


Figure 2. Hurricane Florence Declared Counties

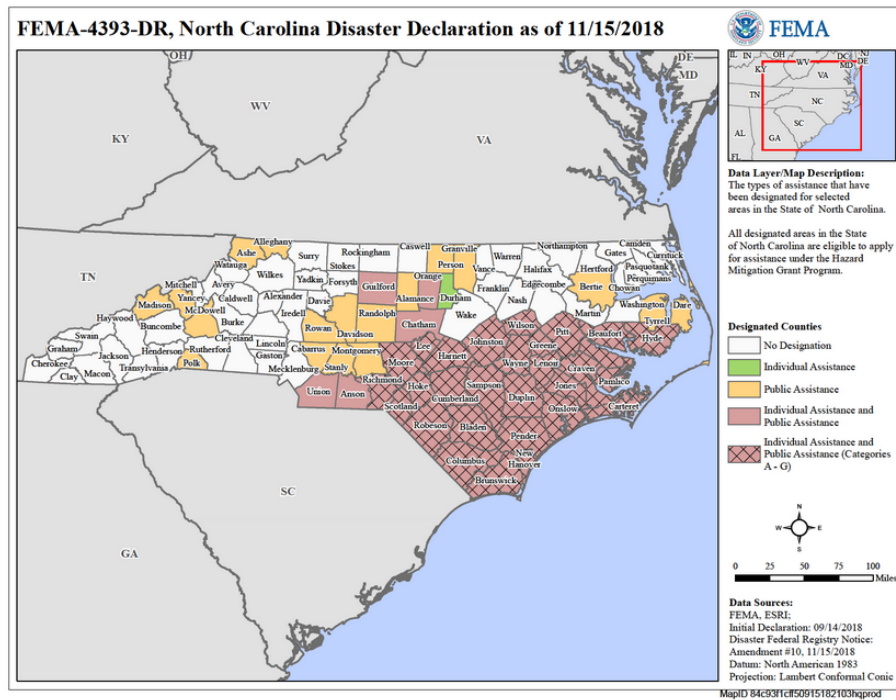


Figure 3. Tropical Storm Michael Declared Counties


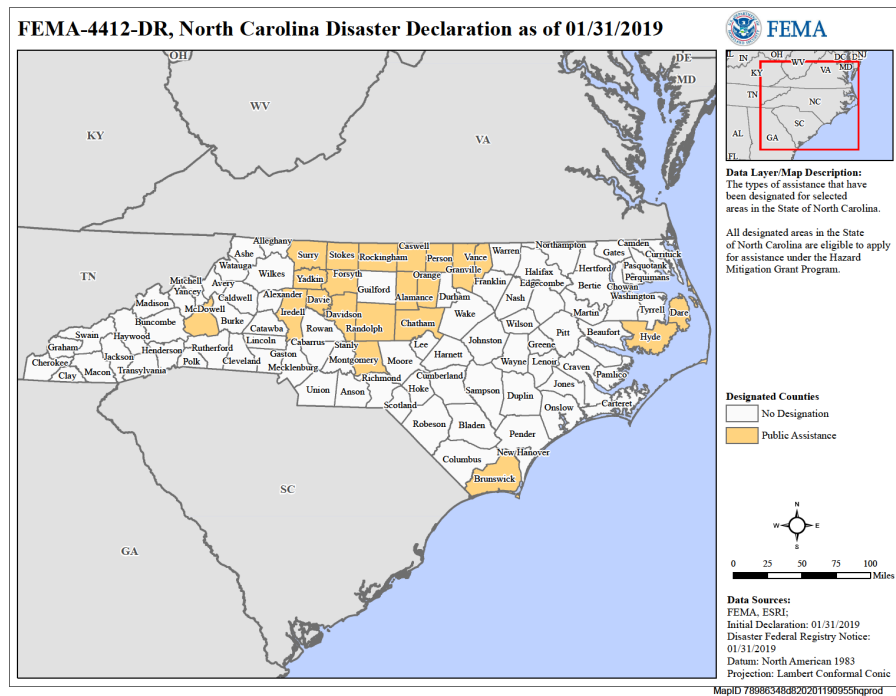


Figure 4. Hurricane Dorian Declared Counties

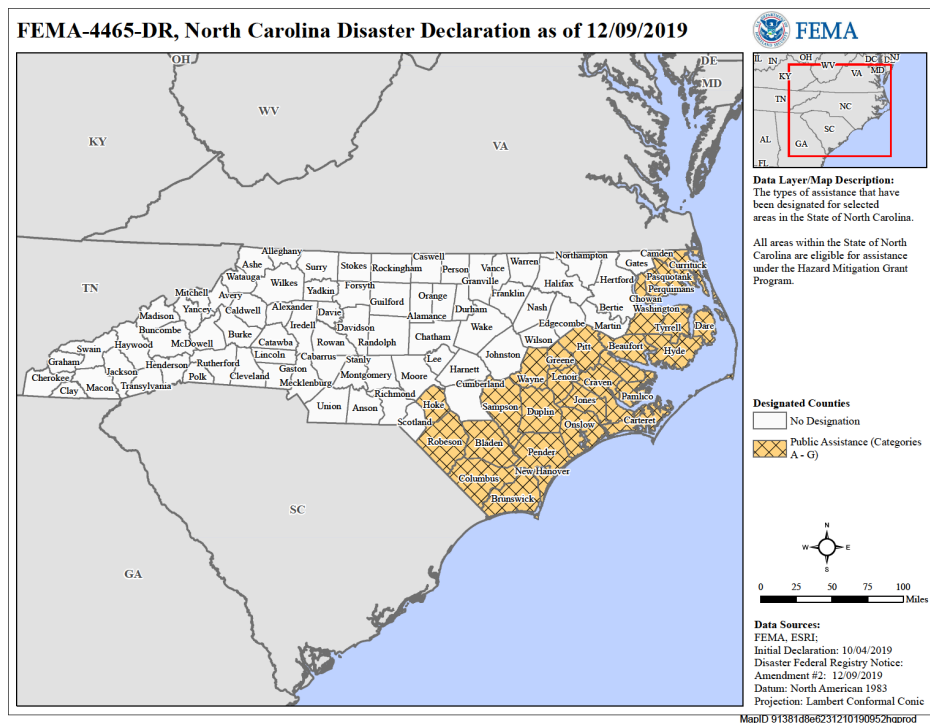

Hurricane Matthew (DR 4285) – As of this reporting period, \$128,034,786 in Individual Assistance was provided for housing and other needs assistance. The Public Assistance program for Matthew

has obligated \$496,090,577 towards repairing public facilities and infrastructure in declared communities, totaling 1,900 projects. HMGP is helping 756 property owners become more resilient against future disasters and has reimbursed \$29 million to local governments thus far. The CDBG-DR program has disbursed \$136 million including activities such as housing repairs, housing reconstructions, buyouts, small rental repairs, multi-family housing construction, and public infrastructure repairs.

Hurricane Florence (DR 4393) - At the end of this reporting period, in total, 139,814 North Carolinians received Individual Assistance, with over \$157,586,547 in funds disbursed for housing and other needs assistance. Public Assistance has worked with local partners to develop 2,925 projects totaling \$1.1 billion. For Florence, the FEMA Hazard Mitigation Grant Program (HMGP) is the process of approving 970 projects in 57 counties. North Carolina was approved for an “expedited” Hazard Mitigation Program for Florence, which is currently being implemented. Through this expedited program, NCEM is acquiring 172 properties. After receiving signed grant agreements in August of 2020, NCORR continued to launch a \$542 million CDBG-DR recovery program funded by US Department of Housing and Urban Development. NCORR opened application intake for the Homeowner Recovery Program on June 15, 2020 and there have been 3,100 new applications.

Tropical Storm Michael (DR 4412) – The state is coordinating a more limited recovery program for Tropical Storm Michael, primarily focused on providing Public Assistance for infrastructure repair in declared communities. As of the end of the reporting period, 216 Public Assistance projects have been proposed for a total of \$31,364,456. The state continues to seek additional public assistance awards for this storm.

Hurricane Dorian (DR 4465) – Making landfall on September 1, 2019, this storm resulted in significant damage to public buildings, infrastructure, businesses, and housing in a limited number of communities. In response, the state executed a state-funded Individual Assistance program in addition to the federally declared Public Assistance Program. \$970,664 has been expended in state Individual Assistance funds to assist local communities with 81 displaced households. The Public Assistance program has 495 obligated projects for an estimated cost of \$98.5 million.

These programs, in addition to those led by the state partners contributing to this report, are helping to support the unmet needs of North Carolinians and local communities across the state.

State Funding Summary Tables

Tables below represent expenses and obligations of state appropriations from SL 2016-124, SL 2017-119, SL 2017-57, SL 2018-5, SL 2018-134, SL 2018-136, SL 2018-138, SL 2019-224 and SL 2019-250, SL . Amounts reported are as of December 31, 2021.

Table 1. State Appropriations Awarded by Agency for Hurricanes Matthew, Florence, Michael and Dorian

Agency	Appropriation	Total Spent to Date	Obligations	Remaining Balance	% Remaining Balance
Administrative Office of the Courts	\$ 1,000,000.00	\$ -		\$ 1,000,000.00	100%
Department of Agricultural Services	\$ 361,150,000.00	\$ 294,514,101.81	\$ 29,894,330.80	\$ 36,741,567.39	10%
Department of Commerce	\$ 10,005,230.00	\$ 6,605,554.81	\$ 3,399,675.19	\$ -	0%
Department of Environmental Quality	\$ 86,675,000.00	\$ 52,758,765.78	\$ 5,539,382.72	\$ 28,376,851.50	33%
Department of Health and Human Services	\$ 12,000,000.00	\$ 9,750,775.10		\$ 2,249,224.90	19%
Department of Insurance	\$ 1,000,000.00	\$ 326,387.12	\$ -	\$ 673,612.88	67%
Department of Natural and Cultural Resources	\$ 5,000,000.00	\$ 470,751.72	\$ 909,608.00	\$ 3,619,640.28	72%
Department of Public Instruction	\$ 93,200,000.00	\$ 91,129,113.00	\$ -	\$ 2,070,887.00	2%
Department of Public Safety	\$ 378,520,946.00	\$ 309,050,531.33	\$ 10,131,878.77	\$ 59,338,535.90	16%
Elizaeth City State University	\$ 5,200,000.00	\$ 1,796,403.84	\$ 2,301,327.56	\$ 1,102,268.60	21%
Golden Leaf	\$ 114,500,000.00	\$ 76,475,584.24	\$ 30,067,055.42	\$ 7,957,360.34	7%
Housing Finance Agency	\$ 30,000,000.00	\$ 21,692,318.40	\$ 3,825,681.60	\$ 4,482,000.00	15%
Lumberton Council of Governments	\$ 5,000,000.00	\$ 5,000,000.00	\$ -	\$ -	0%
NC Community Colleges	\$ 26,100,000.00	\$ 23,883,240.66	\$ 1,735,913.07	\$ 480,846.27	2%
Office of State Budget and Management	\$ 195,543,018.00	\$ 122,241,104.87	\$ 59,795,405.11	\$ 13,506,508.02	7%
University of North Carolina	\$ 40,375,501.00	\$ 34,329,916.02	\$ 93,337.60	\$ 5,952,247.38	15%
Wildlife Resource Commission	\$ 1,550,000.00	\$ 1,442,229.98		\$ 107,770.02	7%
Totals	\$ 1,366,819,695.00	\$ 1,051,466,778.68	\$ 147,693,595.84	\$ 167,659,320.48	12%

Table 2. State Appropriations Awarded by Program for Hurricanes Matthew, Florence, Michael, Dorian, Multiple & Non-Disaster

PROGRAM	Allocation or Appropriation	Total Spent to Date	Obligations	Remaining Balance	% Remaining Balance
Administration	\$ 2,000,000.00	\$ 1,021,843.52	\$ 978,156.48	\$ -	0%
Agricultural	\$ 361,150,000.00	\$ 294,514,101.81	\$ 29,894,330.80	\$ 36,741,567.39	10%
Economic Development	\$ 10,005,230.00	\$ 5,916,260.52		\$ 4,088,969.48	41%
Education	\$ 164,875,501.00	\$ 151,138,673.52	\$ 4,130,578.23	\$ 9,606,249.25	6%
Environmental	\$ 93,225,000.00	\$ 45,033,643.29	\$ 5,562,540.79	\$ 29,028,815.92	31%
GRANTS	\$ 98,888,000.00	\$ 58,830,678.13	\$ 38,396,768.87	\$ 1,660,553.00	2%
Health and Human Services	\$ 12,000,000.00	\$ 9,750,775.10		\$ 2,249,224.90	19%
Housing Programs & Assistance	\$ 177,626,776.00	\$ 84,815,047.23	\$ 3,825,681.60	\$ 58,986,047.17	33%
Local Government Infrastructure	\$ 42,000,000.00	\$ 64,878,752.21	\$ 9,722,744.45	\$ 7,398,503.34	18%
MATCH	\$ 353,763,964.00	\$ 293,649,390.20	\$ 46,308,065.29	\$ 13,806,508.51	4%
Risk Management	\$ 51,285,224.00	\$ 41,917,613.15	\$ 8,874,729.33	\$ 4,092,881.52	8%
Totals	\$ 1,366,819,695.00	\$ 1,051,466,778.68	\$ 147,693,595.84	\$ 167,659,320.48	12%

Table 3. State Appropriations Awarded by Agency for Hurricane Matthew Only

Department of Agricultural Services	\$ 60,450,000.00	\$ 37,813,691.26	\$ 10,415,297.26	\$ 12,221,011.48	20%
Department of Commerce	\$ 10,005,230.00	\$ 6,605,554.81	\$ 3,399,675.19	\$ -	0%
Department of Environmental Quality	\$ 13,600,000.00	\$ 9,638,104.19	\$ 886,449.93	\$ 3,075,445.88	23%
Department of Insurance	\$ 69,523.00	\$ 69,523.00	\$ -	\$ -	0%
Department of Public Safety	\$ 78,926,776.00	\$ 47,554,900.68		\$ 31,371,875.32	40%
Golden Leaf	\$ 65,000,000.00	\$ 54,147,150.83	\$ 6,323,069.26	\$ 4,529,779.91	7%
Housing Finance Agency	\$ 20,000,000.00	\$ 16,174,318.40	\$ 3,825,681.60	\$ -	0%
Lumberton Council of Governments	\$ 5,000,000.00	\$ 5,000,000.00	\$ -	\$ -	0%
NC Community Colleges	\$ 2,700,000.00	\$ 2,699,829.73		\$ 170.27	0%
Office of State Budget and Management	\$ 135,349,112.00	\$ 94,136,925.12	\$ 30,788,457.88	\$ 10,423,729.00	8%
Totals	\$ 391,100,641.00	\$ 273,839,998.02	\$ 55,638,631.12	\$ 61,622,011.86	16%

Table 4. State Appropriations Awarded by Agency for Hurricane Florence Only

Agency	Allocation or Appropriation	Total Spent to Date	Obligations	Remaining Balance	% Remaining Balance
Administrative Office of the Courts	\$ 1,000,000.00	\$ -		\$ 1,000,000.00	100%
Department of Agricultural Services	\$ 300,700,000.00	\$ 256,700,410.55	\$ 19,479,033.54	\$ 24,520,555.91	8%
Department of Environmental Quality	\$ 55,425,000.00	\$ 43,071,170.16	\$ 4,652,932.79	\$ 7,700,897.05	14%
Department of Health and Human Services	\$ 12,000,000.00	\$ 9,750,775.10		\$ 2,249,224.90	19%
Department of Insurance	\$ 930,477.00	\$ 256,864.12	\$ -	\$ 673,612.88	72%
Department of Natural and Cultural Resources	\$ 5,000,000.00	\$ 470,751.72	\$ 909,608.00	\$ 3,619,640.28	72%
Department of Public Instruction	\$ 91,500,000.00	\$ 89,429,113.00		\$ 2,070,887.00	2%
Department of Public Safety	\$ 274,794,170.00	\$ 244,347,649.83	\$ 3,573,481.91	\$ 26,873,038.26	10%
Golden Leaf	\$ 49,500,000.00	\$ 22,328,433.41	\$ 23,743,986.16	\$ 3,427,580.43	7%
Housing Finance Agency	\$ 10,000,000.00	\$ 5,518,000.00		\$ 4,482,000.00	45%
NC Community Colleges	\$ 23,400,000.00	\$ 21,183,410.93	\$ 1,735,913.07	\$ 480,676.00	2%
Office of State Budget and Management	\$ 27,888,000.00	\$ 16,144,410.18	\$ 11,743,589.82	\$ -	0%
University of North Carolina	\$ 40,375,501.00	\$ 34,329,916.02	\$ 93,337.60	\$ 5,952,247.38	15%
Wildlife Resource Commission	\$ 1,050,000.00	\$ 942,280.28		\$ 107,719.72	10%
Totals	\$ 893,563,148.00	\$ 744,473,185.30	\$ 65,931,882.89	\$ 83,158,079.81	9%

Table 5. State Appropriations Awarded by Agency for Tropical Storm Michael Only

Agency	Allocation or Appropriation	Total Spent to Date	Obligations	Remaining Balance	% Remaining Balance
Office of State Budget and Management	\$ 4,176,245.00	\$ 1,183,352.49	\$ 2,992,892.51	\$ -	0%
Totals	\$ 4,176,245.00	\$ 1,183,352.49	\$ 2,992,892.51	\$ -	0%

Table 6. State Appropriations Awarded by Agency for Hurricane Dorian Only

Agency	Allocation or Appropriation	Total Spent to Date	Obligations	Remaining Balance	% Remaining Balance
Department of Public Instruction	\$ 1,700,000.00	\$ 1,700,000.00	\$ -	\$ -	0%
Department of Public Safety	\$ 5,000,000.00	\$ 4,771,650.00		\$ 286,000.00	6%
Elizaeth City State University	\$ 5,200,000.00	\$ 1,796,403.84	\$ 2,301,327.56	\$ 4,687,412.45	90%
Office of State Budget and Management	\$ 22,379,661.00	\$ 10,329,535.10	\$ 9,270,464.90	\$ -	0%
Totals	\$ 34,279,661.00	\$ 18,597,588.94	\$ 11,571,792.46	\$ 4,973,412.45	15%

Table 7. State Appropriations Awarded by Agency for Multiple Storms

Agency	Allocation or Appropriation	Total Spent to Date	Obligations	Remaining Balance	% Remaining Balance
Department of Environmental Quality	\$ 17,650,000.00	\$ 49,491.43	\$ -	\$ 17,600,508.57	100%
Department of Public Safety	\$ 10,000,000.00	\$ 6,509,794.68	\$ 2,624,933.00	\$ 865,272.32	9%
Office of State Budget and Management	\$ 5,750,000.00	\$ 446,881.98	\$ 5,000,000.00	\$ 303,118.02	5%
Totals	\$ 33,400,000.00	\$ 7,006,168.09	\$ 7,624,933.00	\$ 18,768,898.91	56%

Table 8. State Appropriations Awarded by Agency for Non-Disasters

Agency	Allocation or Appropriation	Total Spent to Date	Obligations	Remaining Balance	% Remaining Balance
Department of Public Safety	\$ 9,800,000.00	\$ 5,866,536.14	\$ 3,933,463.86	\$ -	0%
Wildlife Resource Commission	\$ 500,000.00	\$ 499,949.70		\$ 50.30	0%
Totals	\$ 10,300,000.00	\$ 6,366,485.84	\$ 3,933,463.86	\$ 50.30	0%

Department of Public Safety

Federal Programs

1. Individual Assistance

The mission of FEMA's Individual Assistance Program is to provide rapid help to individual disaster survivors with uninsured costs during a disaster response and immediate recovery. Individual Assistance can include providing temporary housing, lodging expenses, basic household expenses, and home repairs. In some cases, if the threshold for a federal IA disaster declaration is not met or there is an additional need for assistance, a state-funded Individual Assistance Program will provide and/or supplement federal assistance. State-funded Individual Assistance was administered by NC Emergency Management for several recent disasters.

Responsible Department and Agency

Department of Public Safety, NC Division of Emergency Management

Summary of Activities (October – December 2021)

Hurricane Florence: The FEMA Direct Housing Program closed with 12 families remaining with permanent housing needs. Collaborating on repair needs with the Office of State Budget recovery, the twelve families relocated to permanent housing by February 2021. Ending in 2020, the Disaster Case Management grant funded recovery efforts for 6,657 survivors. NCEM-Individual Assistance has continued to seek housing and repair solutions for 21 survivors through referrals to NC Rebuild, non-profits and Long-Term Recovery groups.

Hurricane Dorian: North Carolina administered a state-funded Individual Assistance Program for Hurricane Dorian. Grants for approximately fifty-two (52) families enabled them to successfully repair or rebuild new homes especially in hard hit Hyde County. The Small Business Administration awarded 108 families a total of \$6,082,000 in loans towards recovery assistance. Grant closeout completed in December 2020. Zero households remain in temporary housing and VOADs (Volunteer Organizations Assisting with Disasters) continue to work on repair and reconstruction projects.

2. Public Assistance

Hurricane Matthew DR-4285: The mission of FEMA's Public Assistance Program is to aid state, territorial, Indian tribal, and local governments, and certain types of private non-profit (PNP) organizations so communities can quickly respond to and recover from major disasters or

emergencies declared by the President. Through the PA Program, FEMA provides supplemental, federal disaster grant assistance for debris removal, emergency protective measures, and the restoration of disaster-damaged, publicly owned facilities and the facilities of certain PNP organizations. FEMA will provide a reimbursement grant of at least 75% of eligible costs, with the state and local governments sharing the remaining 25%. The performance metrics report on state match expenditures.

Responsible Department and Agency

Department of Public Safety, NC Division of Emergency Management

Performance Metrics

- a. Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution: 15
 - Average number of days from fund distribution to project commencement: This benchmark is contingent upon the amount of time it takes to identify damages and complete the project formulation.
 - Average number of days from project commencement to project completion: The Applicant determines when the projected commences. The oversight for this would be between the Applicant and FEMA.
- b. Amount and % spent/obligated on administrative activities by Program.
 - N/A – FEMA covers 100% of administrative/management costs
- c. Amount spent on State Match on behalf of recipients by program: \$74,281,776

Recent Activities (October - December 2021)

During this quarter, 0 projects were obligated. Of 517 large projects, there are 225 open projects. Large Project Final Inspections and closeouts continue.

Contact

Todd Wright, Assistant Director-Recovery Chief, 919-215-1672, Todd.Wright@ncdps.gov

Hurricane Florence DR-4393: The mission of FEMA’s Public Assistance Program is to aid state, territorial, Indian tribal, and local governments, and certain types of private non-profit (PNP) organizations so communities can quickly respond to and recover from major disasters or emergencies declared by the President. Through the PA Program, FEMA provides supplemental, federal disaster grant assistance for debris removal, emergency protective measures, and the restoration of disaster-damaged, publicly owned facilities and the facilities of certain PNP organizations.

Responsible Department and Agency

Department of Public Safety, NC Division of Emergency Management

Performance Metrics

- a. Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution: 40
 - Average number of days from fund distribution to project commencement: This benchmark is contingent upon the amount of time it takes to identify damages and complete the project formulation.
 - Average number of days from project commencement to project completion: The Applicant determines when the projected commences. The oversight for this would be between the Applicant and FEMA.
- b. Amount and % spent/obligated on administrative activities by Program.
 - N/A – FEMA covers 100% of administrative/management costs N/A
- c. Amount spent on State Match on behalf of recipients by program: \$154,846,549

Recent Activities (October – December 2021)

During this quarter, 20 projects were obligated. Of 690 large projects, there are 428 open projects. Final Inspections and closeouts continue. Hagerty Consulting, Inc. conducted small project validations.

Contact

Todd Wright, Assistant Director-Recovery Chief, 919-215-1672, Todd.Wright@ncdps.gov

Tropical Storm Michael DR-4412: The mission of FEMA’s Public Assistance Program is to aid state, territorial, Indian tribal, and local governments, and certain types of private non-profit (PNP) organizations so communities can quickly respond to and recover from major disasters or emergencies declared by the President. Through the PA Program, FEMA provides supplemental, federal disaster grant assistance for debris removal, emergency protective measures, and the restoration of disaster-damaged, publicly owned facilities and the facilities of certain PNP organizations.

Responsible Department and Agency

Department of Public Safety, NC Division of Emergency Management

Performance Metrics

- a. Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution: 59
 - Average number of days from fund distribution to project commencement. This benchmark is contingent upon the amount of time it takes to identify damages and complete the project formulation.

- Average number of days from project commencement to project completion: The Applicant determines when the projected commences. The oversight for this would be between the Applicant and FEMA.
- b. Amount and % spent/obligated on administrative activities by Program.
 - N/A – FEMA covers 100% of administrative/management costs N/A
- c. Amount spent on State Match on behalf of recipients by program: \$2,165,009

Recent Activities (October – December 2021)

During this quarter, 0 projects were obligated. 33 projects, there are 26 open projects. Large project final inspections and closeouts continue.

Contact

Todd Wright, Assistant Director-Recovery Chief, 919-215-1672, Todd.Wright@ncdps.gov

Hurricane Dorian DR-4465: The mission of FEMA’s Public Assistance Program is to aid state, territorial, Indian tribal, and local governments, and certain types of private non-profit (PNP) organizations so communities can quickly respond to and recover from major disasters or emergencies declared by the President. Through the PA Program, FEMA provides supplemental, federal disaster grant assistance for debris removal, emergency protective measures, and the restoration of disaster-damaged, publicly owned facilities and the facilities of certain PNP organizations.

Responsible Department and Agency

Department of Public Safety, NC Division of Emergency Management

Performance Metrics

- a. Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution: 18
 - Average number of days from fund distribution to project commencement. This benchmark is contingent upon the amount of time it takes to identify damages and complete the project formulation.
 - Average number of days from project commencement to project completion: The Applicant determines when the projected commences. The oversight for this would be between the Applicant and FEMA.
- b. Amount and % spent/obligated on administrative activities by Program.
 - N/A – FEMA covers 100% of administrative/management costs N/A
- c. Amount spent on State Match on behalf of recipients by program: \$11,020,558

Recent Activities (October – December 2021)

During this quarter, 2 projects were obligated. Of 70 large projects, there are 44 open projects. Large Project Final Inspections and closeouts continue.

Contact

Todd Wright, Assistant Director-Recovery Chief, 919-215-1672, Todd.Wright@ncdps.gov

3. Hazard Mitigation

Hurricane Matthew DR-4285, Hurricane Florence DR-4393, Tropical Storm Michael DR-4412, Hurricane Dorian DR-4465, **COVID-19 DR-4487**; Winter Storms 2020 DR-4543, Hurricane Isaias DR-4568, Tropical Storm Eta DR-4588; **TS Fred DR 4617**

The mission of FEMA's Hazard Mitigation Grant Program is to assist North Carolinians, communities, state agencies, local governments and businesses to become less vulnerable to the impacts of natural hazards through the effective administration of hazard mitigation grants, floodplain management, and a coordinated approach to mitigation policy through state, regional and local planning activities. Through the Hazard Mitigation Grant Program, FEMA provides federal disaster grant assistance for eligible mitigation projects related to residential structures and publicly owned facilities. There are 90 mitigation projects ongoing in North Carolina for disasters DR-4285 and DR-4393-Expedited presently. The State has received, but not started work, 48 of 72 awards expected under DR-4393 and 2 of 4 awards expected awards for DR-4412. There are still 50 projects pending FEMA review and approval for DR-4393 Full Program, DR-4412, DR-4465 and DR-4543. The State will submit another 8 projects to FEMA for DR-4568 on 14 Oct and is working three future grants to submit by August 2022.

Responsible Department and Agency

Department of Public Safety, NC Division of Emergency Management

Recent Activities for Current Reporting Period (October - December 2021)

Work continues to answer additional multiple Requests for Information (RFIs) from FEMA RIV for projects in DR-4393 full program, DR-4412, DR-4465, DR-4543 and DR-4568. Received additional awards for projects that have cleared the RFI process, increasing our State's number of awarded projects for both DR-4393 and DR-4412. The Section also continues working on completing projects in DR-4285 (Hurricane Matthew) with some projects already forwarded to FEMA RIV for closeout.

Performance Metrics

- Average Time for Project Delivery by Program

- Average number of days from application to fund distribution: Average of 12 Months
- Average number of days from fund distribution to project commencement: This benchmark is contingent upon the amount of time it takes for communities to get contracts in place – Average 90-120 Days.
- Average number of days from project commencement to project completion: 1,065 Days. The Grant Period of Performance is set at 36 months post application.
- Amount and % spent/obligated on administrative activities by Program. Management Costs to Date Allocated/Spent - \$8,004,619/\$4,749,545(59.3%)
- Amount and % spent/obligated on behalf of recipients by Program. Project Costs awarded to Date/Spent – \$145,787,570/\$37,387,087 (25.6%)

Contact

Steve McGugan, Assistant Director-Hazard Mitigation, 919-873-5843,
steve.mcgugan@ncdps.gov

State Programs

1. Emergency Sheltering and Short-Term Housing Needs

SL 2016-124, Subsection 4.1(2)

Funds provided to support emergency sheltering and short-term housing needs supported the state-funded Transitional Sheltering Assistance (TSA) program, which housed families in hotels until they could identify a permanent housing solution. These funds also supported the state's Disaster Rental Assistance Program (DRAP). In total, \$9,000,000 was allocated for these programs and \$8,636,370 has been spent.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 9,000,000
Expended	\$ 8,636,370
Obligated	\$ 0
Unobligated Balance	\$ 363,630

Performance Metrics

- a. Average Time for Project Delivery by Program – This program was launched prior to December 1, 2019, prior to the reporting requirement.

- b. Amount and % Spent/Obligated on Administrative Activities by Program - \$0 and 0% of this appropriation. Staff costs are covered by appropriations for current operations.
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program - \$8,636,370 (96%)

Recent Activities (October - December 2021)

Since this program and funding was for Hurricane Matthew and was mostly administered and spent in the immediate aftermath of the storm. \$305.00 was spent during this quarter.

Contact

Todd Wright, Assistant Director-Recovery Chief, 919-215-1672, Todd.Wright@ncdps.gov

2. State Acquisition Relocation Fund (SARF)

SL 2016-125 and Subsection 4.1(4), SL 2018-5 and Subsection 5.6(b)(5), SL 2019-224, Subsection 2.1(4)

This funding supports the State Assistance and Relocation Fund (SARF) reimbursement payments for 472 Hurricane Matthew and 172 Hurricane Florence Expedited home acquisitions and provides gap payments to those families in order for them to move into housing equal to their old home and not located in the flood plain.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

	SL 2016-125	SL 2018-5	SL 2019-224
Appropriated	\$ 11,132,000.00	\$ 17,424,000.00	\$ 8,000,000
Expended	\$ 930,329.00	\$ 2,092,448.00	\$ 0.00
Obligated	\$ 0.00	\$ 0.00	\$ 0.00
Unobligated Balance	\$ 10,201,671.00	\$ 15,331,552.00	\$ 8,000,000

Performance Metrics

- a. Average Time for Project Delivery by Program – NA
 - i. Average number of days from application to fund distribution - 30
 - ii. Average number of days from fund distribution to project commencement – NA
 - iii. Average number of days from project commencement to project completion - NA
- b. Amount and % spent/obligated on administrative activities by Program to Date – 12% to Admin activities.

- c. Amount and % spent/obligated on behalf of recipients by Program – 88% paid to recipients.

Recent Activities for Current Reporting Period (October - December 2021)

No reimbursement requests were received this quarter.

Contact

Steve McGugan, NCEM, steve.mcgugan@ncdps.gov

3. Volunteer Organizations Assisting with Disasters (VOAD)

SL 2018-136, Subsection 61(29)

The grant was awarded to six organizations in September 2019. Allocations for this program total \$2,000,000. All funds have been obligated. The maximum that could be awarded to any single VOAD is \$500,000.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$	2,000,000
Expended	\$	834,557
Obligated	\$	1,165,443
Unobligated Balance	\$	0

Performance Metrics

- a. Average Time for Project Delivery by Program – This program was launched prior to December 1, 2019, prior to the reporting requirement.
- b. Amount and % Spent/Obligated on Administrative Activities by Program - \$0 and 0% of this appropriation. Staff costs are covered by receipts and appropriations for current operations.
- c. Amount and % Spent/Obligated on Behalf of Recipients by the Program - \$834,557.11 expended (42%) / \$2,000,000 obligated (100%)

Recent Activities for Current Reporting Period (October - December 2021)

Due to COVID-19 impacts, recipients' activities have slowed with requests to begin program implementation second and third quarters 2020. Multiple organizations were realigning their project scopes, deliverables and timelines with the change in volunteer availability and increased utilization of contractors.

Contact

Matt Kemnitz, Assistant Director of Administration, NCEM (919) 817-2511

4. Local Government Assistance

SL 2018-136, Subsection 6.1(25); SL 2018-138, Subsection 1.5(1)

A total of 17 communities have received funds, ranging from \$200,000 to \$1,000,000. Allocations for the grant program total \$8,000,000 of which \$8,000,000 have been expended.

For the state's Loan Program, SL 2018-138, Subsection 1.5(1), 14 communities have participated and received requested loan amounts, ranging from \$24,909 to \$2,000,000. Allocations for this program total \$20,000,000, of which \$20,000,000 has been expended. A total of \$4,013,633 in loan repayments have been received this fiscal year.

Responsible Department and Agency

Department of Public Safety, NC Office of Recovery and Resiliency

Funding Allocation Update

Grants

Appropriated	\$ 8,000,000
Expended	\$ 8,000,000
Obligated	\$ 0
Unobligated Balance	\$ 0

Loans

Appropriated	\$ 20,000,000
Expended	\$ 20,000,000
Obligated	\$ 0
Unobligated Balance	\$ 0

Performance Metrics

- a. Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution: **30-45 days** for the grants program. Loans are based on actual project expenditures.
 - Average number of days from fund distribution to project commencement - Not applicable. Grants and Loans are awarded for a broad range purposes with varying expenditure schedules.
 - Average number of days from project commencement to project completion - Not applicable. Grants and Loans are awarded for a broad range purposes with varying expenditure schedules.

- b. Amount and % Spent/Obligated on Administrative Activities by Program. \$0 and 0% of this appropriation. Staff costs are covered by appropriations to NCORR for administrative functions.
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program. For the Grant Program, \$8,000,000 had been obligated and expended (100%) / For the Loan Program \$20,000,000 had been obligated and expended (100%)

Recent Activities for Current Reporting Period (October – December 2021)

Local communities continue to benefit from the state’s Loans programs while waiting for their reimbursement from FEMA. NCORR is working with the communities and disbursing funds as needed while their projects are waiting for FEMA reimbursement. There was no activity for the quarter.

Contact

Mary Massey, Budget Director, NCORR

5. Stanly County Airport Training Facility Broadband Infrastructure

SL 2018-5, Subsection 5.6(b)(2)f

This project was completed following Hurricane Matthew. Fiber and end termination equipment installation is complete and permits have been pulled and are posted to the construction site. Allocations for this program total \$100,000, all of which have been expended.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 100,000
Expended	\$ 100,000
Obligated	\$ 0
Unobligated Balance	\$ 0

Performance Metrics

- a. Average Time for Project Delivery by Program - This program was launched prior to December 1, 2019, prior to the reporting requirement.
- b. Amount and % Spent/Obligated on Administrative Activities by Program. \$0 and 0% of this appropriation. Staff costs are covered by appropriations for current operations.

- c. Amount and % Spent/Obligated on Behalf of Recipients by Program. \$100,000 expended (100%).

Recent Activities for Current Reporting Period (October - December 2021)

The tower site is complete. This includes adding in-fill dirt and fencing around the site in accordance with local ordinance. Open Broadband has been installed wireless data services and the site now has access to broadband. Stanly County is working with other commercial broadband providers (Verizon/AT&T) to consider adding their equipment to this newly constructed tower. Any expenses encumbered as a result of this work would be out of the scope of this appropriation.

Contact

Greg Hauser, (919) 825-2262, Greg.Hauser@ncdps.gov

6. Resilient Redevelopment Planning

SL 2016-124, Subsection 4.1(3)

Allocations for this program total \$11,500,000, all of which have been expended for creation of resilient redevelopment plans for the 50 federally declared disaster counties impacted by Hurricane Matthew. The primary goals were to: 1) develop strategic plans and actions, and 2) define any unmet funding needs required to implement those actions after other funds are used. The resulting resilient redevelopment plans serve as the foundation for any supplemental funding received through Congress, the North Carolina General Assembly and other funding sources. These plans also provide the basis for the state's Recovery Action Plan required by the U.S. Department of Housing and Urban Development needed to spend funds allocated through the Community Development Block Grant – Disaster Relief program.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 11,500,000
Expended	\$ 11,500,000
Obligated	\$ 0
Unobligated Balance	\$ 0

Performance Metrics

- a. Average Time for Project Delivery by Program- This program was launched prior to December 1, 2019, prior to the reporting requirement.

- b. Amount and % Spent/Obligated on Administrative Activities by Program - This program was launched prior to December 1, 2019, prior to the reporting requirement.
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program- This program was launched prior to December 1, 2019, prior to the reporting requirement.

Recent Activities for Current Reporting Period (October - December 2021)

Activity was completed prior to the reporting period.

Contact

Chris Koltyk; 919-825-2310; Chris.Koltyk@ncdps.gov

7. 211 Activities

SL 2018-5, Subsection 5.6(b)(2)b

In November 2019, the General Assembly appropriated \$250,000 in recurring funds to the United Way to provide ongoing 211 support to state recovery programs, S.L. 2019-250, Subsection 1.3(a)(1), all of which all have been expended.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 250,000
Expended	\$ 250,000
Obligated	\$ 0
Unobligated Balance	\$ 0

Performance Metrics

- a. Average Time for Project Delivery by Program - This program was launched prior to December 1, 2019, prior to the reporting requirement.
- b. Amount and % Spent/Obligated on Administrative Activities by Program. \$250,000 expended (100%). This is an administrative function.
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program. \$0 expended.

Recent Activities for Current Reporting Period (October - December 2021)

Funds were fully expended prior to the reporting period.

Contact

Keith Acree, Public Information Officer, keith.acree@ncdps.gov

8. Flood Warning Systems, Inundation Zones and Dam Impact Assessments

SL 2018-5, Subsection 5.6(b)(2)c

Through this project, NCEM was able to: 1) install new radar and ultrasonic water level sensors; 2) develop flood inundation mapping libraries and building-level risk assessments; 3) perform dam breach analyses; and 4) conduct building and roadway risk assessments for intermediate and high hazard dams to improve situational awareness for first responders and emergency managers during flood related weather events. All gauge data and flood inundation mapping libraries will be made available to the public through the North Carolina Flood Inundation Mapping and Alert Network (FIMAN) application (<https://fiman.nc.gov/>). Dam failure inundation boundaries and building and roadway risk assessment data will be available to first responders through the secure State Emergency Response Application (SERA - <https://sera.nc.gov/sera/>). Allocations for this program total \$2,835,224, all of which have been expended.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 2,835,224
Expended	\$ 2,835,224
Obligated	\$ 0
Unobligated Balance	\$ 0

Summary of Activities

To date, the following activities have been completed:

1. Installed 25 new radar water level gauges.
2. Completed building level flood risk assessment for flood inundation libraries for the FIMAN application for 25 radar water level gauges.
3. Completed building level flood risk assessment for flood inundation libraries for the FIMAN application for 30 existing FIMAN water level gauges.
4. Completed building level flood risk assessment based on extended flood inundation libraries for the FIMAN application for 20 existing FIMAN water level gauges.
5. Completed dam breach analyses for 76 dams and dam and building level risk assessment for 154 dams.

Performance Metrics

- a. Average Time for Project Delivery by Program- This program was launched and completed prior to December 1, 2019 reporting requirement.
- b. Amount and % spent/obligated on administrative activities by program- This program was launched and completed prior to December 1, 2019 reporting requirement.
- c. Amount and % spent/obligated on behalf of recipients by program- This program was launched and completed prior to December 1, 2019 reporting requirement.

Recent Activities for Current Reporting Period (October - December 2021)

Funds were fully expended prior to the reporting period.

Contact

Chris Koltyk; 919-825-2310; Chris.Koltyk@ncdps.gov

9. NC Search and Rescue Program

SL 2018-5, Subsection 5.6(b)(2)d

With these funds, the North Carolina Search and Rescue Program sustained the North Carolina Search and Rescue teams, trained specialized personnel, maintained specialized equipment, and exercised and maintained capabilities necessary to respond to the needs of North Carolinians.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 2,300,000
Expended	\$ 2,291,474
Obligated	\$ 0
Unobligated Balance	\$ 8,526

Summary of Activities

Since April 2019, 26 State Deployable Water Rescue teams have been issued inflatable rescue boats, motors and dry suits. We were able to outfit seven regional search and rescue task forces with wireless communications equipment, eight advanced night vision equipment, and two all-terrain forklifts with trailers. NCEM completed the Structures Specialist purchase outfitting all 15 disaster engineers with up to date personal protective equipment and the

necessary personal equipment to prepare them for local and state response. In addition, two caches of engineering tools were created to support responders during a structure collapse. The funding period closed June 30, 2019, and no additional activity is anticipated on this funding.

Performance Metrics

- a. Average Time for Project Delivery by Program - This program was launched prior to December 1, 2019, prior to the reporting requirement.
- b. Amount and % Spent/Obligated on Administrative Activities by Program - This program was launched prior to December 1, 2019, prior to the reporting requirement.
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program - This program was launched prior to December 1, 2019, prior to the reporting requirement.

Recent Activities for Current Reporting Period (October - December 2021)

Funds were fully expended prior to the reporting period.

Contact

Matt Kemnitz, Assistant Director of Administration, NCEM (919) 817-2511

10. NC Office of Recovery and Resiliency

SL 2018-136, Subsection 6.1(27)

Allocations for this program total \$2,000,000, of which \$1,021,844 has been expended and \$1,158,720 is obligated to cover the salary and operational costs for non-grant supported activities. NCORR performs certain limited activities that are not covered by federal grants, such as resilience work and state funding reporting requirements. The Resiliency Program works to build a stronger North Carolina, where communities, economies and ecosystems rebound, adapt and thrive amid changing conditions and challenges, including disasters and climate change.

Responsible Department and Agency

Department of Public Safety, NC Office of Recovery and Resiliency

Funding Allocation Update

Appropriated	\$ 2,000,000
Expended	\$ 1,021,844
Obligated	\$ 978,156

Unobligated Balance \$ 0.00

Summary of Activities

State-funded activities covered by these appropriations include the NCORR Resilience Team, program delivery of the Distressed Local Government Grant and Loan Program, state reporting activities, and assisting NCEM and other agencies with recovery coordination.

Performance Metrics

- a. Average Time for Project Delivery by Program – Not applicable, as this appropriation is not project based.
- b. Amount and % Spent/Obligated on Administrative Activities by Program. \$1,021,844 expended
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program. \$978,156 obligated to program delivery costs for NCORR

Recent Activities for Current Reporting Period (October - December 2021)

Cover the costs of staff engaged in supporting long-range resilience planning, the Resilient Communities Program and the coordination and staffing for the State Disaster Recovery Taskforce. Also, this funding covers the staff costs for tracking and monitoring the Distressed Local Government Grants and Loans program and required state reporting and coordination with other state agencies.

Contact

Jim Klingler, Finance Chief, NCORR (984) 833-5397

11. State Match and Other Support for Disaster Recovery

SL 2018-134, Subsection 4.1(2)

This program provides for the non-federal cost-share required for participation in federal Stafford Act Programs. Through June 30, 2019, the entire \$50,000,000 has been expended.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 50,000,000
Expended	\$ 50,000,000
Obligated	\$ 0
Unobligated Balance	\$ 0

Performance Metrics

- a. Average Time for Project Delivery by Program - This program was launched prior to December 1, 2019, prior to the reporting requirement.
- b. Amount and % Spent/Obligated on Administrative Activities by Program - This program was launched prior to December 1, 2019, prior to the reporting requirement.
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program - This program was launched prior to December 1, 2019, prior to the reporting requirement.

Recent Activities for Current Reporting Period (October - December 2021)

Funds were fully expended prior to the reporting period.

Contact

Matt Kemnitz, Assistant Director of Administration, NCEM (919) 817-2511

12. State Match for Federal Assistance Programs

SL 2018-136, Subsection 6.1(3)

This program provides for the non-federal cost-share required for participation in federal Stafford Act Programs. A total of \$40,000,000 for Florence matching funds was appropriated. Through December 31, all \$40,000,000 has been expended.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 40,000,000
Expended	\$ 40,000,000
Obligated	\$ 0
Unobligated Balance	\$ 0

Performance Metrics

- a. Average Time for Project Delivery by Program- This program was launched prior to December 1, 2019, prior to the reporting requirement.
- b. Amount and % Spent/Obligated on Administrative Activities by Program- This program was launched prior to December 1, 2019, prior to the reporting requirement.
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program- This program was launched prior to December 1, 2019, prior to the reporting requirement.

Recent Activities for Current Reporting Period (October - December 2021)

Funds were fully expended prior to the reporting period.

Contact

Matt Kemnitz, Assistant Director of Administration, NCEM (919) 817-2511

13.State Match for Federal Assistance Programs

SL 2020-97, Subsection 6.1(3)

This program provides for the non-federal cost-share required for participation in federal Stafford Act Programs. A total of \$40,000,000 for Florence matching funds was appropriated. Through December 31, all \$40,000,000 has been expended.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 40,000,000
Expended	\$ 40,000,000
Obligated	\$ 0
Unobligated Balance	\$ 0

Performance Metrics

- d. Average Time for Project Delivery by Program- This program was launched prior to December 1, 2019, prior to the reporting requirement.
- e. Amount and % Spent/Obligated on Administrative Activities by Program- This program was launched prior to December 1, 2019, prior to the reporting requirement.
- f. Amount and % Spent/Obligated on Behalf of Recipients by Program- This program was launched prior to December 1, 2019, prior to the reporting requirement.

Recent Activities for Current Reporting Period (October - December 2021)

Funds were fully expended prior to the reporting period.

Contact

Matt Kemnitz, Assistant Director of Administration, NCEM (919) 817-2511

14. NCORR Buyouts and SARF

SL 2019-224, Subsection 2.1(4)

This appropriation provides supplemental funding to support two programs, the Buyout Program in the NC Office of Recovery and Resiliency (NCORR) and the Hazard Mitigation Grant Program (HMGP) in the Division of Emergency Management (NCEM). NCORR will use its portion to expand the buyouts to homeowners who would not otherwise qualify for the Community Development Block Grant – Disaster Recovery (CDBG-DR) program. NCORR initiated a phased intake for the CDBG-DR supported Buyout Program and will soon program these funds to augment the CDBG-DR program. NCEM's portion will be used to provide gap assistance to homeowners who accepted an accelerated-buyout for Hurricane Florence through HMGP and the State Acquisition and Relocation Fund (SARF).

Responsible Department and Agency

Department of Public Safety, NC Office of Recovery and Resiliency and Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 13,000,000
Expended	\$
Obligated	\$
Unobligated Balance	\$ 13,000,000

Performance Metrics

NCORR State-funded Buyouts

- a. Average Time for Project Delivery by Program – NCORR recently launched the CDBG-DR Buyout Program on January 26, 2020. NCORR will program the state funds as the federally-funded program is at full production.
- b. Amount and % spent/obligated on administrative activities by Program. Nothing to report.
- c. Amount and % spent/obligated on behalf of recipients by Program. Nothing to report.

NCEM Florence-Accelerated SARF

- a. Average Time for Project Delivery by Program – 388 days. The agency has implemented an accelerated SARF program for Hurricane Florence Expedited Acquisitions.
- b. Amount and % Spent/Obligated on Administrative Activities by Program – N/A

- c. Amount and % Spent/Obligated on Behalf of Recipients by Program – 00%/\$0.00

Recent Activities for Current Reporting Period (October - December 2021)

The NCORR program is still in the early stages of opening Disaster Risk Reduction Areas and inviting homeowners to apply. As applications are received for households that are otherwise ineligible for CDBG-DR or CDBG-MIT assistance, NCORR can use these funds to assist with a property buyout.

Contact

Jim Klingler Finance Chief, NCORR (984) 833-5397
Steve McGugan, Assistant Director for Hazard Mitigation, NCEM,
steve.mcgugan@ncdps.gov

15. NCORR Loans and Grants

SL 2019-224, Subsection 2.1(4)

This program expands the NC Office of Recovery and Resiliency's (NCORR) Distressed Local Government Grant and Loan Programs. Grants assist local governments in Hurricane Florence declared communities with funding general governmental operations and building recovery capacity. Loans assist local governments with cash-flow expenses that are reimbursable by the federal government. Loans are repaid by the federal reimbursement.

Responsible Department and Agency

Department of Public Safety, NC Office of Recovery and Resiliency

Funding Allocation Update

Appropriated	\$ 9,000,000
Expended	\$ 7,567,797
Obligated	\$
Unobligated Balance	\$ 1,432,203

Performance Metrics

- a. Average Time for Project Delivery by Program
- Average number of days from application to fund distribution **30-45 days**
 - Average number of days from fund distribution to project commencement -
Not applicable. Grants and Loans are awarded for a broad range purposes with varying expenditure schedules.

- o Average number of days from project commencement to project completion - Not applicable. Grants and Loans are awarded for a broad range purposes with varying expenditure schedules.
- b. Amount and % Spent/Obligated on Administrative Activities by Program. - \$0 and 0% of this appropriation. Staff costs are covered by appropriations to NCORR for administrative functions
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program. \$7,567,797 had been expended (84%) / \$1,432,203 (16%) is currently unobligated

Recent Activities for Current Reporting Period (October - December 2021)

NCORR approved and paid 20 applicants through March of 2021 for various needs for Hurricane Disaster recovery assistance for Hurricane Florence. No activity for this quarter.

Contact Mary Massey, Budget Director, NCORR

16. NCEM-VOAD Disaster Recovery

SL 2019-224, Subsection 2.1(7)

The NC VOAD Disaster Recovery Grant program provides financial assistance to volunteer non-profit organizations that provide shelters, housing repairs, and other emergency and disaster recovery services to disaster survivors adversely affected by Hurricane Florence. The program is open to 501(c)(3) nonprofit organizations which provide direct services to disaster survivors in North Carolina. The program has a maximum grant award of \$300,000, requires no matching funds, and may be provided in either a reimbursement or installment basis.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update (2D26-F224)

Appropriated	\$ 1,000,000
Expended	\$ 1,000,000
Obligated	\$ 0
Unobligated Balance	\$ 0

Summary of Activities Summary of Activities

- a. Thirty applications received requesting NC VOAD funding, seven nonprofit Volunteer Organizations Assisting in Disasters awarded funds totaling \$1,000,000.

- b. Budget modifications and scope of work adjustments submitted and reviewed for each applicant.

Performance Metrics

- a. Average Time for Project Delivery by Program - Nothing to report at this time
- b. Amount and % Spent/Obligated on Administrative Activities by Program – \$0 and 0% of this appropriation. Staff costs are covered by receipts and appropriations for current operations.
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program - \$1,000,000 expended (100%).

Recent Activities for Current Reporting Period (October - December 2021)

Due to COVID-19 impacts, recipients' activities have slowed with requests to begin program implementation second and third quarters 2020. Multiple organizations were realigning their project scopes, deliverables and timelines with the change in volunteer availability and increased utilization of contractors.

Contact Matt Kemnitz, Assistant Director of Administration, NCEM (919) 817-2511

17. Purchase and install river gauges to improve flood mapping and real-time flooding information

SL 2019-224 House Bill 200; Subsection II.2.1(7)c

\$2 million allocated to Department of Public Safety, Division of Emergency Management, Purchase and install river gauges to improve flood mapping and real-time flooding information, established in Section 2.1 of SL 2019-224 Senate Bill 429. This project will (1) install river gauges and develop flood inundation libraries and risk assessments for 71 sites for incorporation into the Flood Inundation Mapping and Alert Network (FIMAN) and (2) purchase water level, rainfall gauge and radio equipment to modernize and update equipment at 34 water level, 43 rainfall and 2 radio existing gauge system locations.

Responsible Department and Agency

North Carolina Department of Public Safety, Division of Emergency Management

Funding Allocation Update

	Total	SL here
Appropriated	\$2,000,000	
Expended	\$858,712	
Obligated	\$1,141,288	
Unobligated Balance	\$0	

Summary of Activities

1. Task 1 - Purchase and install river gauges and develop flood inundation libraries and risk assessments for 71 sites for incorporation into FIMAN
 - a. All sites visited by NCEM and approved by local contacts
 - b. NCGS site surveys complete
 - c. Data loggers, GOES Satellite Transmitters, Radar sensor and cables, Batteries, solar charge controllers, antennas, cell modems, solar panels, GPS antennas, GOES Antennas and cables and locks received by NCEM
 - d. Fathom coastal and riverine risk data – data received
 - e. FIMAN library and gauge survey – 49 libraries approved. 0 libraries in QA/QC
 - f. Delivery order for gauge mount design drawing to streamline NCDOT encroachment agreements – Task Complete
 - g. Draft IFB – approved in DocuSign – IFB closed on 8/31/2021. Bid accepted and awarded to contractor. 2 gauges installed. Gauges scheduled to be installed by 5/30/2022. Schedule delayed due to delays in receiving gauge mount parts due to COVID-19 supply chain issues.
2. Task 2 - Purchase water level, rainfall gauge and radio equipment to modernize and update equipment at 34 water level, 43 rainfall and 2 radio existing gauge system locations
 - a. Radar sensor and cables, Batteries, AL200 data loggers, Solar Panels, LoggerNet Datalogger Support Software, Maxon Radios and Pressure transducer calibrator – Received
 - b. TimeWave radio repeater – Grandmother mountain equipment installed
 - c. TimeWave radios/cell modem for Joanna Bald and Cowee – Equipment installation complete
 - d. Need to order pressure transducer replacements and cables.
 - e. Sutron –Purchased new computer.
 - f. Finalizing IFB to perform equipment upgrades at NCEM gauge sites.

Performance Metrics

1. Task 1
 - a. NCEM Gauge Site Visits Completed 71 of 71 – 3/2020
 - b. NCGS Site Surveys Completed 71 of 71 – 8/25/2020
 - c. Radar gauge equipment purchases – 71 of 71
 - d. Radar gauge equipment received – 71 of 71
 - e. Gauge Bridge Mount Design Contracted – 16 of 16 – Contracted 9/30/2020
 - f. Gauge Bridge Mount Design Received – 16 of 16 – 5/19/2021
 - g. Draft IFB Routed to DPS Purchasing for Review – 6/12/2020
 - h. Draft IFB Issued – 71 of 71 – Closed and awarded 8/31/2021
 - i. Radar Gauges Installed – 2 of 71 - 1/31/2022
 - j. ESP FIMAN Library and Gauge Survey RFDO signed in eProcurement – 7/14/2020
 - k. FIMAN Gauge Survey – 0 of 71
 - l. FIMAN Libraries – 68 of 71
 - m. FIMAN Risk Database – 0 of 71
 - n. FIMAN Risk Database Loaded into FIMAN – 0 of 71
2. Task 2

- a. Water Level and Radio Upgrade Equipment entered in eProcurement – 23 of 29
- b. Rainfall Gauge Equipment entered in eProcurement – 86 of 102
- c. Water Level and Radio Upgrade Equipment ordered – 22 of 29
- d. Rainfall Gauge Equipment purchases ordered – 86 of 102
- e. Water Level and Radio Upgrade purchases received – 22 of 29
- f. Rainfall Gauge Equipment received – 86 of 102
- g. Water Level and Radio Upgrade Equipment installed – 5 of 29
- h. Rainfall Gauge Equipment installed – 0 of 102

Recent Activities for Current Reporting Period (October – December 2021)

- 1. Task 1
 - a. Contractor provided additional 19 of 71 FIMAN libraries to NCEM
 - b. IFB posted and awarded to contractor for installation of 71 radar gauges. Draft installation completion date is 5/30/2021. Installation scheduled delayed due to supply chain issues for gauge mount parts.
- 2. Task 2
 - a. Finalizing IFB to perform equipment upgrades at NCEM gauge sites.
 - b. Purchased new Sutron computer.

Contact

Chris Koltyk; 919-825-2310; Chris.Koltyk@ncdps.gov

18. NC Search and Rescue Program

SL 2019-224, Subsection 2.1(7)

North Carolina Search and Rescue Program sustains the North Carolina Search and Rescue teams, trains specialized personnel, maintains specialized equipment, and exercises and maintains capabilities necessary to respond to the needs of North Carolinians.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 1,000,000
Expended	\$ 995,183
Obligated	\$ 4,680
Unobligated Balance	\$ 137

Performance Metrics

- a. Average Time for Project Delivery by Program - Nothing to report at this time.
- b. Amount and % Spent/Obligated on Administrative Activities by Program - Nothing to report at this time.
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program - Nothing to report at this time.

Recent Activities for Current Reporting Period (October - December 2021)

There is no new activity to report in this period. The remaining obligated funds are for registration and titling fees, which are in the process of invoicing/billing.

Contact Matt Kemnitz, Assistant Director of Administration, NCEM (919) 817-2511

19. NCEM Flood Insurance Pilot

SL 2019-224, Subsection 2.1(7)

\$2M allocated to the Department of Public Safety Division of Emergency Management to develop a pilot program to help pay the cost of flood insurance for eligible applicants. Eligible applicants shall not have earned more than eighty percent (80%) of the subject area median income and the applicant's property must be their primary residence and be insurable. Priority shall be given to properties in the most impacted and distressed counties from Hurricane Matthew and/or Hurricane Florence. Assistance can be provided for up to two (2) years.

Responsible Department and Agency

North Carolina Department of Public Safety Division of Emergency Management, Risk Management Section

Funding Allocation Update: Flood Insurance Pilot Program

	Total SL 2019-224; § 2.1(7)
Appropriated	\$2,000,000.00
Expended	\$0.00
Obligated	\$0.00
Unobligated Balance	\$2,000,000.00

Summary of Activities

1. N.C. Office of Recovery and Resiliency (NCORR) agreed to administer the program through ReBuild NC;
2. Developed an implementation outline in conjunction with existing ReBuild NC policies and procedures;
3. Applicants have submitted required information to NCORR via the ReBuild NC Homeowner Recovery Program application;
4. NCORR has identified the program recipient targets from the eligible pool of applicants to the CDBG-DR Homeowner Recovery Program;
5. NCORR has developed the required notification forms and talking points for program implementation;
6. NCORR has developed informational forms on flood insurance according to the FEMA request to provide informational brochures to program participants;
7. NCORR is working on marketing and outreach to eligible applicants towards insuring eligible applicants;
8. NCORR continues to refine program policies, procedures, and system of record business requirements; and
9. NCORR has held multiple discussions with FEMA and NFIP representatives to ensure all requirements are considered prior to implementation.

Performance Metrics

- Average Time for Program Delivery
 - Average number of days from application to fund distribution
 - Average number of days from fund distribution to program delivery
- Number of households included in the program
- Amount and % spent/obligated

Recent Activities for Current Reporting Period (October - December 2021)

In the final quarter of 2021, NCORR preliminarily identified the positions that will be necessary to implement the flood insurance assistance process. The positions and number of personnel in each position, are currently under review by the NCORR Executive Director. Additionally, the program design team outlined the policy and process considerations that need to be made prior to the development of Salesforce business requirements. Salesforce will be the platform utilized for the following activities: (1) identification of eligible applicants, (2) compilation of communication with eligible applicants, (3) retention of documents sent to and received from eligible applicants, (4) calculation of assistance for eligible applicants, and (5) transition from the implementation teams to the NCORR finance team when funds are ready to be disbursed to eligible applicants and/or directly to FEMA. Furthermore, multiple options of how this process may be reflected in Salesforce have been outlined. The final Salesforce design is contingent upon the decisions on the recent policy and process considerations presented which will be made in Q1 2022.

Contact

Paul Ervin; 919-825-2279; paul.ervin@ncdps.gov

20. State Match and Other Support for Disaster Recovery

SL 2019-250, Subsection 1.1(1)

Provides for the non-federal cost-share required for participation in federal Stafford Act Programs. This allocation is specifically for state match for Hurricane Florence.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update (2D01)

Appropriated	\$ 70,812,336
Expended	\$ 70,812,336
Obligated	\$ 0
Unobligated Balance	\$ 0.00

Performance Metrics

- a. Average Time for Project Delivery by Program – This appropriation is a reserve for federal cost-share and does not directly fund recovery projects.
- b. Amount and % Spent/Obligated on Administrative Activities by Program – This appropriation is a reserve for federal cost-share and does not directly fund recovery projects.
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program – This appropriation is a reserve for federal cost-share and does not directly fund recovery projects.

Contact

Matt Kemnitz, Assistant Director of Administration, NCEM (919) 817-2511

21. Expand Flood Mitigation Studies

SL 2019-250 House Bill 200; Subsection 1.1.2(2)a

\$5 million allocated to Department of Public Safety, Division of Emergency Management, expand flood mitigation studies, established in Section 1.2 of SL 2019-250 House Bill 200. This project will (1) develop and perform new flood mitigation studies for the Northeast Cape Fear River (including Burgaw Creek), Cape Fear, and Little River (into Cape Fear River),

and the Cashie River Basins and (2) will develop new flood studies, building level risk assessments and building mitigation strategies for approximately 12,000 square miles of unstudied streams in the counties that were most significantly impacted by riverine flooding from Hurricane Matthew and Florence.

Responsible Department and Agency

North Carolina Department of Public Safety, Division of Emergency Management

Funding Allocation Update

	Total	SL here
Appropriated	\$5,000,000	
Expended	\$2,883,974	
Obligated	\$2,116,026	
Unobligated Balance	\$0	

Summary of Activities

3. Task 1 - Flood Mitigation Studies Northeast Cape Fear River (including Burgaw Creek), Cape Fear, and Little River (into Cape Fear River), and the Cashie River Basins
 - a. Mitigation alternatives analysis for Little River and NE Cape Fear are in QC review. Mitigation alternatives analysis for Cape Fear mainstem is under development. Community meeting preparation for Cape Fear River is underway for 2nd meeting to be held in late January.
 - b. Cashie River modeling and mitigation alternative analysis are complete and draft report is being developed. Community meeting preparation underway for meeting to be held in January.
4. Task 2 - New Flood Studies on Unstudied Stream, Building Level Flood Risk Assessments and Mitigation Strategies and Application for 12,000 square miles (80 HUC10 Basins)
 - a. H&H Analysis for 80 of 80 basins has been completed.
 - b. Mapping products for 80 of 80 basins have been completed.
 - c. Risk data for 80 of 80 basins has been completed.
 - d. Building level mitigation for 80 of 80 basins has been completed. Contractors working on HUC-10 reports for all basins.
 - e. Contractor working on Flood Mitigation Data Viewer and website with anticipated completion at end of January.

Performance Metrics

3. Task 1 - Flood Mitigation Studies Northeast Cape Fear River (including Burgaw Creek), Cape Fear, and Little River (into Cape Fear River), and the Cashie River Basins (4 Basins)
 - a. Contracts Signed – 5/19/2020 COMPLETE
 - b. Northeast Cape Fear River Field Survey – 33 of 33 cross-sections – 8/7/20 COMPLETE
 - c. Magnitude and Causes of Flooding – 4 of 4 watersheds – 5/28/2021 COMPLETE
 - d. Community Meeting 1 – Scheduled for 7/21/2021 COMPLETE
 - e. Baseline Analyses – 4 of 4 watersheds – 6/11/2021 COMPLETE

- f. Development of Mitigation Strategies 3 of 4 watersheds – 1/15/2022
 - g. Cashie Community Meeting 1 – 1/30/2022
 - h. Cape Fear Community Meeting 2 – 1/30/2022
 - i. Final Reports – 2/28/2022
 - j. Load Data into Viewer - 2/2022
4. Task 2 - New Flood Studies on Unstudied Streams, Building Level Flood Risk Assessments and Mitigation Strategies and Application for 12,723 square miles (80 HUC10 Basins)
- a. Contracts Signed – 5/19/2020 COMPLETE
 - b. Flood Risk and Mitigation Data Viewer – 1/20/2022
 - c. Updated Building Footprints – 80 of 80 watersheds – 8/25/2021 COMPLETE
 - d. 2-D Hydrologic and Hydraulic Analyses – 80 of 80 watersheds – 6/30/2021 COMPLETE
 - e. Flood Rasters and CNMS - 80 of 80 watersheds - 7/26/2021 COMPLETE (pending CNMS delivery)
 - f. Flood Risk Assessment Databases – 80 of 80 watersheds – 7/28/2021 COMPLETE
 - g. Flood Mitigation Databases - 80 of 80 watersheds – 9/1/2021 COMPLETE (pending database upload)
 - h. Flood Risk and Mitigation Databases Loaded to Viewer - 0 of 80 watersheds – 1/30/2022

Recent Activities for Current Reporting Period (October – December 2021)

- 1. Task 1
 - a. Northeast Cape Fear River 2D mitigation alternative analysis was completed and is in 2nd QC review. Little River 2D mitigation alternative analysis was completed and is in 1st QC review. Continued development of Cape Fear mainstem alternatives analysis. Preparation for 2nd community meeting continued.
 - b. Cashie River BCA and draft report were completed and internal contractor review was started. Continued preparation for community meeting to be held in January.
- 2. Task 2
 - a. Mapping products were completed for another 5 of 80 basins. All mapping now complete.
 - b. Building footprint updates were completed for another 5 of 80 basins. All building footprint updates are now complete.
 - c. Risk data development was completed for another 8 of 80 basins. All risk data is now complete.
 - d. Building level mitigation runs were completed for 80 of 80 basins. All runs are now complete and contractors started work on reports for all HUC-10 basins.
 - e. Continued work on developing Data Viewer and Website.

Contact

Chris Koltyk; 919-825-2310; Chris.Koltyk@ncdps.gov

Water Level and Breach Monitoring Systems for 1,510 High and Intermediate Risk Dams

SL 2019-250 House Bill 200; Subsection I.1.2(2)b

\$4.8 million allocated to Department of Public Safety, Division of Emergency Management, Water Level and Breach Monitoring Systems for 1,510 High and Intermediate Risk Dams, established in Section 1.2 of SL 2019-250 House Bill 200. This project will (1) complete dam breach analysis for the remaining 859 intermediate and high hazard dams in NC that currently do not have dam failure inundation boundaries or building and road risk information, (2) develop rainfall runoff hydrologic modeling to determine critical rainfall amounts to potentially overtop a dam for 287 dams, (3) install gauges to monitor potential dam failures for 130 critical state and locally owned dams and (4) integrate dam breach analyses, overtopping modeling and dam gauge data into a secure dam monitoring, alert and warning system.

Responsible Department and Agency

North Carolina Department of Public Safety, Division of Emergency Management

Funding Allocation Update

	Total	SL here
Appropriated	\$4,800,000	
Expended	\$2,982,562	
Obligated	\$1,817,438	
Unobligated Balance	\$0.00	

Summary of Activities

5. Task 1 - Dam Breach Inundation Modeling for 859 Dams
 - a. Contracts in place with engineering firms for dam breach analyses
 - b. Project management SharePoint and AGOL sites complete
 - c. Dam breach analyses completed for 859 dams (to include 12 dams completed for Risk)
 - d. Dam risk databases completed for 859 dams
 - e. Reviewing and testing the 859 dam databases for the SERA dam application.
6. Task 2 - Simplified HEC-HMS Rainfall-Runoff and Reservoir Routing Modeling for 287 Dams
 - a. Contracts in place with engineering firms for dam overtopping engineering analyses and dam surveys
 - b. Letters sent to dam owners for site access for Survey for overtopping analyses.
 - c. Dam "as-builts" received from NCDEQ
 - d. Field survey complete for all 119 dams being surveyed. NCEM completed field survey for 3 additional structures
 - e. Rainfall-runoff modeling complete for all 287 dams
 - f. Task 2 is 100% complete

7. Task 3 - Installation of New Gauges at 130 Dams
 - a. Pressure transducer gauge equipment ordered in E-Procurement
 - b. IFB reissued for ultrasonic gauge equipment and installation
 - c. NCEM site visits complete to sites where water level gauges will be installed
 - d. IFB contract awarded for installation of 45 pressure transducer gauges. Developing IFB for remaining sites.
8. Task 4 - Development of Dam Warning System and Incorporation of Breach Analysis, Overtopping Analyses and Dam Gauge Data
 - a. Gauge warning system software purchase ordered in E-Procurement
 - b. Initial deployment of DamWatch is complete.
 - c. Data for all rainfall runoff models have been loaded into dam warning application
 - d. 19 gauges loaded into alert application
 - e. Additional year of service ordered in E-Procurement

Performance Metrics

5. Task 1 - Dam Breach Inundation Modeling for 859 Dams
 - a. Contracts signed – 5/19/2020
 - b. Site survey letters provided to dam owners – 6/18/2020
 - c. Dam breach analyses complete (90%) – 859 of 859 – 09/30/21
 - d. Dam risk databases complete – 859 of 859 – 12/31/2021
 - e. Dam risk databases loaded to SERA – 0 of 859 – 2/25/2022
6. Task 2 - Simplified HEC-HMS Rainfall-Runoff and Reservoir Routing Modeling for 287 Dams
 - a. Contracts Signed – 5/19/2020
 - b. EM Letters Sent for Site Surveys – 6/18/2020
 - c. Dam Surveys Complete – 119 of 119 – 10/1/2020
 - d. Rainfall Runoff Modeling 100% Complete – 287 of 287 – 12/31/2020
7. Task 3 - Installation of New Gauges at 130 Dams
 - a. EM Site Visits – 130 of 130
 - b. Pressure Transducer Gauge Equipment Purchases - ordered in eProcurement – 12/7/2020
 - c. Ultrasonic Gauge Equipment/Installation - entered in eProcurement – 5/7/2020 – IFB quote being revised by vender
 - d. Ultrasonic Gauge Equipment Installed – 0 of 34
 - e. Pressure Transducer Gauge Installation – IFB with DPS purchasing
 - f. Onset Gauge Installation – 45 of 96 - IFB – Contract awarded 10/12/2021
 - g. Onset Gauges Installed – 11 of 96
 - h. Gauge Surveys Completed – 0 of 130
8. Task 4 - Development of Dam Warning System and Incorporation of Breach Analysis, Overtopping Analyses and Dam Gauge Data
 - a. Dam Warning Application - Ordered in eProcurement – 9/30/2020
 - b. Dam Warning Application Initial Setup - Complete
 - c. Dam Warning Application Rainfall Runoff Models Loaded – 555 of 555
 - d. Dam Warning Application Dam Gauges Loaded – 19 of 130

Recent Activities for Current Reporting Period (October – December 2021)

- a. Task 1

- a. Dam breach analyses completed for 859 dams (100%)
 - b. Reviewing all 859 dam databases for the SERA application for dams
- b. Task 2
 - a. Task complete
- c. Task 3
 - a. IFB for pressure transducer gauges issued for 45 dam gauge sites
- d. Task 4
 - a. Data for all 555 rainfall runoff models have been loaded into dam warning application
 - b. 19 dam gauges loaded into alert application

Contact

Chris Koltyk; 919-825-2310; Chris.Koltyk@ncdps.gov

22. Local Government Assistance Loans

SL 2019-250, Subsection 1.2(3)a

The NCORR Temporary Cash-Flow Assistance Loan Program to Local Governments provides cash-flow loans to distressed local governments in declared counties for Hurricanes Matthew, Florence, Dorian, and Tropical Storm Michael. These loans may only cover federally reimbursable expenses, and the loans are repaid by the federal reimbursement.

Responsible Department and Agency

Department of Public Safety, NC Office of Recovery and Resiliency

Funding Allocation Update

Appropriated	\$ 10,000,000
Expended	\$ 6,509,795
Obligated	\$ 2,624,933
Unobligated Balance	\$ 865,272

Performance Metrics

- a. Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution **30-45 days.**
 - Loans are based on actual expenditures or estimates of pending expenses
 - Average number of days from fund distribution to project commencement - Not applicable. Grants and Loans are awarded for a broad range of purposes with varying expenditure schedules.
 - Average number of days from project commencement to project completion - Not applicable. Grants and Loans are awarded for a broad range of purposes with varying expenditure schedules.

- b. Amount and % Spent/Obligated on Administrative Activities by Program - \$0 and 0% of this appropriation. Staff costs are covered by appropriations to NCORR for administrative functions
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program \$6,509,795 had been expended (65%) / \$2,624,933 had been obligated (26%)

Recent Activities for Current Reporting Period (October -December 2021)

NCORR is continuing to work with their loan applicants to ensure the funds for their FEMA projects are being disbursed timely. No activity for the quarter.

Contact Mary Massey, Budget Director, NCORR

23. NCORR – Grants to Local Governments

SL 2019-250, Subsection 1.2(3)(b)

This program expands the NC Office of Recovery and Resiliency's (NCORR) Distressed Local Government Grant Program. Grants assist local governments in Hurricane Dorian declared communities with funding general governmental operations, building recovery capacity, and performing recovery activities.

Responsible Department and Agency

Department of Public Safety, NC Office of Recovery and Resiliency

Funding Allocation Update

Appropriated	\$ 5,000,000
Expended	\$ 4,771,650
Obligated	\$
Unobligated Balance	\$ 228,350

Performance Metrics

- a. Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution **30-45 days**
 - Average number of days from fund distribution to project commencement - Not applicable. Grants and Loans are awarded for a broad range of purposes with varying expenditure schedules.)

- o Average number of days from project commencement to project completion- Not applicable. Grants and Loans are awarded for a broad range of purposes with varying expenditure schedules
- b. Amount and % Spent/Obligated on Administrative Activities by Program - \$0 and 0% of this appropriation. Staff costs are covered by appropriations to NCORR for administrative functions
- c. Amount and % Spent/Obligated on Behalf of Recipients by Program \$4,771,650 had been expended (95%)

Recent Activities for Current Reporting Period (October – December 2021)

No Activity for the Quarter.

Contact

Mary Massey, Budget Director, NCORR

24.State Match for Federal Assistance Programs

SL 2020-97, Subsection 2.6.(a)

This program provides for the non-federal cost-share required for participation in federal Stafford Act Programs. A total of \$27,796,610 for Florence matching funds was appropriated.

Responsible Department and Agency

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$ 27,796,610
Expended	\$ 300,000
Obligated	\$
Unobligated Balance	\$ 27,496,610

Performance Metrics

- g. Average Time for Project Delivery by Program- This program was launched with the 2020 approved legislation.
- h. Amount and % Spent/Obligated on Administrative Activities by Program- This program was with the 2020 approved legislation

- i. Amount and % Spent/Obligated on Behalf of Recipients by Program- This program was launched with the 2020 approved legislation.

Recent Activities for Current Reporting Period (October - December 2021) No activity for the quarter.

Contact

Matt Kemnitz, Assistant Director of Administration, NCEM (919) 817-2511

Department of Agriculture and Consumer Services

1. The NCFS Wildfire Response

SL 2016-124; Subsection 4.1 (10)(a)

Allocates \$23M of the \$25.5M to the North Carolina Forest Service from “The Disaster Recovery Act of 2016” for wildfire response. Wildfires in the western part of the State burned tens of thousands of acres and destroyed hundreds of structures. Starting just weeks after Hurricane Matthew on October 23, 2016, and continuing throughout November, 26 major and dozens of smaller fires impacted air quality across the State. More than 62,000 total acres burned in NC including more than 25,000 acres on land protected by the State. More than 2,400 emergency responders responded to the wildfires and related events. Firefighters from 40 states joined NC to assist in firefighting efforts.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; NC Forest Service

Funding Allocation Update

Appropriated	\$11,400,000.00
Expended	\$11,299,731.10
Obligated	\$0.00
Unobligated Balance	\$100,268.90

Summary of Activities

- a. 26 Major Fires
- b. More than 62,000 total acres burned
- c. Over 2,400 emergency personnel responded
- d. Value of homes protected exceeded \$383 million

Performance Metrics

- Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution
 - 90 days from receipt of cost documentation
 - Average number of days from fund distribution to project commencement
 - Not applicable
 - Average number of days from project commencement to project completion
 - Not applicable
- Amount and % spent/obligated on administrative activities by Program.
 - \$0.00, 0%
- Amount and % spent/obligated on behalf of recipients by Program.

- \$20,404,581.32, 100%

Recent Activities for Current Reporting Period (October - December 2021)

No activities to report. Project is complete.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

2. Timber Restoration

SL 2016-124; Subsection (10) (a)

Allocates \$1M of the \$25.5M to the North Carolina Forest Service for disaster-related timber restoration.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; NC Forest Service

Funding Allocation Update

Appropriated	\$1,000,000
Expended	\$711,928.19
Obligated	\$0.00
Unobligated Balance	\$288,071.81

Summary of Activities

- 330 timber restoration projects, with 479 practices, on 18,121 acres.

Recent Activities for Current Reporting Period (October – December 2021)

Projects completed in January 2020. No recent activities for current reporting period. All unallocated funds may be de-obligated.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

3. Claridge Nursery Operations and Non-Capital Repairs

Allocates \$1.5M of the \$25.5M to the North Carolina Forest Service for repairs and operational expenses at Claridge Nursery in Wayne County.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; NC Forest Service

Funding Allocation Update

Appropriated	\$1,500,000.00
Expended	\$203,324.60
Obligated	\$1,296,675.40
Unobligated Balance	\$0.00

Summary of Activities

- a. FEMA Grant request received in the amount of \$256,533 and has been credited to Funding Allocation Update Expended amount shown above.
- b. Nursery has been able to use cash reserves to cover majority of operating expenses
- c. Designer hired to develop repair and renovation plan for damaged buildings
- d. Bids have been requested for repair work
- e. Bids received and accepted
- f. Repair and renovation work completed on 6 buildings.
- g. Repair made to damaged seedling refrigeration units.
- h. Building demolition.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by Program
 - a. Average number of days from application to fund distribution
 - i. Not applicable
 - b. Average number of days from fund distribution to project commencement
 - i. Solicitation of design for repairs began immediately following fund availability
 - ii. Completed plans finalized in Spring 2018
 - iii. NCDA&CS takes over as “own general contractor” in June 2019 due to lack of interest in projects.
 - iv. Current Administrative Building Bid was responded to within 5 working days of receipt.
 - c. Average number of days from project commencement to project completion
 - i. Projects are ongoing. Average time to completion is approximately 36 months.
- b. Amount and % spent/obligated on administrative activities by Program.
 - a. \$0 and 0% is obligated to administrative items
- c. Amount and % spent/obligated on behalf of recipients by Program.
 - a. \$459,857.60/100%

Recent Activities for Current Reporting Period (October - December 2021)

No activities to report.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

4. AgWRAP Farm Pond and Dam Repair with PEs

SL 2016-124; Subsection 4.1 (10)(b)

Allocates \$1.7M of the \$12.2M to the Division of Soil and Water Conservation for supplemental funding of the Agricultural Water Resources Assistance Program (AgWRAP) to support disaster-related farm pond and dam repairs.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; Division of Soil & Water Conservation

Funding Allocation Update

Appropriated	\$1,700,000.00
Expended	\$1,426,148.23
Obligated	\$273,851.77
Unobligated Balance	\$0.00

Summary of Activities

- The 2016 funds allocated for AgWRAP Farm Pond and Dam Repair are being used primarily to cover the turnkey engineering evaluations, designs, bidding, and construction oversight aspects of pond repair projects. Construction cost share contracts with individual producers are being funded primarily out of the 2017 funds. Construction funds are not obligated until the final design is completed and approved by the landowner. This is the very last step in a complex process that also requires the farmer to send a check for their contribution to the Division.
- The table below reports the current status of engineering progress:

Engineering Activity	# authorized	# Complete	Notes
Engineering Assessment	55	51	4 withdrawn by applicant
Engineering Design	21	14	3 withdrawn by applicant

Bidding & Site Showing	11	10	1 withdrawn by applicant
Construction Oversight	13	12	1 pond is under construction, and one is awaiting a landowner decision to proceed with construction

- c. Referred projects to the USDA Farm Service Agency (FSA) to determine the amount of Federal funding available for these projects. FSA approved Federal funding in the amount of \$2,605,155 for 24 ponds. 14 of these 24 have been withdrawn by the applicant.
- d. Completed thirteen pond repair projects, three in Duplin County, two in Lenoir, and one each in Johnston, Lee, Nash, Harnett, Franklin, Robeson, Cumberland and Sampson County.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution - 360 days
 - o Average number of days from fund distribution to project commencement – 717 days
 - o Average number of days from project commencement to project completion – 268 days
- b. Amount and % spent/obligated on administrative activities by Program. \$17,146 4.4%
- c. Amount and % spent/obligated on behalf of recipients by Program. \$373,851.28, 95.6%

Recent Activities for Current Reporting Period (October - December 2021)

Completed design for one pond repair, but repair is on hold pending confirmation of availability of federal funding that is critical to funding the repair. One pond project is still in the design phase pending a decision by the landowner.

One pond in Johnston County has been authorized to begin work.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

5. Non-field Farm Road Repairs

SL 2016-124; Subsection 4.1 (10)(b)

Allocates \$1.0M of the \$12.2M to the Division of Soil and Water Conservation for non-field farm road repairs.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; Division of Soil & Water Conservation

Funding Allocation Update

Appropriated	\$550,000*
Expended	\$404,868
Obligated	\$0
Unobligated Balance	\$145,132

Summary of Activities

- Soil and Water Conservation Districts, with assistance from the Division of Soil and Water Conservation and the Natural Resources Conservation Service, are conducting site visits, working on cost share contracts with the cooperators, and providing technical assistance.
- Districts developed 153 contracts to repair roads in 17 counties. 125 contracts have been installed and completed. 28 contracts have been cancelled at the request of the applicant.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution – 190 days
 - Average number of days from fund distribution to project commencement – 144 days
 - Average number of days from project commencement to project completion – 136 days
- b. Amount and % spent/obligated on administrative activities by Program. \$10,288, 29%
- c. Amount and % spent/obligated on behalf of recipients by Program. \$24,634.00, 71%

Recent Activities for Current Reporting Period (October - December 2021)

All contracts have now either been completed or cancelled. No additional work for non-field farm road repairs due to Hurricane Matthew is anticipated.

* Reallocated \$450,000 to stream debris removal as of the July 2019 meeting of the NC Soil and Water Conservation Commission.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

6. Stream Debris Removal

SL 2016-124; Subsection 4.1 (10)(b)

Allocates \$9.5M of the \$12.2M to the Division of Soil and Water Conservation for stream debris removal.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; Division of Soil & Water Conservation

Funding Allocation Update

Appropriated	\$9,950,000.00*
Expended	\$9,852,207.11
Obligated	\$97,792.89
Unobligated Balance	\$0.00

Summary of Activities

- a. The Department has 44 fully executed contracts with local sponsors including cities, counties, soil and water conservation districts, and organizations.
 - a. 25 of these agreements have funds from both 2016 and 2017 appropriations
- b. Local sponsors have cleared 2,165.00 miles of waterways with funding from both 2016 and 2017.
- c. Thirty-eight contracts have been completed.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution - 255 days
 - o Average number of days from fund distribution to project commencement - 309 days
 - o Average number of days from project commencement to project completion – 858 days
- b. Amount and % spent/obligated on administrative activities by Program. \$41,151.38, 3%
- c. Amount and % spent/obligated on behalf of recipients by Program. \$1,263,548.02, 97%

Recent Activities for Current Reporting Period (October - December 2021)

Six contracts were extended until December 31, 2022. Eleven contracts were completed and closed as of December 31, 2021. Debris removal was completed for 41 miles of streams.

* Reallocated funds from Non-field Farm Repair as of the July 2019 meeting of the NC Soil and Water Conservation Commission.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

7. Cherry Research Farm Dike Repair

SL 2016-124; Subsection 4.1 (10)(c)

\$250k of the \$37,950,000 to the Research Stations Division for dike repairs at the Cherry Research Farm in Wayne County.

Responsible Department and Agency

Department of Agriculture and Consumer Services; Research Stations Division

Funding Allocation Update

Appropriated	\$250,000
Expended	\$-5875
Obligated	\$
Unobligated Balance	\$255,875

Summary of Activities

- a. Design of repairs to the berm are complete and reviewed. Bid solicitation has commenced and contract awarded to repair berm on July 7, 2020. Actual repair of berm started in Sept 2020 and repairs have been slowed due to wet soils and rain. Project is 100% complete. Follow up needed to ensure construction is sound.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution – 90 days
 - o Average number of days from fund distribution to project commencement – 730 days
 - o Average number of days from project commencement to project completion – 1000 days
- b. Amount and % spent/obligated on administrative activities by Program.
 - o 5%; \$1570
- c. Amount and % spent/obligated on behalf of recipients by Program.
 - o NA

Recent Activities for Current Reporting Period (July – September 2021)

Construction was completed in April. No new activity to report.

Contact Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

8. AgWRAP Farm Pond and Dam Repair with PEs

SL 2017-119; Subsection 1.3

Allocates \$6.5M of the \$20M to the Division of Soil and Water Conservation for supplemental funding of the Agricultural Water Resources Assistance Program (AgWRAP) to support disaster-related farm pond and dam repairs.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; Division of Soil & Water Conservation

Funding Allocation Update

Appropriated	\$3,400,000.00*
Expended	\$797,801.71
Obligated	\$1,874,593.00
Unobligated Balance	\$727,605.29**

Summary of Activities

- a. The 2016 funds allocated for AgWRAP Farm Pond and Dam Repair are being used primarily to cover the turnkey engineering evaluations, designs, bidding, and construction oversight aspects of pond repair projects. Construction cost share contracts with individual producers are being funded primarily out of the 2017 funds. Construction funds are not obligated until the final design is completed and approved by the landowner. This is the very last step in a complex process that also requires the farmer to send a check for their contribution to the Division.
- b. Completed twelve pond repair projects, three in Duplin County, two in Lenoir, and one each in Johnston, Lee, Nash, Harnett, Franklin, Robeson, and Sampson County. One pond is under construction in Cumberland County, and one is about to begin construction in Johnston County.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution – 138 days

- Average number of days from fund distribution to project commencement – 189 days
- Average number of days from project commencement to project completion – 199 days
- b. Amount and % spent/obligated on administrative activities by Program. \$0, 0%
- c. Amount and % spent/obligated on behalf of recipients by Program. \$ 536,454, 100%

Recent Activities for Current Reporting Period (October - December 2021)

One pond in Cumberland County has been completed, and one in Johnston County has been authorized to begin work.

Additional repair is necessary for the emergency spillway for one pond that was damaged by Tropical Storm Eta 3 days after it was certified. This project is on hold pending a landowner decision to proceed with the repair.

* Reallocated to stream debris removal as of the July 2019 meeting of the NC Soil and Water Conservation Commission.

** Reallocates \$144,174 and \$88,000 from Matthew Ponds as of November 2021 to Eta stream debris and Michael stream debris, respectively.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

9. Non-field Farm Road Repairs

SL 2017-119; Subsection 1.3

Allocates \$1.0M of the \$20M to the Division of Soil and Water Conservation for non-field farm road repairs.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; Division of Soil & Water Conservation

Funding Allocation Update

Appropriated	\$76,338*
Expended	\$71,038
Obligated	\$0

Unobligated Balance \$5,300

Summary of Activities

- a. Soil and Water Conservation Districts, with assistance from the Division of Soil and Water Conservation and the Natural Resources Conservation Service, are conducting site visits, working on cost share contracts with the cooperators, and providing technical assistance.
- b. Districts developed 15 contracts to repair roads in 7 counties. 13 contracts have been installed and completed.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution – 1 days
 - o Average number of days from fund distribution to project commencement – 64 days
 - o Average number of days from project commencement to project completion – 87 days
- b. Amount and % spent/obligated on administrative activities by Program. \$0, 0%
- c. Amount and % spent/obligated on behalf of recipients by Program. \$71,038, 100%

Recent Activities for Current Reporting Period (October - December 2021)

No activities to report. All contracts have now either been completed or cancelled. No additional work for non-field farm road repair is anticipated.

* Reallocated to stream debris removal as of the July 2019 meeting of the NC Soil and Water Conservation Commission.

**Reallocates \$5,300 from Matthew ponds as of November 2021 to Eta stream debris.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

10. Stream Debris Removal

SL 2017-119; Subsection 1.3

Allocates \$11.5M of the \$20M to the Division of Soil and Water Conservation for stream debris removal.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; Division of Soil & Water

Conservation

Funding Allocation Update

Appropriated	\$15,523,662.00*
Expended	\$12,184,058.37
Obligated	\$3,202,394.21**
Unobligated Balance	\$137,209.42**

Summary of Activities

- a. The Department has 41 fully executed contracts with local sponsors including cities, counties, soil and water conservation districts, and organizations.
 - a. 25 of these agreements have funds from both 2016 and 2017 appropriations
- b. Local sponsors have cleared 2,165.00 miles of waterways with funding from both 2016 and 2017.
- c. Thirty-eight contracts have been completed.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution – 403 days
 - o Average number of days from fund distribution to project commencement – 329 days
 - o Average number of days from project commencement to project completion – 1092 days
- b. Amount and % spent/obligated on administrative activities by Program. \$88,557.68, 1.7%
- c. Amount and % spent/obligated on behalf of recipients by Program. \$5,190,852.57, 98.3%

Recent Activities for Current Reporting Period (October - December 2021)

Six contracts were extended until December 31, 2022. Twelve contracts were completed and closed as of December 31, 2021. Debris removal was completed for 59 miles of streams.

** Reallocates \$365,835 from Matthew stream debris as of November 2021 to Eta stream debris.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

11. Drought Pasture Renovation

SL 2017-119; Subsection 1.3

Allocates \$1.0M of the \$20M to the Division of Soil and Water Conservation to be used for drought relief in the 20 counties in western North Carolina that have been declared a federal disaster by the Secretary of the United States Department of Agriculture due to the prolonged drought.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; Division of Soil & Water Conservation

Funding Allocation Update

Appropriated	\$1,000,000.00
Expended	\$865,309.00
Obligated	
Unobligated Balance	\$134,691.00**

Summary of Activities

- a. Soil and Water Conservation Districts have developed 261 contracts for Drought Pasture Renovation over 4,595 acres in 15 counties.
- b. 233 contracts have been completed, restoring 3,981 acres of pasture. To date, farmers cancelled 28 contracts.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution – 9 days
 - o Average number of days from fund distribution to project commencement – 78 days
 - o Average number of days from project commencement to project completion – 444 days
- b. Amount and % spent/obligated on administrative activities by Program. \$52,716, 26%
- c. Amount and % spent/obligated on behalf of recipients by Program. \$151,954.00, 74%

Recent Activities for Current Reporting Period (October - December 2021)

No activities to report. All contracts have now either been completed or cancelled. No additional work for drought pasture renovation is anticipated.

** Reallocates \$134,691 from Matthew pasture renovation as of November 2021 to Eta stream debris.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

12. Stream Debris Removal

SL 2019-224; Section 2.1 (9)

Allocates \$1M for stream debris removal.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; Division of Soil & Water Conservation

Funding Allocation Update

Appropriated	\$1,000,000.00
Expended	\$0.00
Obligated	\$869,319.24
Unobligated Balance	\$130,680.76

Summary of Activities

Two contracts have been fully executed with local sponsors. The two sponsors have received money from Florence appropriations as well.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution – 27 days
 - o Average number of days from fund distribution to project commencement – 94 days
 - o Average number of days from project commencement to project completion – 488
- b. Amount and % spent/obligated on administrative activities by Program. \$0, 0%
- c. Amount and % spent/obligated on behalf of recipients by Program. \$0, 0%

Recent Activities for Current Reporting Period (October - December 2021)

No activity to report.

Contact

13. Stream Debris Removal

SL 2019-250; Section 1.2(5)

In addition to any other funds appropriated during the 2019-2020 fiscal year, there is appropriated from the unappropriated balance in the General Fund, fifty-nine million fifty thousand dollars (\$59,050,000) in nonrecurring funds for the 2019-2020 fiscal year to be allocated of which the Department of Agriculture and Consumer Services, Division of Soil and Water Conservation received \$5M for stream debris removal.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; Division of Soil & Water Conservation

Funding Allocation Update

Appropriated	\$5,000,000.00
Expended	\$1,655,129.98
Obligated	\$3,444,870.02
Unobligated Balance	\$0

Summary of Activities

The Division of Soil & Water Conservation has entered into contracts with 28 local sponsors to perform debris removal activities. 14 of those local sponsors have received Florence money also. 11 projects have expended funds, and two have completed their projects.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution – 218 days
 - o Average number of days from fund distribution to project commencement – 179 days
 - o Average number of days from project commencement to project completion – 305 days
- b. Amount and % spent/obligated on administrative activities by Program. \$0, 0%
- c. Amount and % spent/obligated on behalf of recipients by Program., \$1,655,129.98, 100%

Recent Activities for Current Reporting Period (October - December 2021)

Debris removal was completed for 32 miles of stream.

14. Forest Service Emergency Response Equipment

SL 2018-5; Subsection 5.6 (b) (2)e

Provides \$700,000 from the State Emergency Response/Disaster Relief Reserve to purchase emergency response equipment, including fire dozers, truck tractors, and trailers.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; NC Forest Service

Funding Allocation Update

Appropriated	\$700,000
Expended	\$700,000
Obligated	\$0
Unobligated Balance	\$0

Summary of Activities

- a. Purchase of Fire Control Tractor for Bladen County
- b. Purchase of 35-ton trailer to transport fire control trailer in Bladen County
- c. Purchase of Fire Control Tractor for Harnett County

Recent Activities for Current Reporting Period (October - December 2021)

All funds have been expended; no activities to report.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

15. Purchase of Bulldozers & Tractor Plows

SL 2019-224; Subsection 2.1 (9)

Allocates \$1M for the purchase of wildland fire emergency response initial attack bulldozers and tractor/plow units.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; NC Forest Service

Funding Allocation Update

Appropriated	\$1,000,000
Expended	\$1,000,000
Obligated	\$0.00

Unobligated Balance \$0.00

Summary of Activities

- a. 3 fire control bulldozers have been ordered, received, and paid.
- b. 2 transport trailers (part of the tractor/plow units) have been ordered, received, and paid.

Performance Metrics

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution
 - Not Applicable
 - o Average number of days from fund distribution to project commencement
 - Requisitions were entered for the full amount 8 days after notice of SB429 passing.
 - o Average number of days from project commencement to project completion
 - The project has not yet been completed.
- b. Amount and % spent/obligated on administrative activities by Program.
 - \$0.00; 0%
- c. Amount and % spent/obligated on behalf of recipients by Program.
 - \$1,000,000; 100%

Recent Activities for Current Reporting Period (October - December 2021)

All equipment has been received and put in service in Caswell, Duplin, and Northampton counties.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

16. Agricultural Disaster Program

SL 2018-138; Subsection 1.3(3)

\$240M allocated to the Department of Agriculture and Consumer Services, Hurricane Florence Agricultural Disaster Program of 2018, established in Section 5.11 of SL 2018-136. The program will provide financial assistance to farmers for disaster recovery affected by Hurricane Florence.

Responsible Department and Agency

North Carolina Department of Agriculture and Consumer Services

Funding Allocation Update

Appropriated	\$240,000,000.00
Expended	\$233,645,973.16
Obligated	\$0
Unobligated Balance	\$6,354,026.84

Summary of Activities

1. 7,518 eligible applications from 77 counties across NC.
2. \$233,645,973.16 paid out to affected farmers statewide as of December 31, 2021.
3. Four main types of applications: row crops, specialty crops, livestock and poultry, and aquaculture.
4. Assistance was divided into 4 payments due to ongoing addition of disaster counties and applications.

Program Timeline

November 7, 2018	Application Submission Opens
December 20, 2018	Application submission closes (Aquaculture submission remains open)
January 25, 2019	Aquaculture submission closes
January 30, 2019	1 st round of payments begins
March 11, 2019	Application submission opens for Wilkes and Iredell counties
March 23, 2019	Application submission closes for Wilkes and Iredell counties
April 15, 2019	Application submission re-opens for sharing partners and additional crops
April 30, 2019	Application submission closes for sharing partners and additional crops
May 13, 2019	2 nd round of payments begins
June 20, 2019	2 ND round of payments completed
October 11, 2019	3 rd round of payments to specialty crops begins
October 23, 2019	3 rd round of payments to specialty completed
November 6, 2019	Application submission opens for Buncombe, Haywood, Henderson, Rutherford and Transylvania counties
November 20, 2019	Application Submission closes for Buncombe, Haywood, Henderson, Rutherford and Transylvania counties
December 11, 2019	Payments begin to Buncombe, Haywood, Henderson, Rutherford and Transylvania counties
December 23, 2019	Payments completed to Buncombe, Haywood, Henderson, Rutherford and Transylvania counties

January 28, 2020	Final round of payments begins
March 16, 2020	Final round of payments completed

Performance Metrics

- a. Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution: 56 Days
 - Average number of days from fund distribution to project commencement: N/A
 - The Florence Aid to Farmers program funds were distributed directly to program applicants. No additional projects were started
 - Average number of days from payment commencement to payment completion: 332 Days
- b. Amount and % spent/obligated on administrative activities by Program: \$0/0%
- c. Amount and % spent/obligated on behalf of recipients by Program: \$233,645,973.16 /100%

Recent Activities for Current Reporting Period (October - December 2021)

No activities to report.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

17. State Match for Federal Farmer Assistance

SL 2018-136; Subsection 6.1 (5)

Allocates \$20M to the Department of Agriculture and Consumer Services to provide the State match for federal farmer assistance programs. Session Law 2019-224 Section 1.2 reverts the sum of \$17M from the Department of Agriculture and Consumer Services to the Hurricane Florence Disaster Recovery Fund.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; Emergency Programs

Funding Allocation Update

	Total	Session Law 2018-136
		Session Law 2019-224
Appropriated	\$3,000,000	
Expended	\$0	

Obligated	\$0
Unobligated Balance	\$3,000,000

Summary of Activities

- Composted 4.1 million poultry, preventing public health issues associated with improper carcass disposal during a mass mortality event.
- Through the efforts of AgEOC livestock teams, prevented stranded, isolated or loose animals from dying by delivering feed and fencing supplies.
- Managed and assisted efforts to prevent companion animal deaths at flooded animal shelters.
- Protected public health and consumer safety by inspecting retail outlets for contaminated or otherwise spoiled products unfit for human consumption, primarily due to contact with flood waters.
- Inspected crop damages caused by hurricane flooding and assisted affected farmers.

Performance Metrics

No response or recovery activity for this period. Program ended before October 2019.

Recent Activities for Current Reporting Period (October - December 2021)

Returned FEMA reimbursement funds to DPS June 2020. No new activity to report.

Contact Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

18. Agriculture Recovery for Farmers

SL 2018-136; Subsection 6.1 (23)

Allocates \$50M to the Department of Agriculture and Consumer Services to assist farmers with recovery activities such as hay relief, pasture renovation, non-field farm road repair, best management practices renovations, reforestation efforts and to provide federal matches as needed.

Responsible Department and Agency

North Carolina Department of Agriculture & Consumer Services; Division of Soil & Water Conservation, NCFS

Funding Allocation Update

Appropriated	\$50,000,000
Expended	\$16,828,075.95
Obligated	\$15,264,845.28

Unobligated Balance \$17,907,078.77*

Summary of Activities

- a. 2019 Florence Reforestation Fund reimbursed 185 unduplicated landowners, 215 projects, 214 forestry practices on 7,897 acres.
- b. 2020 Florence Reforestation Fund reimbursed 245 unduplicated landowners, 274 projects, 635 forestry practices on 27,114 acres.
- c. 1790 bales of hay delivered to 25 farmers.
- d. 2021 Florence Reforestation Fund reimbursed 393 unduplicated landowners, 435 projects, 466 forestry practices on 17,935 acres.
- e. The Department has received applications from 76 local sponsors (counties, soil and water conservation districts, drainage districts, municipalities, and NGOs) to address restoration of critical drainage networks by removing vegetative debris and sediment deposited during Hurricane Florence that is impeding drainage. This is being done in close coordination with the USDA Emergency Watershed Protection Program. For sites approved for federal assistance, state funds are being used to provide the non-federal match to local sponsors.
- f. The Department received state funding to supplement federal funds to Emergency Conservation Program (ECP) payments, such that producers receiving ECP assistance may pay as little as 7 percent of eligible costs for covered activities.
- g. The Soil and Water Conservation Commission approved eight eligible cost share practices and allocations for soil and water conservation districts to contract with farmers and landowners to install best management practices to help address the damage that Hurricane Florence caused.
 - a. Winter Forage Crop Planting – This practice is intended to establish winter forage crops to replace lost livestock feed and to provide a late season receiving crop to enable livestock to manage wastes going into the winter. Local soil and water conservation districts implemented 77 contracts of Winter Forage Crop replanting 4,957 acres of annual grasses in 19 counties. All contracts have been completed and the program is closed.
 - b. Disaster Pasture Renovation – This practice is intended to restore pastureland and spray field vegetation that was damaged by flood waters. Local districts developed 173 contracts with farmers who are seeking assistance to restore 5,650 acres. 108 of these contracts have been implemented replanting 3,293 acres of pastureland in 24 counties. To date, 33 farmers cancelled their contracts. Additional acres will be planted during the fall planting season.
 - c. Disaster Lagoon Management - This program assists farmers with the costs of extraordinary actions needed to manage waste lagoons associated with livestock operations. Soil and water conservation districts have approved and

implemented 126 contracts of Disaster Lagoon Management Incentive properly applying 134 million gallons of lagoon liquid in 13 counties. All contracts have been completed and the program is closed.

- d. Agricultural Pond Repair/Retrofit and Emergency Agricultural Pond Repair/Retrofit – These two practices assist farmers to repair or rebuild agricultural water supply ponds damaged during Hurricane Florence. Districts have approved 24 contracts in ten counties to repair damaged ponds. Repairs have been completed for 20 ponds.
- e. Non-field Farm Road Repair and Emergency Access Restoration – These two practices assist farmers to repair farm access roads that were damaged during Hurricane Florence. Local districts have developed 386 farm road repair contracts in 29 counties; farmers cancelled 51 of these contracts. To date 314 contracts have been completed. Two districts received allocations for new contracts and 2 were installed in 2 counties spending \$10,009.
- h. The Division developed design tools to expedite practice design and installation.
- i. The Division improved program delivery by implementing process improvements to speed contracting, construction certification and payment.
- j. The Division coordinates with USDA on road repair and pond repair projects to ensure federal and state funds are used cooperatively.

Performance Metrics (Cumulative since January 1, 2020)

- a. Average Time for Project Delivery by **NCFS Program**
 - Average number of days from application to fund distribution
 - Additional \$2.5M awarded to NCFS was announced December 2020. Applications began to receive allocation for project funding in January 2021.
 - Average number of days from fund distribution to project commencement
 - Project funding is available immediately to landowners once funding is complete.
 - Average number of days from project commencement to project completion
 - Landowners are required to complete projects before May 1, 2022 expiration date.
- b. Amount and % spent/obligated on administrative activities by Program.
 - \$25,000 total obligated for administrative activities
 - \$10,465.34/42% spent; \$14,534.66/58% obligated
- c. Amount and % spent/obligated on behalf of recipients by Program.
 - \$5,000,000 awarded for recipient allocation
 - \$2,369,664.34/47% spent; \$2,296,622.00/46% obligated
- d. Average Time for Project Delivery by **DSWC Program**

- Average number of days from application to fund distribution – 149 days
- Average number of days from fund distribution to project commencement – 89 days
- Average number of days from project commencement to project completion – 200 days
- e. Amount and % spent/obligated on administrative activities by Program.
\$163,513.78/1.4%
- f. Amount and % spent/obligated on behalf of recipients by Program.
\$11,443,189.72/98.6%

Recent Activities for Current Reporting Period (October - December 2021)

NC Forest Service Activities

42 landowners completed 49 practices on 1,906 acres, reimbursed \$93,717.20. Funded 18 Replant Projects to 17 landowners for 18 planting practices on 873 acres, \$34,188.00.

Division of Soil & Water Conservation Activities

ECP - 7 producers were paid during this reporting period totaling \$7,252.80. To date 1294 payments have been made totaling \$6,229,284.64.

Stream Debris – The Department has allocated debris removal funds to 76 local sponsors. 68 contracts are fully executed. For 38 of the 76 local sponsors, NCDA&CS funds are matching more than \$26.7 million in USDA Emergency Watershed Protection Program funding. 12 contracts are complete. The Division paid \$1,824,030.60 to 18 local sponsors for work completed.

Agricultural Pond Repair/Retrofit and Emergency Agricultural Pond Repair/Retrofit – No pond repair projects were completed this quarter.

Non-field Farm Road Repair and Emergency Access Restoration - Three road repair projects have been completed this quarter bringing the total number of road repairs completed to 314.

Pasture Renovation - Three pasture renovation contracts were completed this quarter affecting 184.77 acres in Duplin and Jones Counties.

BMP Repair/Renovation - No new work was completed this quarter.

* Reallocated 1.7M from Florence as of November 2021 to Eta \$700,000 stream debris removal and Fred \$1M stream debris removal.

Contact

Carrie Sticklin; 919-707-3034; Carrie.Sticklin@ncagr.gov

Department of Commerce

1. Grants to Repair, Replace and Build New Infrastructure

SL 2016-124 Section 4.1 (8)

Grants to local governments to assist with the repair or replacement of public infrastructure or for new infrastructure to support new residential structures in areas outside the 100-year floodplain. Infrastructure includes water, sewer, sidewalks, storm drainage, public buildings and other similar projects to aid with Hurricane Matthew, the western wildfires, and Tropical Storms Julia and Hermine.

Responsible Department and Agency

North Carolina Department of Commerce, Rural Economic Development Division

Funding Allocation Update

	Total	SL here
Appropriated		\$10,000,000.00
Expended		\$6,600,324.81
Obligated		\$3,399,675.19
Unobligated Balance		\$0.00

Summary of Activities

- a. Awarded 16 grants
- b. Paid \$325,152 to OSBM for reporting requirements
- c. \$6,660,324.81 has been paid to grantees through December 31, 2021 based upon grantee requests for funds
- d. Six grantees have drawn down all funds and the grants are closed out.

Performance Metrics

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to Contract-30 days
- b. Amount and % spent/obligated on administrative activities by Program.-Paid to OSBM-\$325,152-.03%
- c. Amount and 0% spent/obligated on behalf of recipients by Program.-\$0

Recent Activities for Current Reporting Period (October-December 2021)

No payments were issued during this project period. Staff participated in meetings with grantee and funder representatives for the Town of Princeville project. Grantees have reported that

60,025 residential and non-residential units will benefit from infrastructure repairs/replacements.

Contact

Melody Adams, melody.adams@ncommerce.com

Department of Environmental Quality

1. Grants for Environmental Infrastructure

SL 2016-124, 4.1 (9)

Program service charges in the amount of \$325,152 per agency were paid to the Office of State Budget and Management (OSBM) and to the Department of Public Safety, Division of Emergency Management (DEM) for administration, technical assistance, and program management services.

Responsible Department and Agency

Department of Environmental Quality, Division of Administration

Office of State Budget and Management

Department of Public Safety, Division of Emergency Management

Funding Allocation Update

Appropriated	\$650,304
Expended	\$650,304
Obligated	\$
Unobligated Balance	\$

Summary of Activities

- a. Effective and prudent deployment of recovery funds to ensure maximum utilization of federal funds. OSBM provides statewide auditing, financial reporting, financial and budget guidance to all state agencies and other entities specified in the 2016 through 2018 Disaster Recovery Acts.
- b. Funding for DEM's statewide cost to modify storm victim applicant tracking systems to better track environmental studies, environmental status reports, local agency environmental infrastructure projects and related administrative costs associated with storm damage recovery.

Performance Metrics

Not available from DEQ. The funds were transferred for the activities above in FY2016.

Recent Activities for Current Reporting Period (October - December 2021)

All funds expended, no activities to report.

Contact: Office of State Budget and Management

Department of Public Safety, Division of Emergency Management

2. Emergency Watershed Protection Program Match

SL 2018-138, 1.3 (6)

The Division of Coastal Management has been granted federal assistance under the Emergency Watershed Protection (EWP) program, Natural Resources Conservation Service (NRCS) to restore damages caused by Hurricane Florence. The project focus is removal of destroyed docks, decks, bulkheads, displaced vessels, and other shoreline structures that resulted in widespread marine debris in coastal waterways and on public trust properties from Brunswick County north through Carteret. Debris removal was prioritized through field mapping conducted by NRCS with assistance from the Division. As of February 2, 2020, NRCS and the Division entered into an agreement that includes a total project budget of \$2,416,884.00. This includes \$543,120 in non-federal match. \$250,000 of this match is from the Florence Disaster Bill (SL2018-138) and the \$293,120 is from lapsed salary from the Department of Environmental Quality. Work began in July 2020 and by the end of the EWP project, over 1,254,280 pounds of debris, not including weights of 24 abandoned storm-displaced vessels, had been removed from State owned and public lands.

Responsible Department and Agency

Department of Environmental Quality, Division of Coastal Management

Funding Allocation Update

	Total	SL 2018-138 1.3 (6)
Appropriated	\$250,000	
Expended	\$222,240.00	
Obligated	\$27,760.00	
Unobligated Balance	\$0	

Summary of Activities

- A contract with the North Carolina Coastal Federation to conduct the debris removal work was finalized on 15 June 2020.
- June 2020 – July 2020: The Division and Coastal Federation coordinated on project logistics, including prioritization of debris removal.
- July 2020 – June 2021: Debris and vessel removal conducted in New Hanover, Onslow, Pender, Craven, Carteret, and Brunswick counties.

- July 2021 – September 2021: Debris and vessel removal continued and ended on 31 August 2021.
- 10 September 2021 – December 2021: The EWP project ended, and clean-up activities resumed with non-state funds that were awarded directly to the contractor by the National Fish and Wildlife Foundation.

Performance Metrics

- Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution: 454 days (November 7, 2018 – February 4, 2020)
 - Average number of days from fund distribution to project commencement: 160 days (February 4, 2020 – July 15)
 - Average number of days from project commencement to project completion: 679 days (3 extensions were granted during federal part of project; anticipated end date for entire project is 30 May 2022)
- Amount and % spent/obligated on administrative activities by Program: 0
- Amount and % spent/obligated on behalf of recipients by Program. \$27,760.00

Recent Activities for Current Reporting Period (October – December 2021)

During the reporting period, the contractor – North Carolina Coastal Federation – continued debris removal with a non-state funding source when the EWP project concluded on 10 September 2021. Remaining debris removal with \$27,760.20 of SL 2018-138 1.3(6) will conclude no later than May of 2022.

Contact

Paula Gillikin, 252-838-0886, paula.gillikin@ncdenr.gov

3. Various Projects within DEQ – Division of Coastal Management SL 2019-224 2.1 (3)

The purpose of this program is to help increase the resilience of N.C.'s coastal communities and natural resources. Part I. *Creating a State Framework for Coastal Resilience Planning & Project Readiness* will fund local vulnerability assessments, develop construction-ready projects, and complete at least one ecosystem restoration or enhancement project. Part II. *Collaborative Resilience Planning and Engineering to Strengthen Ecosystems at the Rachel Carson Reserve* will build upon an existing vulnerability assessment to develop a resilience plan that will help strengthen ecosystems at the Rachel Carson Reserve, which protects the Town of Beaufort. The program will leverage a \$1.14 million federal matching grant to complete these tasks.

Responsible Department and Agency

Funding Allocation Update

	Total SL 2019-224 2.1 (3)
Appropriated	\$1,480,000
Expended	\$223,307.20
Obligated	\$225,454.54
Unobligated Balance	\$1,031,238.26

Part I. State Framework for Coastal Resilience Planning and Project Readiness

Summary of Activities

These funds were used as match for a competitive proposal to the 2019 Emergency Coastal Resilience Fund, administered by the National Fish and Wildlife Foundation (NFWF), and NFWF awarded DCM \$1.14 million. DCM is partnering on this project with the N.C. Office of Recovery and Resiliency, N.C. Sea Grant, and The Nature Conservancy. DCM designed and launched the NC Resilient Coastal Communities Program ([RCCP](#)) in October 2020, which consists of four phases:

- Phase 1: Community Engagement and Risk & Vulnerability Assessment
- Phase 2: Planning, Project Selection and Prioritization
- Phase 3: Engineering and Design
- Phase 4: Implementation

Performance Metrics

After some delay, DCM executed contracts with 10 subgrantees effective August 11th, to provide technical assistance to 26 communities, and has started receiving invoices for work completed.

- 26 Community Action Teams created, representing over 200 engaged stakeholders.
- \$339k invoiced to date, representing 48 percent of the \$705k obligated to date.

Recent Activities for Current Reporting Period (October – December 2021)

The Division of Coastal Management's (DCM) [Resilient Coastal Communities Program](#) (RCCP) is underway, with funding from DEQ under S.L. 2019-224, and an Emergency grant from the National Fish and Wildlife Foundation (NFWF). 26 communities and 10 vendors have been selected, contracts were executed, and work began in August. Phases 1 & 2 contracts total \$705,000, from a combination the NFWF grant and our state match.

The Planning Handbook lays out the required activities and deliverables for this work, and the communities and contractors are well underway. Most work is expected to be complete by March 31, 2022. The main components of the final deliverable, which consists of the outcomes of each activity, are listed below.

Vision & Goals

- ☐ State the community's vision and resilience goals

Community Action Team Report

- ☐ Create a Community Action Team, consisting of key stakeholders
- ☐ Meeting agendas, minutes, and list of participants

Stakeholder Engagement Strategy

- ☐ Plan for engagement with the community during risk assessment and project development, including a minimum of two public events.

Review Existing Local & Regional Efforts

- ☐ Inventory of relevant plans, ordinances, policies, and programs

Risk and Vulnerability Assessment Report

- ☐ Maps of critical assets, natural infrastructure and vulnerable populations
- ☐ Assess vulnerability
- ☐ Estimate risk

Project Portfolio

- ☐ Portfolio detailing a minimum of five shovel-ready priority projects and action items.

Additional Files

- ☐ Mapping products and excel spreadsheets generated from the risk and vulnerability assessments.

All communities have gotten at least to the point of inventorying existing plans and data, and most have completed at least an initial draft of their Risk and Vulnerability Assessment Report. The 10 contractors have been doing most of their engagement with the 26 Community Action Teams, small teams of 5-12 key community stakeholders. Teams have been meeting regularly, and providing much of the information that is compiled and put out for public review and input. As the teams work to complete the tasks and finalize their deliverables by March 2022, DCM has been working to draft a Request for Applications for the Phase 3 Engineering and Design sub-awards. We intend to release the RFP in January, and to fund up to 26 E&D projects at an average of \$45,000 per project. We have a total of \$1.2 million budgeted for E&D sub-awards. In November, DCM was notified that we have been awarded \$545,860.00 by the National Fish and Wildlife Foundation, for a grant application that we submitted in June. \$616k of our S.L. 2019-224 appropriation has been committed as match. We are currently awaiting the funds from NFWF.

Part II. Collaborative Resilience Planning and Engineering to Strengthen Ecosystems at the Rachel Carson Reserve

Summary of Activities

- Provided a tour for engineering partners to view areas that were discussed at the partner meeting.
- Held several project team meetings to digest partner feedback and begin to identify two shovel-ready projects for engineering.
- Engaged with outside initiatives (below) that are conducting relevant work to identify synergies between projects.
 - [Town of Beaufort Comprehensive Plan](#)
 - Town of Beaufort Resilience Communities Program (NFWF Part I)
- Refined purpose, vision, and goals of the habitat resilience plan and began adding strategies and actions as developed by staff or through the partner meeting feedback and input. View the document, [here](#).
- Scopes of work have been drafted for engineering partners and contracts will be executed early in 2022.

Recent Activities for Current Reporting Period (October – December 2021)

In September, (last reporting period), the platform “Mural” was used to successfully support an experience where participants interacted with [reserve maps, vulnerability assessment information, and provided feedback in real-time](#) as group facilitators moved through the material. The results of the meeting revealed that there are areas of the site that should be prioritized for resilience projects, with a popular theme of conducting additional research in tandem with or prior to implementation of on-the-ground projects. Staff and engineering partners are currently working through workshop input and outcomes to pinpoint two shovel-ready projects that will be soon engineered. We are now in the process of developing contracts with Kris Bass Engineering and North Carolina State University’s Department of Biological and Agricultural Engineering (professor and students) to develop and produce the engineered plans to the point of shovel-readiness. Work continues to develop the Rachel Carson Reserve habitat resilience plan outline into a draft plan with full text. A draft of the vision, purpose, goals, and partially developed strategies can be found, [here](#).

Contact

Tancred Miller, tancred.miller@ncdenr.gov, 252-808-2808 ext. 224.

4. Disaster Recovery for Coastal Reserves

SL 2019-250, 1.2(9)

This appropriation supports disaster recovery at the DEQ Division of Coastal Management’s N.C. Coastal Reserve sites, specifically, “repair, restoration, and related environmental disaster

recovery activities.” With ten sites located along the coast of N.C., the Coastal Reserve sites received direct impacts from Hurricanes Florence and Dorian such as erosion and deposition on oceanfront and estuarine shorelines, grounded vessels at the Rachel Carson and Masonboro Island Reserves, significant accumulation of large marine debris such as lumber, floating docks and pilings, downed trees blocking trails and roads at 5 reserve sites, missing signs, and damage to the boardwalk at the Currituck Banks and Rachel Carson Reserves. The Reserve’s operational budget does not include funding for disaster recovery and these funds are complementing federal funds and partner contributions to complete recovery activities and prepare for the upcoming storm season.

Responsible Department and Agency

Department of Environmental Quality, Division of Coastal Management

Funding Allocation Update

	Total SL 2019-250 1.2 (9)
Appropriated	\$50,000.00
Expended	\$49,491.43
Obligated	\$0
Unobligated Balance	\$508.57

Summary of Activities

To date, this appropriation has supported clean-up of trails at 4 reserve sites, allowing the sites to reopen safely to the public in fall 2019. This included supplies and travel for downed tree removal and hiring a contractor to remove a hazardous tree. A contract is completed with Atlantic Coast Marine Group (\$40,500) to remove a Dorian-stranded vessel at the Masonboro Island Reserve and large pieces of marine debris at the Rachel Carson and Masonboro Island Reserves (end date of June 30, 2021). Replacement signs and supplies for the 2020 storm season were purchased. Plants were purchased and planted to help restore the storm-damaged Rachel Carson Reserve bird rookery habitat. Remaining funds will be used to purchase storm supplies for the 2022 season.

Performance Metrics

- Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution – 143
 - Average number of days from fund distribution to project commencement - 0
 - Average number of days from project commencement to project completion -1095 (anticipated completion June 30, 2022)
- Amount and % spent/obligated on administrative activities by Program. - \$0
- Amount and % spent/obligated on behalf of recipients by Program. – 49,191.00

Recent Activities for Current Reporting Period (October – December 2021)

Activities for the current reporting period included the following: Plants from the native plant nursery were planted to help restore the storm-damaged Rachel Carson Reserve bird rookery habitat. Plant expenses are not yet reflected in the funding allocation update as they had not posted to the system at the time of the report generation. Remaining funds will be used to purchase storm supplies for the 2022 season in early 2022.

Contact

Rebecca Ellin, rebecca.ellin@ncdenr.gov, 252.838.0880

5. Grants for Environmental Infrastructure

SL 2016-124, 4.1(9)

The funding from this Session Law within the Division of Energy, Mineral, and Land Resources was used to address five separate projects in response to Hurricane Matthew. The first project addressed issues at Salvo Cemetery that occurred as a direct cause by Hurricane Matthew. Severe erosion began to impact the Salvo Day Use Cemetery in Dare County. Dare County installed a 230 feet vinyl bulkhead and armor stone along the sound front edges. This project was completed in June 2018. Projects two and three included the planning and implementation of controlled emergency breaches of Woodlake Dam in Moore County and Gables Dam in Cumberland County to render them safe. Both dams were severely damaged as a result of Hurricane Matthew threatening the life, health, safety and property of the downstream public. Projects one through three are complete. Projects four and five can be classified as Safety and Resilience projects that include dam overtopping studies of over 200 dams in the Neuse River Basin and approximately 50 dams in the Lumber River Basin. These studies include hydrology and hydraulic modeling to determine likely storm sizes that could overtop the dams in the study population. This information allows the state and local governments to set priorities on responses to dams given limited personnel resources as well as monitor the need for dam modifications in the future. These two study projects are complete currently. This project with its tasks is complete.

Responsible Department and Agency

Department of Environmental Quality, Division of Energy, Mineral, and Land Resources

Funding Allocation Update

	Total	SL 2016-124 4.1 (9)
Appropriated	\$3,118,302.00*	
Expended	\$3,117,711.91	

Obligated \$

Unobligated Balance \$ 590.00

Summary of Activities

- DEQ/DEMLR/Dam Safety Implemented a controlled emergency breach of Woodlake Dam (Moore County)
- DEQ/DEMLR/Dam Safety Implemented a controlled emergency breach of Gables Dam (Cumberland County)
- Emergency Response, Safety and Resilient Overtopping study of over 260 dams in the Neuse and Lumber River Basins

Salvo Cemetery Bulkhead

- a. Dare County was the recipient of the funding.
- b. A contractor was selected, and design was prepared.
- c. Construction started in May 2018 and was completed in late June 2018.

Performance Metrics

1. Salvo Cemetery Bulkhead

Salvo Cemetery Bulkhead

- a. Average Time for Project Delivery by Program
Application by County made in early 2018. Contractor selected by County following State procurement rules.

Funds were distributed as specific tasks were completed. (1) bulkhead design, (2) securing permits, (3) construction of bulkhead and backfill of sand, (4) documentation of project completion. From start to finish approximately 8 months. This project is complete.
- b. Amount and % spent/obligated on administrative activities by Program.
- c. Amount and % spent/obligated on behalf of recipients by Program.

2. Woodlake Dam (Moore County)

- a. Average Time for Project Delivery by Program
 - i. Average number of days from application to fund distribution
 1. Not applicable as project undertaken directly by DEQ
 - ii. Average number of days from fund distribution to project commencement
 1. Not applicable as project undertaken directly by DEQ
 - iii. Average number of days from project commencement to project completion

1. Approximately two years as there was a lot of legal work that had to be done during this project by DEQ, State Construction, and the Attorney General's Office to meet state emergency, contracting, safety and regulatory guidelines. This project is complete.
 - b. Amount and % spent/obligated on administrative activities by Program.
This work was performed by DEQ with Time Limited Staff, Engineering Design Consultants and Contractors that worked directly for DEQ.
 - c. Amount and % spent/obligated on behalf of recipients by Program.
Not applicable.
3. Gables Dam (Cumberland County)
 - a. Average Time for Project Delivery by Program
 - i. Average number of days from application to fund distribution
 1. Not applicable as project undertaken directly by DEQ
 - ii. Average number of days from fund distribution to project commencement
 1. Not applicable as project undertaken directly by DEQ
 - iii. Average number of days from project commencement to project completion
 1. Approximately two years as there was a lot of legal work that had to be done during this project by DEQ, State Construction, and the Attorney General's Office to meet state emergency, contracting, safety and regulatory guidelines. This project is complete.
 - b. Amount and % spent/obligated on administrative activities by Program.
This work was performed by DEQ with Time Limited Staff, Engineering Design Consultants and Contractors that worked directly for DEQ. Less than 5% was used toward administrative activities.
 - c. Amount and % spent/obligated on behalf of recipients by Program.
Not applicable.
4. Neuse River Basin Dam Overtopping Study
 - a. Average Time for Project Delivery by Program
 - i. Average number of days from application to fund distribution
 1. Not applicable as project undertaken directly by DEQ
 - ii. Average number of days from fund distribution to project commencement
 1. Not applicable as project undertaken directly by DEQ
 - iii. Average number of days from project commencement to project completion
 1. Approximately three years as this work involved digital scanning of existing dam files, development of a dams database with the US Army Corps of Engineers, surveying of dams, development of the study model, implementation of the study model and contracting with five Engineering Consulting Firms to assist in performing the computer

dam models. Future projects will move forward much faster as a result of the infrastructure this project set up. This project was completed in October of 2020 and the final report was published in March of 2021. All contractual payments have been completed and this project is complete.

- b. Amount and % spent/obligated on administrative activities by Program.

This work was performed by DEQ with three Time Limited Staff, existing staff and

Contracted engineering firms. Less than 5% was used toward administrative activities.

- c. Amount and % spent/obligated on behalf of recipients by Program.

Not applicable.

5. Lumber River Basin Dam Overtopping Study

- a. Average Time for Project Delivery by Program

- i. Average number of days from application to fund distribution

- 1. Not applicable as project undertaken directly by DEQ

- ii. Average number of days from fund distribution to project commencement

- 1. Not applicable as project undertaken directly by DEQ

- iii. Average number of days from project commencement to project completion

- 1. Approximately 12 months as this work involved surveying of dams, implementation of the study model and contracting with three Engineering Firms to assist in performing the computer dam models. This project took place much quicker than project 4 due to taking advantage of the process initially developed by project 4. This project is complete.

- b. Amount and % spent/obligated on administrative activities by Program.

This work was performed by DEQ with three Time Limited Staff, existing staff and

Contracted engineering firms. Less than 5% was used toward administrative activities.

- c. Amount and % spent/obligated on behalf of recipients by Program.

Not applicable.

Recent Activities for Current Reporting Period (October - December 2021)

Dam Overtopping Hydrology and Hydraulic (H&H) Study

The purpose of this study is to deliver hydrologic and hydraulic (H&H) computer modeling, modeling reports/results, and a database to house the data collected from the H&H studies for 210 dams housed in the Neuse River Basin and 51 dams in the Lumber River Basin. The

data, reports, and models collected from these targeted dams (high hazard and larger impoundments) are generated and available for use by the North Carolina Emergency Management Emergency Operations Center (NCEM EOC), Division of Energy, Mineral, and Land Resources (DEMLR), US Army Corps of Engineers (USACE), Local Emergency Management services and other State & Local agencies. This information will provide more complete and accurate data that could be used for emergency flood response, such as the amount and intensity of precipitation that it would take to overtop dams. This data may also be used to prepare for extreme flooding events, emergency response during the events, advise dam owners to draw down water levels behind structures in advance to a storm event to help with flash flooding and flood control, and to alert emergency management personnel of potential hazards before and during events.

This study is part of a larger project that also includes digitizing all historical data and engineering documents supported by a geodatabase currently being constructed by the USACE for our DEMLR Dam Safety Program to further enhance information availability, improve emergency response and contribute to our overall State resilience efforts.

Summary of Work:

The study for both the Neuse Basin and Lumber Basin are complete. The Volume comprising the 210 dams in the Neuse Basin has been published for download by Local and State EM with the following Laserfiche Link.

<https://edocs.deq.nc.gov/EnergyMiningLandResources/Browse.aspx?dbid=0&startid=17>

The Volume comprising the 51 dams in the Lumber Basin is complete and going through final technical edits. This Volume is also complete.

Contact

W.E. Toby Vinson, Jr., PE, DEMLR Chief of Program Operations, 919-707-9201,
toby.vinson@ncdenr.gov

Dr. Kenneth B. Taylor, PG, State Geologist and Section Chief, (919) 707-9211,
kenneth.b.taylor@ncdenr.gov

*Includes Salvo Cemetery Funds

6. Landslide Mapping

SL 2018-5 5.6(b)(2) a

Funding was authorized to establish a Landslide Mapping Team in the N.C. Geological Survey Section of DEMLR. The team performs landslide emergency response and documents landslide occurrence, susceptibility, modes of failure, areal extent of landslide impacts, and effects and impacts on individuals, property, residences, and infrastructure. The team was composed of four (4) geologists from June 1, 2019 until May 25, 2021. The

team had three (3) geologists from June 1 until July 23, 2021. Currently the team is composed of 2 (2) geologists.

Responsible Department and Agency

Department of Environmental Quality, Division of Energy, Mineral and Land Resources

Funding Allocation Update

	Total	SL 2018-5 5.6(b)(2)
		a
Appropriated	\$3,600,000.00	
Expended by quarter	\$ (2,467.51)	
Expended		
\$1,494,604.25		
Obligated	\$ 886,449.93	
Unobligated Balance	\$1,218,945.82	

Summary of Activities

- Conducts landslide mapping in western North Carolina Counties through in-house mapping, contract mapping by Appalachian Landslide Consultants, PLLC (ALC) and in coordination with Western Carolina University for Rutherford County.

County Progress:

1. **Polk County:** 921 landslides, 685 outlines of areas affected by landslides (547 acres), and 287 deposits from past landslide activity (4,922 acres).
2. **Rutherford County:** 1,607 landslides, 1,391 outlines of areas affected by landslides (1,922 acres) and 603 deposits from past landslide activity (10,044 acres) to date.
3. **Transylvania County:** 130 landslides, 100 outlines of areas affected by landslides (182 acres) and 322 deposits from past landslide activity (4,024 acres) to date.

These features are recorded in the N.C. Geological Survey's landslide geodatabase.

- Landslide susceptibility (where landslides may start) and potential debris flow pathways (where landslide may go) models are complete and posted on the web viewer for Macon, Henderson, Buncombe, Watauga, Polk, and Rutherford Counties. Preliminary landslide susceptibility and potential debris flow pathway models are complete for 16 additional western N.C. counties.
- Developed under contract with UNC-Asheville NEMAC (National Environmental and Modeling and Analysis Center) a publicly available web-based landslide map viewer

that includes landslide data for western N.C., a users' guide, landslide education materials, and landslide susceptibility, and potential debris flow pathway maps for Macon, Watauga, Buncombe, Henderson, Polk, Rutherford Counties.

<http://landslidesncgs.org/>

- Ongoing emergency response to landslides when tasked by the State Division of Emergency Management or requested by county emergency managers. One hundred nine landslides have been mapped and entered the landslide geodatabase to date as part of landslide response activities in 13 western North Carolina counties.
- Ongoing outreach and education on landslide hazards to county government, municipal governments, state agencies, property owners, and professional organizations.
- Ongoing operation and maintenance of landslide monitoring equipment (precipitation gauges, movement monitors) at 9 sites in western North Carolina in collaboration with the U.S. Geological Survey.
- Ongoing coordination with the National Weather Service on identifying and forecasting weather conditions related to landslides, and public advisories in public weather statements and briefings.

Performance Metrics

- Average Time for Project Delivery by Program
 - NEMAC Contract – Work assignments for years 1, 2 and 3 complete. Total payments to date: \$292,796.83.
 - ALC Contract:
 - Polk County:** Task Orders 1 and 2 mapping complete; final data reviewed and in the landslide geodatabase.
 - Rutherford County:** Task Order 3 and 4 field mapping is complete; County quality review is in process.
 - Transylvania County:** A purchase order for Task Order 5 was executed 12/16/2021. Work will begin 1/3/2022.

Recent Activities for Current Reporting Period (October – December 2021)

- a. Field and remote mapping of landslides and QC review of the Polk County data are complete. Data are publicly available in the landslide web map viewer. Field and remote mapping of landslides and QC review of Rutherford County data are complete for Task Order 3. QC review of Rutherford County Task Order 4 in progress with estimated January 2022 completion.
- b. 19 inquiries regarding landslide response, landslide risk, sinkhole hazards, and public relations.
- c. 447 landslides mapped in Rutherford and Transylvania counties October through December 2021.
- d. Ongoing outreach and education on landslide hazards to county government, municipal governments, state agencies, property owners, and professional organizations.
- e. Ongoing operation and maintenance of landslide monitoring equipment (precipitation gauges, movement monitors) at 9 sites in western North Carolina in collaboration with the U.S. Geological Survey.
- f. Ongoing coordination with the National Weather Service on identifying and forecasting weather conditions related to landslides, and public advisories in public weather statements and briefings.

Contact

David Korte, P.G. – Senior Geologist for Engineering Geology and Geologic Hazards, N.C. Geological Survey Section, DEMLR, e-mail: David.Korte@ncdenr.gov [828-296-4540 office].

7. Various Projects within DEQ - DEMLR

SL 2019-224, 2.1(3)

This project is a continuation of our two Safety and Resilience projects that were initiated under **SL 2016-124 4.1 (9)**. In those projects, the DEMLR Dam Safety Program developed hydrology and hydraulic models to determine storm sizes (the amount of rain) that would cause ~261 dams in the Neuse and Lumber River Basins to overtop. Dam overtopping is a sign of inadequate spillway capacity but more importantly is a characteristic of dams in stress which could lead to failure of the dam. This project will continue this overall study effort into the Cape Fear River Basin. The information gained in this study will allow State and Local

governments to set priorities on responses to dams given limited personnel resources as well as monitor the need for dam modifications in the future. The two studies funded under **SL 2016-124 4.1 (9)** have been completed and that reporting is closed for SL 2016-124 4.1(9). DEMLR Dam Safety has completed contracts with the engineering service firms under **SL 2019-224 2.1(3)** and has started this phase of expansion into the Cape Fear River Basin to study approximately 326 dams. The contractors have completed field data gathering. The modeling has also begun and that is approximately 40% complete. We have lost two of our Time-Limited Staff and are in the process of filling them.

Responsible Department and Agency

Department of Environmental Quality, Division of Energy, Mineral, and Land Resources

Funding Allocation Update

	Total SL 2019-224 2.1 (3)
Appropriated	\$2,356,674.00
Expended	\$797,360.17
Obligated	\$ 174,977
Unobligated Balance	\$ 1,384,336.83

Summary of Activities

- Model development process for the Cape Fear Study is complete and we have contracted with RTI and engineering services to gather field data and model each dam.
- Field data gathering is complete at this time.
- Modeling has begun with use of the field survey data and will continue until completion which is expected in July of 2022.

Performance Metrics Cape Fear Dam Overtopping Study

- d. Average Time for Project Delivery by Program
 - i. Average number of days from application to fund distribution
 1. Not applicable as project undertaken directly by DEQ
 - ii. Average number of days from fund distribution to project commencement
 1. Not applicable as project undertaken directly by DEQ
 - iii. Average number of days from project commencement to project completion
 1. It is anticipated that this project will take approximately 18 months, starting in January 2021, as this work involves surveying of dams, implementation of the study model and contracting with Engineering Firms to assist in developing the dam models. This project will take

place much quicker on a time per dam basis than with the initial projects in the Neuse and Lumber basins due to taking advantage of the process initially developed by that project. We do anticipate a longer period of time to complete as was provided in the first report as we are including 50 % more dams (326) than originally envisioned possible in the first quarter. We also anticipate leveraging cost savings from the engineering service firms to possibly expand this study into other river basins impacted by Hurricanes Matthew and Florence.

2. It is also anticipated that the Probable Maximum Precipitation Study, if it cannot be funded by NCORR through Federal HUD grants, will take as long as 18-24 months due to the size of the project and with coordinating with capturing cost savings by teaming with the State of South Carolina in developing the study for both States. At this time, we have been notified that NCORR will be able to use HUD funding for the PMP study. Once verified, we will re-apply DR funding to further expansion of our H&H studies.
- e. Amount and % spent/obligated on administrative activities by Program.
This work is performed by DEQ with three Time Limited Staff, existing staff and Contracted engineering firms. It is anticipated that less than 5% of the total project costs will go to administrative activities.
- f. Amount and % spent/obligated on behalf of recipients by Program.
Not applicable.

Recent Activities for Current Reporting Period (October - December 2021)

Staff have completed the model plan and are working with the contracted firms to complete the field surveys and work on the models using the gathered field data. Project kick-off began in January 2021 and field data gathering is complete. This project is currently moving along quite well.

Contact

W.E. Toby Vinson, Jr., PE, DEMLR Chief of Program Operations, 919-707-9201,
toby.vinson@ncdenr.gov

8. Commercial Fishing Assistance

SL 2018-136, 6.1(19) and SL 2018-138, 1.3(5)

The Commercial Fishing Assistance program was designed to help make up for the losses to the

state's nearly billion-dollar commercial fishing industry due to the storm. Compensation based on income losses from September, October and November harvest reductions due to Hurricane Florence as documented by state harvest records.

Responsible Department and Agency

Department of Environmental Quality, Division of Marine Fisheries

Funding Allocation Update

	Total	SL 2018-136 6.1 (19)	SL 2018-138 1.5 (5)
Appropriated	\$1,600,000		\$10,000,000.00
Expended	\$1,600,000		\$ 9,940,611.32
Obligated	\$0.00		\$ 0.00
Unobligated Balance	\$0.00		\$ 59,388.68

Summary of Activities

- a. 1,782 award letters were mailed to eligible Commercial Fisherman for September landings.
- b. 728 checks disbursed for September losses totaling \$3,568,446.09.
- c. 1,829 letters were mailed to eligible Commercial Fisherman for October and November landings
- d. 1,041 checks disbursed for October and November losses totaling \$7,456,025.99.
- e. An additional final check write was sent out on June 12, 2019 to 1,176 fishermen who participated in the program totaling \$450,000.

Performance Metrics

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution – There was no application process for these funds. Legislation was enacted on 10/16/18 (\$1.6 million) & 12/3/18 (\$10 million). The first phase of fund distribution was for September losses and occurred over multiple check writes between 1/31/19 and 5/13/19. The second phase of fund distribution was for October and November losses and occurred over multiple check writes between 4/3/19 and 5/13/19. The third phase and final phase of fund distribution covered the months of September, October and November and was sent out to exhaust the existing funds from the assistance program on 6/12/19.

- Average number of days from fund distribution to project commencement – The legislation was enacted on 10/16/18 and 12/3/18 and the first funds were distributed on 1/31/19, approximately 60 days.
- Average number of days from project commencement to project completion – The legislation was enacted on 10/16/18 and 12/3/18 and final checks were distributed on 6/12/19, approximately 180 days.
- b. Amount and % spent/obligated on administrative activities by Program. \$66,139.34 was expended on administrative activities/0.57%
- c. Amount and % spent/obligated on behalf of recipients by Program. \$11,474,472.08 distributed to Commercial Fishermen/98.9%

Recent Activities for Current Reporting Period (October - December 2021)

This program resulted in a total of 2,945 individual checks to 1,176 fishermen totaling \$11,474,472.08. This program was able to cover 85.4% of September losses, 91.76% of October losses, and 82.29% of November losses. The program is complete.

Contact

Beth Govoni, Administrative & Maintenance Services Section Chief
(252) 808-8005 office
Beth.Govoni@ncdenr.gov

9. Marine Debris Cleanup

SL 2018-136, 6.1(20)

The North Carolina General Assembly approved funding of \$400,000 to remove marine debris from North Carolina coastal waters and public trust properties. The funds are to be used by the North Carolina Coastal Federation to contract with third parties to collect.

Responsible Department and Agency

Department of Environmental Quality, Division of Marine Fisheries

Funding Allocation Update

Appropriated	\$400,000
Expended	\$400,000
Obligated	\$0.00
Unobligated Balance	\$0.00

Summary of Activities

- a. Documenting the types and locations of marine debris that needs to be collected; securing additional federal and state funds to increase collection efforts; Logistical discussions regarding how to use third party contractors for the identification, collection, transport, disposal and tracking of marine debris; and Identification of third-party contractors and their capabilities in order to determine how best to secure their services for the project.
- b. Marine Debris Site Inventory: Federation staff worked with community partners including local, state and federal government representatives, Hammocks Beach State Park, local boat captains and state agencies to conduct a preliminary site assessment of the locations of concentrations of marine debris in public trust areas of the coast impacted by Hurricane Florence. Federation staff and volunteers surveyed estuarine islands by boat and through marsh walks to locate and photograph marine debris that needs to be collected. Boat surveys in Bogue Sound, Bogue Inlet, White Oak River, Bear Creek, and Hammocks Beach State Park were conducted in December and January. One of these surveys included three potential contractors that identified substantial amounts of marine debris including treated lumber, abandoned and derelict vessels, remnants of docks, piers and pilings and multiple other storm debris. With additional financial assistance from the Natural Resources Conservation Service, a more formal Damage Assessment Survey is still being completed that covers a geographic area from Hyde County to Wilmington. This survey will help to focus the use of additional federal and state funds as well as the current cleanup.
- c. Leveraging State Funds for Additional Federal Funding: The federation is working with the N.C. Division of Coastal Management to secure up to \$1 million in additional federal funding from the Emergency Watershed Program run by the Natural Resources Conservation Service (NRCS) to expand the marine debris removal efforts described in this document. This additional federal funding will be matched with a portion of the funding from this project as well as an additional \$250,000 appropriated by the N.C. General Assembly to the Division. If approved by NRCS, this additional funding will allow the federation and Division to include much of the entire coast of N.C. in their cleanup efforts and to remove many abandoned vessels. The request for this additional federal funding has received preliminary approval from NRCS.
- d. Cleanup: The federation has executed contracts with third party contractors to collect marine debris. The clean-up process consists of three phases. Phase I is the collection of smaller debris that consists of plastic bottles, Styrofoam pieces, aluminum cans, food containers and an assortment of consumer and household debris. Phase II clean-up efforts focus on the heavier wooden debris such as dock,

pilings, decking and pressure treated wood that requires heavy equipment for removal. Phase III will focus on abandoned and derelict vessels.

Performance Metrics

- a. Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution - contract executed December 6, 2018, first fund distribution December 18, 2018, second fund distribution March 26, 2019, third/final fund distribution June 26, 2019.
 - Average number of days from fund distribution to project commencement – legislation enacted October 18, 2018, contract executed December 6, 2018 and first funds were distributed on December 18, 2018, approximately 60 days.
 - Average number of days from project commencement to project completion – approximately 365 days
- b. Amount and % spent/obligated on administrative activities by Program. – 0%
- c. Amount and % spent/obligated on behalf of recipients by Program. – 100%

Recent Activities for Current Reporting Period (October - December 2021)

Phase I:

In the Coastal Federation's central region, contractors removed smaller and lighter debris items that mechanical equipment can't remove. Using hand labor, the debris is bagged and removed to landfills in rented dumpsters. These contractors are commercial fishers and other local residents hired at a daily rate. The standard cleanup crew for this part of the project includes a lead contractor who provides transportation and boats, a crew foreman, and five additional watermen for the work crew. This work crew started February 11 and finished April 12 and mainly focused on publicly owned dredge spoil islands. The crew collected 12.6 tons (25,100 pounds) of marine debris. The crew also removed debris from the 1.3-mile shoreline of Huggins Island, which is part of Hammocks Beach State Park. Using hand labor, the debris is bagged and taken to a 40-yard dumpster. The federation coordinated the placement of the dumpster with Waste Removal LLC at a local marina in Swansboro. The work crew fills the dumpster at the end of each work day and calls for the debris to be carried to the landfill once full.

In the Coastal Federation's South East region, a 4-person crew started April 30. The crew began in the lower New River and are currently working in Stump Sound. The crew has covered 22 miles of shoreline including islands, embankments and creeks. They completed a preliminary clean-up of the shoreline (3 miles) of the Permuda Island Coastal Reserve. The majority of their work has been in Onslow County. As of June 30, the crew had picked up 48.2 tons.

Approximately 3-5 tons of this debris was removed from within the Permuda Island Coastal Reserve. All of this work has been done by hand. The crew should conclude their work between August 8 and August 16.

Phase II:

A local marine contractor used barges, dumpsters, excavator and other equipment to pick up and remove the larger and much heavier marine debris. This contractor focused on navigational hazards in waterways, chemically-treated wood debris on publicly-owned islands and shorelines as well as several abandoned boats. This phase of the cleanup began April 15 and finished June 13. The crew removed 112.7 tons (225,360 pounds) of wooden dock debris, pilings, railings, benches, and 3 abandoned vessels from Hurricane Florence. The crew consisted of an excavator operator, barge operator, and 4-9 person ground crew depending on site. The crew covered 21 miles along the Atlantic Intracoastal Waterway from marker 34-55 including Huggin's Island, which is part of Hammocks Beach State Park.

The federation has also been working with volunteers to educate about the project and involve them in the cleanup process. Since early February, the federation has organized six volunteer groups to remove 3,685 pounds of debris. Volunteers work for approximately 2 hours at each site.

- On February 9, a group of seven volunteers from the Leadership Carteret class of the Carteret County Chamber of Commerce, a group of business professionals, removed 380 pounds of marine debris off a dredge spoil island directly across from the Cedar Point Wildlife Boat Ramp.
- On February 12, seven community volunteers participated in a shoreline cleanup at the Hoop Pole Creek Nature Preserve in Atlantic Beach. They collected 940 pounds of debris during this event.
- On March 4, nine East Carolina University students participated in a shoreline cleanup at the Hoop Pole Creek Nature Preserve, as part of their alternative spring break program. The students removed 385 pounds of marine debris from the site.
- On April 12, twenty volunteers participated in a shoreline cleanup at Ward's Creek. They collected 1,400 pounds of debris during the event.
- On May 14, after a living shoreline planting event in Morehead City, 17 volunteers collected 300 pounds of debris from the shoreline.
- On June 12, 16 volunteers participated in a shoreline cleanup on Jones Island. They collected 280 pounds of debris during the event.

The total amount of marine debris removed as of July 24 by both the work crew and volunteers is 174.8 tons. The total funds spent on this project to date is \$400,000.

Above is the history of activity.
No recent activity for this reporting period.

Contact

Rachael Carlyle, NC Coastal Federation
(252) 393-8185 x102
rachaelc@nccoast.orG

10. Grants for Environmental Infrastructure

SL 2016-124, 4.1(9)

The intended purpose of this program was to aid businesses and individuals who suffered financial loss due to impacts of Hurricane Matthew (primarily flooding related) to underground storage tank (UST) systems.

Responsible Department and Agency

Department of Environmental Quality, Division of Waste Management

Funding Allocation Update

	Total	SL 2016-124 4.1(9)
Appropriated	\$650,000.00	
Expended	\$595,680.49	
Obligated	\$ 54,319.51	
Unobligated Balance	\$0	

Summary of Activities

- Nineteen applications received totaling \$685,640 in requested reimbursements.
- Applicants include twelve petroleum business facilities, three school facilities, three private residences, and one municipal utility system
- Nineteen (19) applications have been approved and paid totaling approximately \$595,680
- Work has been fully completed at all sites. (Four applications containing costs not related to petroleum USTs have been wholly or partially denied.)
- The final payment from the program (for Robeson County Board of Education) was approved and processed on 8/1/19. Final payment was made on 8/6/19. This closes out DWM's projects funded by Hurricane Matthew disaster funds.

Performance Metrics

- Average Time for Project Delivery by Program

- Average number of days from application to fund distribution
 - 21 days after submittal of all required documentation.
- Average number of days from fund distribution to project commencement
 - The program was designed as a reimbursement program, not one by which DWM awarded grants or contracted directly for work required.
- Average number of days from project commencement to project completion
 - The time required and the project schedules varied greatly and were not controlled by DWM. (Some projects were already completed and seeking reimbursement. Others required multi-month work scopes with phased reimbursements as work was documented complete.)
- Amount and % spent/obligated on administrative activities by Program.
 - DWM treated the program as an additional duty and did not expend any grant monies for administrative activities.
- Amount and % spent/obligated on behalf of recipients by Program.
 - DWM spent 91.64% of the program award to reimburse claimants. 8.36% of the program award was to be released for use by other agencies after 8/16/19.

Recent Activities for Current Reporting Period (October – December 2021)

The projects funded through this program are all completed; no activity since 8/16/19.

Contact

Vance Jackson

919-707-8262 (O)

919-538-2830 (C)

vance.jackson@ncdenr.gov

11. Various Projects within DEQ – Division of Waste Management

SL 2019-224 2.1 (3)

The intended purpose of this program was to aid businesses and individuals who suffered financial loss due to impacts of Hurricanes Florence, Michael, or Dorian (primarily flooding related) to underground storage tank (UST) systems.

Responsible Department and Agency

Department of Environmental Quality, Division of Waste Management

Funding Allocation Update

	Total SL 2019-224 2.1 (3)
Appropriated	\$1,021,095.00
Expended	\$ 585,587.26
Obligated	\$
Unobligated Balance	\$ 435,507.74

Summary of Activities

Damage Claims

- Received reimbursement claims for UST system damage from twenty-eight (28) facilities.
- Processed and reviewed twenty-eight (28) packages totaling \$513,593.76
- Approved or partially approved twenty-eight (26) claims totaling \$272,734.95 (Spreadsheet included separately.)
- One claim denied in total
- Claim acceptance period remains open
- Re-contacted facilities determined by the UST Section as having potential storm related attributable to storm damage; encouraged facilities to complete and submit reimbursement claims for designated storm events.
- No new claims were submitted during July 2021 – December 2021.
- No funds currently obligated for damage reimbursement.

Resiliency

The grant has also been utilized for temporary staff to identify and catalog at-risk ASTs and noncommercial USTs statewide by using aerial imagery and ground reconnaissance. These unregulated tanks represent potential sources of petroleum releases associated with potential flooding.

- 43,811 unregulated tanks identified to date.
- Four temporary staff continue to complete reconnaissance, ground-truthing, and GIS documentation.

Performance Metrics

- Average Time for Project Delivery by Program
 - Average less than 30 days from application to fund distribution
 - Given the time lapse in program authorization, this program is designed to provide reimbursement for testing and repairs already completed by UST owners/operators.

- The percentages of total funding expended to individual activities are not an appropriate measure of efficiency since the Program extended the deadline to receive claims.

Recent Activities for Current Reporting Period (October – December 2021)

Facilities have been slow to respond to contacts and submit claims. We believe this is due to the time elapsed between the storm events and authorization of the Program.

Owners/operators appear to be reticent to put together the documentation, including invoices and payment verification necessary for reimbursement. We have renewed efforts to encourage them to submit claims to assist with their recovery.

Final extension of claim deadline was posted, followed by re-contact of identified facilities that have not yet replied.

Resiliency activities will continue throughout FY 21-22.

Contact

Vance Jackson

919-707-8262

vance.jackson@ncdenr.gov

12. Coastal Beach and Dredging Needs Assessment

SL 2018-136 6.1 (18)

Funds were used to compensate municipalities for surveys of beaches and channels completed because of hurricane related damage. Additionally, these funds will be used to conduct an analysis of dredge material placement sites in support of an overall statewide coastal dredged material management plan (DMMP).

Responsible Department and Agency

Department of Environmental Quality, Division of Water Resources

Funding Allocation Update

	Total SL 2018-136 6.1 (18)
Appropriated	\$2,000,000.00
Expended	\$ 351,805.00
Obligated	\$ 0.00
Unobligated Balance	\$1,648,195.00

Summary of Activities

- a. Surveys have been completed and funds have been distributed as follows:
 - Bald head Island \$54,907.14,
 - Oak Island \$63,549.00,
 - Kill Devil Hills \$12,047.54,
 - Holden Beach \$21,264.00,
 - Dare County \$1,400.00,
 - Bogue Banks \$126,800.00, and
 - North Topsail \$71,838.32.
- b. A Scope of Work has been drafted in cooperation with the USACE, DWR, and DCM for submittal for the development of a DMMP. The State of North Carolina and the U.S. Army Corps of Engineers (USACE) are partnering, under Section 22 – Planning Assistance to States (PAS) under the “comprehensive plan” category, to conduct analysis of dredge material placement sites. The Phase 1 of the project will be a 50/50 cost share with \$133,000.00 in State funds to complete Phase 1.
- c. The DMMP PAS has been signed by the state and USACE and the funds have been disbursed to the USACE.
- d. The USACE has begun to reach out to local stakeholders to determine their dredging and dredge spoil site needs along the Intercoastal Waterway.
- e. The USACE has begun to contact property owners of existing potential spoil sites along the Intercoastal waterway.

Performance Metrics

- Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution: 120 days: The applications were completed on 3/31/19 and all survey funds were distributed by 11/18/2019. However, most of the project funds were distributed within four months of receiving applications.
 - Average number of days from fund distribution to project commencement: Not applicable: Funds were distributed by 11/18/2020 but municipalities were being reimbursed for projects already completed.
 - Average number of days from project commencement to project completion: Not applicable: the project commencement dates are not available because the projects were completed at the date of fund disbursement.
- Amount and % spent/obligated on administrative activities by Program. Not applicable.
- Amount and % spent/obligated on behalf of recipients by Program. Not applicable.

Recent Activities for Current Reporting Period (October - December 2021)


DWR has partnered with USACE through the Planning Assistance to States (PAS) program in which USACE provided a 50% match of \$133,000 to complete the Dredge Material Management Plan (DMMP). A scope of work for the DMMP was approved by the USACE Planning and Environmental Branch. The agreement between the state and USACE has been finalized and a payment has been provided to the USACE. The USACE has begun development of the database, contacting stakeholders along the ICWW to obtain dredging needs, and contacting potential spoil site property owners. The State and USACE have begun discussions to develop the scope of work for Phase 2 of the DMMP to determine dredging needs over the next 20 years. Although pictures cannot be provided of a final product some preliminary images of the location of the marinas and numbers of marina contacted by the USACE staff are attached.

Contact

Kevin Hart

919-707-3607

Kevin.Hart@ncdenr.gov

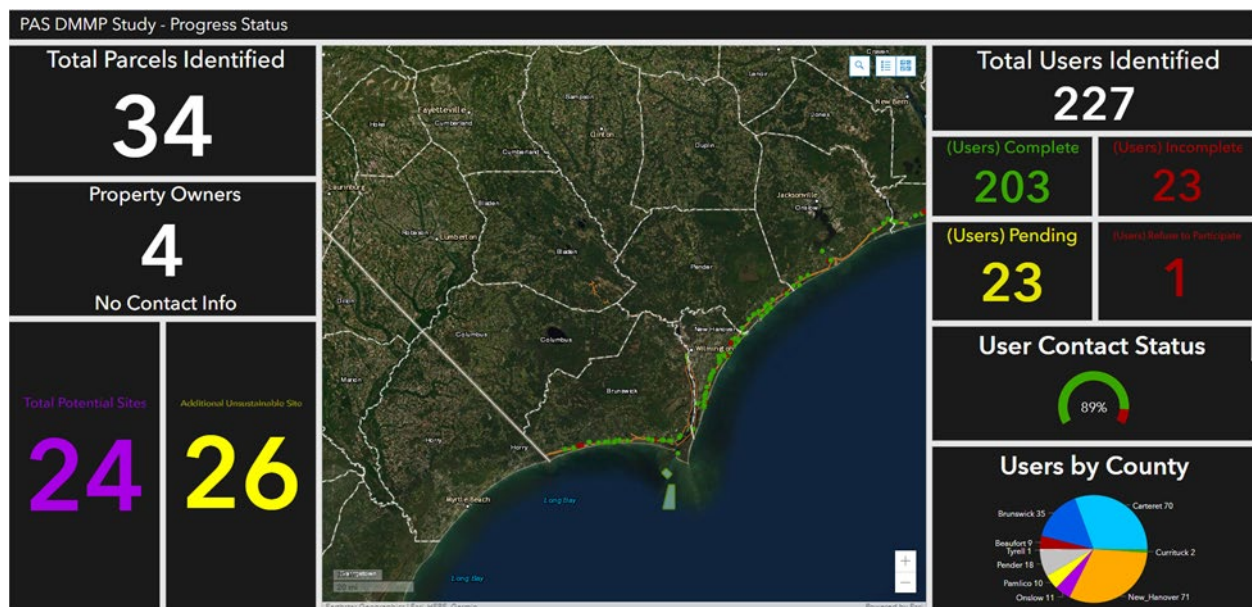

13. Coastal Storm Damage Mitigation (Oak Island and Bogue Banks)

SL 2018-138 1.3 (8)

The funds allocated for Coastal Storm Damage Mitigation may be used to provide no more than fifty percent (50%) of the total cost of an eligible project. These projects provided 18.5 million in funds help rebuild coastal communities and to mitigate or remediate coastal storm damage to the ocean beaches and dune systems of the state.

Responsible Department and Agency

Department of Environmental Quality, Division of Water Resources

Funding Allocation Update

Appropriated	\$18,500,000
Expended	\$18,500,000
Obligated	\$0.00
Unobligated Balance	\$0.00

Summary of Activities

- a. Applications were submitted by Oak Island and Bogue Banks for appropriated funds on December 6, 2019 as a requirement for updated language in Session Law 2019-241.
- b. A payment request form was submitted for Bogue Banks on March 23, 2020 and for Oak Island on April 1, 2020. Disbursement of funds were completed for Bogue Banks on April 15, 2020 and Oak Island on April 29, 2020

Performance Metrics

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution: 129 days: The applications were completed on December 6, 2019 and the funds were distributed by April 29, 2020.
 - o Average number of days from fund distribution to project commencement: 180 days: Funds were distributed on April 1, 2020 and the projects have either already started or will begin within a few months of receipt of funds.
 - o Average number of days from project commencement to project completion: 730 days: Projects are typically two-year projects.
- b. Amount and % spent/obligated on administrative activities by Program. Not applicable.
- c. Amount and % spent/obligated on behalf of recipients by Program. Not applicable.

Recent Activities for Current Reporting Period (October – December 2021)

No activity for this reporting period. All funds have been distributed from SL 2018-138 1.3 (8).

Contact

Kevin Hart

919-707-3607

Kevin.Hart@ncdenr.gov

14. Various Projects within DEQ – Coastal Storm Damage Mitigation Fund

SL 2019-224 2.1 (3)

The funding comes from Session Law 2019-224 which allocated \$11.5 million to the Division of Water Resources' Coastal Storm Damage Mitigation Fund. Funding may only be used for costs associated with beach nourishment, artificial dunes, and other projects to mitigate or remediate coastal storm damage to the ocean beaches and dune systems of the State.

Responsible Department and Agency

Department of Environmental Quality, Division of Water Resources

Funding Allocation Update

	Total	SL 2019-224 2.1 (3)
Appropriated	\$11,500,000.00	
Expended	\$ 7,275,258.94	
Obligated	\$ 4,224,741.06	
Unobligated Balance	\$0	

Summary of Activities

- Program guidelines and applications were developed to provide to coastal communities.
- Guidelines and applications were sent to coastal communities on February 28, 2020.
- A press release was sent on March 3, 2020, to announce the funding opportunity.
- Applications were accepted until April 30, 2020.
- A committee was formed to review applications.
- Applications were reviewed, and award letters were distributed.
- Contracts have been executed for all the projects.
- Partial payments have been distributed for 9 projects.

Performance Metrics

- Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution: to be determined.
 - Average number of days from fund distribution to project commencement: to be determined.
 - Average number of days from project commencement to project completion: to be determined.

- Amount and % spent/obligated on administrative activities by Program. Not applicable.
- Amount and % spent/obligated on behalf of recipients by Program. Not applicable.

Recent Activities for Current Reporting Period (October 2021- December 2021)

Nine Local governments were notified of their award amounts and provided the information required to execute a contract so funds can be disbursed. Contracts for all 9 projects have been finalized and funds are being dispersed on a quarterly basis. Quarterly payments to all of the projects have been distributed to the local governments as of January 6, 2022. The following list shows the nine awarded projects, total awarded funds, and distributed funds (as of Dec 2021).

Project	Funds Distributed (as of Dec 2021)	Award total
Town of Holden Beach	\$106,000.00	\$106,000.00
Town of Oak Island	\$336,058.99	\$1,344,235.96
Town of Surf City	\$1,024,179.78	\$1,365,573.03
Town of Southern Shores	\$1,056,185.44	\$1,408,247.19
Town of Nags Head	\$704,123.60	\$1,408,247.19
Town of Kitty Hawk	\$704,123.69	\$1,408,247.19
Town of Duck	\$1,088,191.10	\$1,450,921.35
Town of Kill Devil Hills	\$1,088,191.10	\$1,450,921.35
County of Dare Buxton	\$1,130,865.49	\$1,557,606.74
	\$7,275,258.94	\$11,500,000.00

Contact

Kevin Hart

919-707-3607

Kevin.Hart@ncdenr.gov

15. Various Projects within DEQ (FerryMon)

SL 2019-224 2.1 (3)

FerryMon provides long-term and real-time water quality data for the Neuse River estuary and Pamlico Sound. The data are used to evaluate the impacts of tropical storms and hurricanes, and to examine the relationships between nutrients, chlorophyll *a*, and algae. The project goal is to support long-term fisheries and recreational use of the Albemarle-Pamlico Estuarine System. The FerryMon web page is located here:

<http://paerllab.web.unc.edu/projects/ferrymon/>.

Responsible Department and Agency

Department of Environmental Quality, Division of Water Resources (DWR)

Funding Allocation Update

Appropriated	\$175,000
Expended	\$175,000
Obligated	\$0.00
Unobligated Balance	\$0.00

Summary of Activities

- a. 2019-2020 funding directed to University of North Carolina to accomplish project goals.
- b. Continuous water quality data collected via NCDOT ferries.
- c. Data provided to DEQ Division of Water Resources and Division of Marine Fisheries.

Performance Metrics

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution: 33 days: Task order completed December 11, 2019 and the funds were distributed on January 14, 2020.
 - o Average number of days from fund distribution to project commencement: 0 days: Funds were distributed on January 14, 2020 and the project started on January 14, 2020.
 - o Average number of days from project commencement to project completion: This project is ongoing with no projected completion date.
- b. Amount and % spent/obligated on administrative activities by Program: Not applicable.
- c. Amount and % spent/obligated on behalf of recipients by Program: Not applicable.

Recent Activities for Current Reporting Period (October - December 2021)

FerryMon Directed Grant funds are being distributed by DWR and the project is being completed by the University of North Carolina at Chapel Hill's Institute of Marine Sciences. Hans Paerl, PhD, is the principal investigator for the project.

Contact (DWR): Tammy L. Hill, Environmental Specialist II, 919-743-8412,
Tammy.L.Hill@ncdenr.gov

16. Various Projects within DEQ (Surry County)

SL 2019-224 2.1 (3)

The North Carolina General Assembly appropriated funds to the Department of Environmental Quality (DEQ) to assist Surry County with the construction of three stream stabilization projects. The law appropriating these funds, Session Law 2019-224 (The Disaster Recovery Act) requires the Department to make quarterly reports on disbursements for this purpose. Attached are reports covering the fourth and final quarter of FY 2020-2021.

Responsible Department and Agency

Department of Environmental Quality, Division of Water Resources

Funding Allocation Update

	Total	SL 2019-224 2.1 (3)
Appropriated		\$3,000,000
Expended		\$3,000,000
Obligated		\$0.00
Unobligated Balance		\$0.00

Summary of Activities

- Final quarterly funds disbursement was verified in the NC Accounting System (NCAS). The final recurring payment for Big Elkin Creek was made on 4/29/21. No further recurring payments are scheduled for these projects.
- Big Elkin Creek has been completed and Mitchell River construction will begin in August.
- Cedar (Camp) Creek, the third project, is currently in Dam Safety permit review.

Performance Metrics

- Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution: 112 days. The applications were completed on 12/30/2019 and 1/8/2020 and the quarterly disbursement of funds began on 4/22/2020.
 - Average number of days from fund distribution to project commencement: 14. Quarterly disbursement of funds began on 4/22/2020 and the projects are underway.

- Average number of days from project commencement to project completion:
730 days: Projects generally take at least two years to complete.
- Amount and % spent/obligated on administrative activities by Program. Not applicable.
- Amount and % spent/obligated on behalf of recipients by Program. Not applicable.

Recent Activities for Current Reporting Period (October - December 2021)

The State & Local Projects section (S&L) of the Water Resources Development Grant Program (WRDG) has conducted several program and contract administration activities during the current reporting period. Below is an overview of recent activities and accomplishments:

- Conducted final QA/QC of database information for active and completed grants since 2016.
- Coordinated launch of [Featured Projects](#) portion of WRDG website with DEQ's Digital Strategist which takes viewers to the WRDG Featured Projects Collective. This collective is a set of interactive, visually appealing summaries of the five types of State & Local projects that the WRDG provides funding for.
- Prepared, compiled, and submitted online application review materials for 21 Fall 2020 projects for S&L grant review team.
- Completed formal interagency review process and grant award notification to local government grantees for 21 Fall 2020 applications received.
- Completed contract and requisition request process for 11 Fall 2020 projects that were recommended for funding.
- Conducted grant close-out site activities for 11 projects that were completed during this reporting period. These projects have provided environmental, economic, social and regional benefits to the communities in which these projects were completed.
- Processed 13 reimbursement payments for local government grantees.

Contact

Amin Davis
State & Local Projects Manager
Water Resources Development Grant Program
919-707-9132
Amin.Davis@ncdenr.gov

17. Grants for Environmental Infrastructure

SL 2016-124 4.1 (9)

Funding (grants) for disaster-related infrastructure for water and wastewater utilities.

Responsible Department and Agency

Department of Environmental Quality, Division of Water Infrastructure

Funding Allocation Update

	Total SL 2016-124 4.1 (9)
Appropriated	\$5,470,209
Expended	\$3,668,619
Obligated	\$1,801,590
Unobligated Balance	\$0

Summary of Activities

Projects include:

- Pump station improvements to make water or sewer infrastructure more resilient to flooding
- Rehabilitating or replacing existing gravity sewer to minimize impacts to capacity from storm water or groundwater getting into the system
- Moving a municipal drinking water well out of the flood plain

Performance Metrics

- Average Time for Project Delivery by Program
 - Average number of days from receipt of payment application to fund distribution is seven working days when all required documentation is submitted.
 - Average number of days from project commencement to project completion varies by project. Most of the construction projects have been impacted by subsequent hurricanes and COVID-19.
- None of the funding has been spent/obligated on administrative activities by Program.
- All of the funding has been spent/obligated on behalf of recipients by Program.

Recent Activities for Current Reporting Period (October - December 2021)

Completed projects include Dublin, Elizabeth City, Enfield, Fair Bluff (wastewater), and Neuse Regional WSA. No updates available for Benson. For the Fair Bluff drinking water well project, Engineering Design is approximately 65% complete and hydraulic modeling services are approximately 90% complete. For Wadesboro, the Bid and Design package was approved, bids have been solicited, received, and opened, and the responsive low bidder

was awarded the construction contract.

Applicant Name	Project Name	State Grant Disaster Recovery (SL. 2016-124 4.1(9))	Expended
Benson, Town of	Main Street Sewer Rehabilitation	\$875,000	\$815,316
Dublin, Town of *closed*	Lyons Landing Lift Station Rehabilitation	\$107,532	\$107,532
Elizabeth City, Town of *closed*	Herrington Road Gravity Sewer Replacement	\$995,000	\$995,000
Enfield, Town of *closed*	Raw Water Pump Station Improvements	\$99,785	\$99,785
Fair Bluff, Town of *closed*	Pump Station Flood Resiliency Improvements	\$1,341,553	\$1,341,553
Fair Bluff, Town of	Relocation of Drinking Water Well #2	\$1,031,409	\$160,672
Neuse Regional WSA *closed*	NRWSA Pump Station Improvements	\$19,930	\$19,930
Wadesboro, Town of	Burns Street Basin Sewer Rehabilitation	\$1,000,000	\$128,831
Total		\$5,470,209	\$3,668,619

Contact

Jon Risgaard, SRF Section Chief

Division of Water Infrastructure

Jon.Risgaard@ncdenr.gov; 919-707-9174

18. Various Projects within DEQ – Water Infrastructure

SL 2019-224, 2.1(3)

Funding (grants) for disaster related infrastructure for water and wastewater utilities.

Responsible Department and Agency

Department of Environmental Quality, Division of Water Infrastructure

Funding Allocation Update

	Total	SL 2019-224 2.1(3)
Appropriated	\$3,142,231	
Expended	\$0.00	
Obligated	\$3,142,231	
Unobligated Balance	\$0.00	

Summary of Activities

This funding will supplement federal funding provided for disaster-related water infrastructure projects through the state revolving funds (SRF) programs. These state grants will be targeted to smaller, rural utilities which will relieve the recipients from federal requirements under the SRF programs. Funding Applications were accepted, and awards made concurrently (applications received April 30, 2020 and awarded July 8, 2020) with the SRF funds (SL 2019-250).

Performance Metrics

- Applications received and funding awarded (completed)
- Disbursements

Recent Activities for Current Reporting Period (October – December 2021)

Reporting metric per S.L. 2019-250

- The average number of days from application to fund distribution, project commencement, and project completion, where applicable and practicable.
- Average cost per project, by county where practicable. *See table below, average project cost*
= \$1,133,667
- Amount and percentage of disaster recovery funds spent on administrative activities.
\$0, 0%
- Amount and percentage of disaster recovery funds obligated for administrative activities.
\$0, 0%
- Amount and percentage of disaster recovery funds disbursed on behalf of recipients.
\$0, 0%
- Amount and percentage of disaster recovery funds obligated on behalf of recipients.
\$0, 0%
- Number of individuals, households, entities, or other unit served, by county

where practicable: Data *not tracked*. *Projects support entire community*.

The following table shows the projects awarded funding for disaster related infrastructure funds per SL 2019-224 2.1(3).

Projects awarded funding through SL.
2019-224 2.1(3)

Applicant	Project Description	Funding Requested	Award Date	State Grant Disaster Relief (SL. 2019-224 2.1(3))	State Reserve Grant	State Reserve Loan
Tabor City, Town of	Gore Street Pump Station Relocation and Flood Protection	\$1,543,000	July 8, 2020	\$1,543,000		
Trenton, Town of	2020 WWTP Operations Building Relocation	\$955,000	July 8, 2020	\$955,000		
Dublin, Town of	Sewer Outfall Replacement	\$903,000	July 8, 2020	\$644,231	\$33,019	\$225,750
		Total		\$3,142,231	\$33,019	\$225,750

Projects have two years to enter a construction contract based on NCGS 159G-41. The program provides payments based on invoices of incurred expenses.

Contact

Jon Risgaard, SRF Section
Chief Division of Water
Infrastructure
Jon.Risgaard@ncdenr.gov 919-707-9174

19. State Match for ASADRA

SL 2019-250 1.1(3)

Funding provided under SL 2019-250 1.1(3) provides state match (total of approximately \$17.5 million) for state revolving fund (SRF) programs that leverages over \$87 million in federal funding under the federal Additional Supplemental Appropriations for Disaster Relief Act (ASADRA). ASADRA provides funding for wastewater treatment works and drinking water facilities impacted by Hurricanes Florence and Michael.

Responsible Department and Agency

Funding Allocation Update

Total SL 2019-250 1.1(3)

Appropriated	\$17,600,000
Expended	\$0.00
Obligated	\$0.00
Unobligated Balance	\$17,600,000

Summary of Activities

Intended Use Plan (IUP) for EPA grant application finalized.

Applications were accepted in April 2020 and funds awarded on July 8, 2020 for a first round of ASADRA funding. A second round of ASADRA funding was held last fall for eligible projects identified during the spring 2020 application round. Complete applications were due September 30, and funds were awarded February 10, 2021.

Once project funding is awarded, projects have two years to enter a construction contract pursuant to NCGS 159G-41. The program provides payments based on invoices of incurred expenses.

Performance Metrics

- Applications received and awarded (2 funding rounds competed July 8, 2020, and February 10, 2021)
- Disbursements

Recent Activities for Current Reporting Period (October – December 2021)

Reporting metric per S.L. 2019-250

- The average number of days from application to fund distribution, project commencement, and project completion, where applicable and practicable.
- Average cost per project, by county where practicable. *See table below, average funding provided per project = \$4,789,300*
- Amount and percentage of disaster recovery funds spent on administrative activities. *\$0, 0%*
- Amount and percentage of disaster recovery funds obligated for administrative activities. *\$0, 0%*
- Amount and percentage of disaster recovery funds disbursed on behalf of recipients. *\$0, 0%*

- Amount and percentage of disaster recovery funds obligated on behalf of recipients.
\$0, 0%
- Number of individuals, households, entities, or other unit served, by county where practicable: Data *not tracked*. Projects support entire community.
-

The remaining ASADRA funds were awarded as part of the September 2020 funding cycle in February 2021. Projects are starting to submit engineering reports for review and approval. Terms and conditions of the ASADRA fund loan will not be established until the project has completed both engineering review, plans and specification review, and a contract has been awarded.

Drinking Water ASADRA Funding Obligations

Applicant Name	Project Name	Amount of Funding Requested	Principal Forgiveness	Loan
Scott's Hill Water and Sewer District	Elevated Water Tank and Associated Improvements	\$7,940,000	\$1,985,000	\$5,955,000
Rocky Point Topsail Water and Sewer District	RO Water Treatment Plant and Associated Improvements	\$66,870,000	\$5,000,000	\$15,000,000
River Bend, Town of	Water Meter Replacement - ASADRA	\$602,500	\$602,500	
Washington, City of	WTP Emergency Generator	\$409,160	\$102,290	\$306,870
Lumberton, City of	2020 Well Replacement	\$2,316,900	\$2,316,900	
Dunn, City of	Raw Water Electrical Relocation and 24" Line Replacement	\$3,515,000	\$878,750	\$2,636,250
Surf City, Town of	Water System Resiliency Projects	\$2,805,000	\$701,250	\$2,103,750
Johnston County	2022 AC Water Main Replacement	\$5,242,800		\$5,242,800
Reidsville, City of	Redundant Water Supply Line	\$4,654,000	\$1,000,000	\$3,654,000
Elm City, Town of	Water Filtration and Emergency Backup Generation	\$1,989,086	\$497,272	\$1,491,815
Lincoln County	St. James Water Line	\$3,070,581		\$3,070,581

Totals for ASADRA Drinking Water Projects	\$13,083,961	\$39,461,065
	\$52,545,026	

Wastewater ASADRA Funding Obligations

Applicant Name	Project Name	Amount of Funding Requested	Principal Forgiveness	Loan
Yadkin Valley Sewer Authority	2020 Collection System Rehabilitation - Part I (Pipeline Rehab)	\$670,000	\$502,500	\$167,500
Liberty, Town of	Liberty Collection System Improvements	\$3,000,000	\$3,000,000	
Pollocksville	2020 WWTP Facilities Relocation	\$3,000,000	\$3,000,000	
Graham, City of	Graham WWTP Improvements Project	\$30,694,000		\$23,000,000
Clinton, City of	Clinton WWTP Resiliency Improvements	\$3,000,000	\$3,000,000	
St. Pauls, Town of	Wastewater Treatment Plant Relocation	\$6,093,450	\$2,700,000	\$2,893,450
Southern Pines, Town of	Warrior Woods Pump Station Relocation	\$2,998,000		\$2,998,000
Sparta, Town of	Wastewater Interceptor Project	\$1,268,000		\$1,268,000
Goldsboro, City of	Little Cherry Big Cherry Pump Station Relocation Out of Floodplain	\$3,058,000		\$3,058,000
Eden, City of	Contracts IIB and V - Junction Pump Station Rehab & Smith River Replacement and Rehab and Siphon Replacement	\$7,158,982		\$5,042,373
Tryon, Town of	Braewick Road Sewer Rehabilitation Project	\$2,189,950	\$1,000,000	\$1,189,950
Totals for ASADRA Wastewater Projects			\$13,202,500	\$39,617,273
			\$52,819,773	

Contact

Jon Risgaard, SRF Section

Chief Division of Water

Infrastructure

Jon.Risgaard@ncdenr.gov 919-707-9174

Department of Health and Human Services

1. Disaster Supplemental Nutrition Program (D-SNAP)

SL 2018-136 Subsection 5.4

The intended purpose of the Disaster Supplemental Nutrition Program (D-SNAP) is to provide funding to assist counties in matching federal funds for the administrative expenses incurred by local departments of social services in operating D-SNAP, a program to provide food assistance to low-income households with food loss or damages caused by Hurricane Florence. The funding will fulfill this purpose by offsetting county staffing costs and other expenditures related to D-SNAP operations in declared counties and offsetting expenses incurred by other counties that assisted affected counties, thereby ensuring D-SNAP operations were successful.

Responsible Department and Agency

Department of Health and Human Services, Division of Social Services

Funding Allocation Update

Appropriated	\$3,500,000
Expended	\$2,325,628
Obligated	\$0
Unobligated Balance	\$1,174,372

Summary of Activities

- a. 34 declared disaster counties and 8 helper counties were provided match funding which alleviated an additional financial burden to the declared counties during hurricane recovery.
- b. Certification periods for existing SNAP recipients in the 34 impacted counties were extended six months to ensure there was no disruption in ongoing SNAP benefits.
- c. After providing shelter operations during the storm, county departments of social services staff immediately transitioned to implementing the DSNAP for eight days during which they helped over one million people have access to food during the DSNAP period.

Performance Metrics

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution
 - DSNAP applications are typically processed within three days of the date of application (exception is if all information is not available)

- The benefits are available to the applicants the day following the application is approved.
 - Average number of days from fund distribution to project commencement
 - Since DSNAP is a reimbursement program no funds are received prior to project commencement
 - Average number of days from project commencement to project completion
 - DSNAP application period was for 8 days in each affected county. There were several phases for the different counties. The first phase began on September 28, 2018 and the final phase ended on November 9, 2018.
- b. Amount and % spent/obligated on administrative activities by Program:
\$2,250,775.10 - 100%
Therefore 100% of these funds were spent on behalf of recipients.
- c. Amount and % spent/obligated on behalf of recipients by Program
\$0 – 0%

Recent Activities for Current Reporting Period (October - December 2021)

No new activities for this reporting period.

Certification periods for existing SNAP recipients in the 34 impacted counties were extended six months to ensure there was no disruption in ongoing SNAP benefits. This also allowed county departments of social services offices to focus on recovery and ongoing assistance for families affected by the storm. DSNAP is now over and the program has ended. No further update.

Contact: Richard Stegenga 919-527-6337 Richard.Stegenga@dhhs.nc.gov

2. Emergency Prescription Assistance Program (EPAP)

SL 2018-136, and 6.1 (17)

This federally authorized program is to provide emergency medical care to individuals affected by public health emergencies and catastrophic events that overwhelm the response capacity of state and local emergency medical systems. EPAP is activated as a cost-sharing program. The state requesting EPAP activation submits to FEMA a Mission Assignment request for EPAP activation and agree to pay 25% of the total cost for EPAP activation.

Responsible Department and Agency

Department of Health and Human Services (DHHS)

At the time North Carolina secured match funding, FEMA stated that it was more than 30 days post event and the program design is to assist with immediate prescription assistance and medical equipment needs due to loss or displacement primarily during the first 30 days. North Carolina was not able to demonstrate a need to FEMA for them to turn on the EPAP. FEMA views the EPAP as a program for immediately after the disaster in the impacted areas before they are set up and to provide assistance. After about two weeks, when FEMA is up and helping in all the areas, they use their other public assistance programs as opposed to the EPAP.

Funding Allocation Update

Appropriated	\$1,000,000
Expended	0
Obligated	0
Unobligated Balance	\$1,000,000

Performance Metrics

Since this program was not activated there are no performance metrics.

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution
 - o Average number of days from fund distribution to project commencement
 - o Average number of days from project commencement to project completion
- b. Amount and % spent/obligated on administrative activities by Program.
- c. Amount and % spent/obligated on behalf of recipients by Program.

Summary of Activities

Program not activated.

Recent Activities for Current Reporting Period (October - December 2021)

Program not activated. No other update.

Contact

Amanda Fuller Moore, 919-707-5299 amanda.fullermoore@dhhs.nc.gov

Department of Insurance

3. Infrastructure Repairs

SL 2016-124 4.1 (11)

SL 2018-136 6.1 (26)

The purpose of this program was to provide grants to Volunteer Fire Departments for repairs of damages caused by Hurricane Matthew, the wildfires in the western part of the state, and Tropical Storms Julia and Hermine that were not covered by federal assistance or by the proceeds of insurance policies.

Volunteer Fire Departments Infrastructure Repairs SL 2018-136 6.1 (4) – The purpose of this program was to provide grants to Volunteer Fire Departments for repairs of damages caused by Hurricane Florence that were not covered by federal assistance or by the proceeds of insurance policies.

Responsible Department and Agency

Department of Insurance – Office of the State Fire Marshal

Funding Allocation Update

Appropriated	\$1,000,000
Expended	\$326,387
Obligated	\$0.00
Unobligated Balance	\$673,613

Summary of Activities

Nine grants have been awarded and paid totaling \$326,387 for infrastructure repairs in Craven, Carteret County, Duplin County, Pamlico County, Transylvania, Wilson, Wayne and Beaufort counties.

Recent Activities for Current Reporting Period (October – December 2021)

There was no activity for the current reporting period.

Contact

Darlene Langston, (919) 807-6036, darlene.langston@ncdoi.gov

Department of Public Instruction

1. School Nutrition Employee Compensation

SL 2018-134, subsection 4.1(1)

Session law provided financial accommodations for extraordinary circumstances due to Hurricane Florence. Federal cash reimbursement for nutritious meals served to students as part of the instructional day accounts for the majority of revenues required to operate the school nutrition programs in local education agencies (LEAs) in NC. When unanticipated school closures prevent meal service to students, there is no basis for LEAs to claim cash reimbursement payments. LEAs rely on the reimbursement of Federal School Nutrition funds to support the local operation of their School Nutrition Programs. Without Federal cash reimbursements for meals served, there are no State or local funds to support the salaries/benefits of School Nutrition personnel. These funds were used to compensate School Nutrition employees who would have otherwise not been compensated.

2. Capital Recovery Funds

SL 2018-136, subsection 6.1.(6), SL 2018-138 subsections 1.3(1) and 1.3(2)

Session law provided an appropriation to support immediate disaster recovery efforts for the repair and renovation of facilities and the repair and/or replacement damaged furnishings and equipment as a result of the damage caused by Hurricane Florence in Local Administrative Agencies (LEAs). Documentation was required to substantiate the issuance of funds. All LEAs were required to take reasonable steps to obtain alternative funds to cover damages; where insurance funds or alternative funds were recovered, LEAs are required to return the recovered funds to the appropriate funding source.

3. Disaster Relief and Resiliency

SL 2019-250, subsection 1.2(7)

Session law provided \$1,700,000 to the Department of Public Instruction as a directed grant to Hyde County for repairs to the Ocracoke School necessitated by Hurricane Dorian. These funds were transferred in full to Hyde County.

Responsible Department and Agency

North Carolina Department of Public Instruction, Offices of the Superintendent, Chief of Staff, Chief Financial Officer, Chief School Business Officer and Divisions of School Nutrition and District Operations.

Funding Allocation Update

	Total	SL 2018-134	SL 2018-136	SL 2018-138	SL 2019-250
Appropriated	\$ 6,500,000	\$ 60,000,000	\$ 25,000,000	\$ 1,700,000	
Expended	\$ 5,114,330	\$ 59,992,012	\$ 24,322,770	\$ 1,700,000	
Obligated	\$ 0	\$ 0	\$ 0	\$ 0	
Unobligated Balance	\$ * 0	\$ 7,987	\$ 677,230	\$ 0	

* Unobligated funds totaling \$1,385,670 reverted to the general fund as of 6/30/2019.

Summary of Activities

Funds were distributed to Local Education Agencies (LEAs) expeditiously as directed by the Superintendent in order to return students to school safely and quickly.

- a. Funds were issued to LEAs based upon written documentation to include estimates (bids, proposals or quotes), actual invoices and other artifacts to substantiate the catastrophic nature of the requests for funding.
- b. The Department has maintained documentation to support the distribution of all funds to LEAs.
- c. As of June 30, 2020, the NC Public School Insurance Fund (NC PSIF) closed and finalized all property insurance claims related to Hurricane Florence. A final payout of \$55,536,478.34 was distributed to PSIF members for property claims resulting from Hurricane Florence. A spreadsheet reflecting all closed claims is attached.
NOTE: The payment of insurance claims was in addition to the allocated funding LEAs received from the State disaster assistance.
- d. S.L. SL 2018-136, subsection 6.1.(6) and SL 2018-138 subsections 1.3(1) require all LEAs to reimburse any alternative funds received from insurance or other resources, back to the applicable funding source. Funds for school nutrition equipment and inventory replacement were allocated to LEAs, but the total amounts were not drawn down as other funds were used to support the costs.
- e. Pursuant to SL 2019 – 250, the department reallocated \$4.9M in unobligated Hurricane Florence Disaster Recovery funds from Pender County Schools to Hyde County Schools to support Hurricane Dorian disaster recovery and notified the NC General Assembly of this action.
- f. The department has issued written communications to LEAs that received State disaster assistance advising them to reconcile and report their insurance, federal, local, and other assistance used to support disaster recovery, and upon reconciliation, to return any remaining State funds.
- g. All assigned obligations have been met by the Department.

Performance Metrics

- a. Average time for Project Delivery by Program.

- Average number of days from application to fund distribution
- Average number of days from fund distribution to project commencement
- Average number of days from project commencement to project completion
- b. Amount and % spent/obligated on administrative activities by Program.
- c. Amount and % spent/obligated on behalf of recipients by Program.

Recent Activities for Current Reporting Period (October – December 2021)

No activity for this reporting period.

Contact

Office of the State Superintendent, NC Department of Public Instruction

Elizabeth City State University

4. Repairs to Residential and Academic Buildings - Hurricane Dorian

SL 2019-250 and Subsection 3.5 (c)

The intended purpose of this program is to provide funding for repairs for damages sustained from Hurricane Dorian. The repairs include roofing materials repair/replacement. Repairing water damage from intrusion through windows and walls. The repair and replacement of roofing metal damaged received by high winds.

Responsible Department and Agency

Design and Construction, Elizabeth City State

Funding Allocation Update

	Total	SL here
Appropriated		\$5,200,000.00
Expended		\$1,796,403.84
Obligated		\$2,301,327.56
Unobligated Balance		\$1,102,268.60

Summary of Activities

- First 8 buildings under construction.
- Four buildings substantially completed.
- Active Construction is ongoing on 4 buildings.
- Three projects experienced project delays due to material shortages.

Performance Metrics

- Average Time for Project Delivery by Program
- Amount and % spent/obligated on administrative activities by Program.
- Amount and % spent/obligated on behalf of recipients by Program.

Recent Activities for Current Reporting Period (October - December 2021)

Elizabeth City State University contracted for the repairs of the first 8 buildings. Two buildings remain non-constructed. Warranty period of one building has begun, three others are substantially completed but not yet certified under warranty. We have experienced material delays and shortages which has extended the construction of three roof replacements.

Contact

Onyel Bhola- Director of Facilities and Planning

Phone: 252.335.3961 Email: ogbhola@ecs.edu

Fayetteville State University

1. Capital Recovery Funds

SL 2018-136, Subsection 6.1 (7)

Responsible Department and Agency

Fayetteville State University

Funding Allocation Update

Appropriated	\$455,000
Expended	
Obligated	
Unobligated Balance	\$455,000

Summary of Activities (April-June 2019)

- a. Insurance claim information submitted to SPFIF
- b. Council of State approved and authorized payment of claim
- c. Insurance proceeds received
- d. Projects submitted to FEMA for expenses not covered by insurance
- e. Projects currently under review by FEMA

Summary of Activities (July – September 2019)

- f. Received reimbursement from FEMA for Cat B
- g. Cat E still under review

Summary of Activities (October – December 2019)

- h. No additional activity during reporting period

Summary of Activities (January – March 2020)

- i. Submitted supplemental claim information to SPFIF

Summary of Activities (April – June 2020)

- j. Claim Approved – Payment received from SPFIF

Summary of Activities (July – September 2020)

- k. No additional activity during reporting period

Recent Activities for Current Reporting Period (October - December 2021)

FSU submitted Proof of Loss/Request for Payment to State Property Fire Insurance Fund on April 23, 2019. The claim was evaluated, submitted to and approved by Council of State on June 4, 2019. Insurance proceeds were received by FSU on June 21, 2019.

FSU submitted second proof of loss to SPFIF on March 4, 2020 for additional damage.

As of March 31, 2020, claim information still being reviewed.

Claim for additional damage was approved by Council of State on April 7, 2020.

Payment from SPFIF received by University on April 18, 2020.

During this quarter, no additional activity has taken place.

Contact

Jon Parsons, PE, PEM

Associate Vice Chancellor for Facilities Management

910-672-1403

jparson2@uncfsu.edu

Golden Leaf Foundation

1. Grants to Repair, Replace, and Build New Infrastructure

SL 2016-124, subsection 4.1(7); SL 2017-119, subsection 1.2; SL 2018-5, subsection 5.6 (b)(3); SL 2018-136, subsection 6.1(21); modified by SL 2018-138, subsection 2.10; SL 2019-224, subsection 2.1(5); SL 2019-250, subsection 1.2(4)

Funds appropriated to Golden LEAF to award grants to units of local government and 501(c)(3) nonprofit organizations for repair or replacement of infrastructure and equipment damaged as a result of Hurricane Matthew, Hurricane Florence, Tropical Storm Michael, and Hurricane Dorian. Following Hurricane Matthew, funds were used construction of new infrastructure to support new housing. Funds may also be used for the construction of new infrastructure for hazard mitigation. The intent of this program is to assist eligible entities with unmet needs following FEMA Public Assistance and insurance.

Responsible Department and Agency

Golden LEAF Foundation

Funding Allocation Update

Total	SL 2016-124	SL 2017-119	SL 2018-5	SL2018-136	SL2019-224	SL2019-250
Appropriated	\$20,000,000	\$30,000,000	\$10,000,000	\$20,000,000	\$4,500,000	\$15,000,000
Expended	\$16,594,396	\$24,342,239	\$7,680,170	\$12,490,304	\$2,534,782	\$1,397,625
Obligated	\$3,405,603	\$5,557,937	\$2,319,830	\$7,480,217	\$1,962,447	\$13,538,901
Unobligated	\$0	\$99,824	\$0	\$29,479	\$2,770	\$63,473

Summary of Activities

- The Golden LEAF Board awarded funds for 215 projects in this program. 127 projects are complete. 2 projects were de-obligated.
- The primary outcome for these projects is the number of households and businesses that will benefit from the project.
- Approximately half of the projects in this program include insurance proceeds, FEMA Public Assistance, CDBG-DR or other state, local, private, or federal funds.
- More information, including the application is available online:
<https://www.goldenleaf.org/grant-seekers/disaster-recovery-programs/hurricane-florence-disaster-recovery-grant-program/>

Performance Metrics

- Average Time for Project Delivery by Program
 - 71.23 days from application to award

- 293 days from award date to first disbursement (if requested by grantee)
- 677 days from project commencement to project completion
- b. \$0 spent/obligated on administrative activities.
- c. \$0 spent/obligated on behalf of recipients.

Recent Activities for Current Reporting Period (October - December 2021)

Golden LEAF continues to work with over 85 active projects in this program. Grantees have reports due at six-month intervals and request disbursement of funds as needed. Due to lack of available contractors, and other design/engineering issues, around 20 projects are delayed and are compiling extension requests. Approximately 15 projects have submitted final reports or are approaching their project end date. The remainder of grantees have continued their progress on their projects with no anticipated delays.

Funds de-obligated from a project completed under budget are returned to the program. Unobligated funds are used for projects experiencing increased construction costs or other unforeseen issues resulting in an increased cost to complete the project.

Contact

Kasey Ginsberg

Director of Programs – Disaster Recovery

Director of External Affairs

kginsberg@goldenleaf.org, 252-442-7474 (o), 919-980-0148 (m)

2. Small Business Recovery Loans

SL 2016-124, subsection 4.1(6); SL 2018-136, subsection 6.1(22); SL 2018-138, subsection 1.3(4)

Funds appropriated to Golden LEAF to award grants to non-profit entities to make loans to small businesses affected by Hurricane Matthew, Hurricane Florence, and Hurricane Dorian. Loan funds may only be used for eligible purposes under the Small Business Administration (SBA) disaster loan assistance program. Intent of these funds is to assist businesses that were denied by SBA or do not have access to other available capital.

Responsible Department and Agency

Golden LEAF Foundation

Funding Allocation Update

	Total	SL 2016-124	SL 2018-136	SL 2018-138
Appropriated	\$5,000,000.00	\$5,000,000.00	\$5,000,000.00	\$5,000,000.00

Expended	\$4,338,601.95	\$5,000,000.00	\$1,572,419.57
Obligated	\$661,389.05	\$0.00	\$3,427,580.43
Unobligated	\$0.00	\$0.00	\$0.00

Summary of Activities

- a. All funds in this program are managed by the Rural Center. Golden LEAF previously provided funds to the Carolina Small Business Development Fund and the Community Development Initiative as well, however those grants are now closed.
- b. More than 100 loans have been made through this program.
- c. More information, including the application is available online:
<https://www.threadcap.org/disaster-recovery/>

Performance Metrics

- a. Not applicable for this program.

Recent Activities for Current Reporting Period (October – December 2021)

This program is closed.

Contact

Kasey Ginsberg

Director of Programs – Disaster Recovery

Director of External Affairs

kginsberg@goldenleaf.org, 252-442-7474 (o), 919-980-0148 (m)

Lumber River Council of Governments

1. Construct Low-Income Multifamily Housing Units in Town of Fair Bluff

SL 2017-119, 1.1(b)

The purpose of this program is to construct low-income housing complexes in the Town of Fair Bluff.

Responsible Department and Agency

Lumber River Council of Governments

Funding Allocation (Update)

Appropriated	\$5,000,000.00
Expended	\$5,000,000.00
Obligated	\$0.00
Unobligated Balance	\$0.00

Summary of Activities

- a. Civil plan design has been approved by the Town of Fair Bluff.
- b. Site permit applications are in process. Erosion control permit has been approved. Storm-water permit has been approved. Driveway application has been submitted.
- c. Wetland testing has revealed potential wetlands on the property and alternative designs are being considered to resolve the concerns.
- d. Architectural plan design is in process. The Town of Fair Bluff has been able to secure funding to upsize the water lines to the site to provide adequate water pressure to the site for fire suppression.
- e. Annexation of additional land has been approved by the Town of Fair Bluff.
- f. Foundations have been laid for the buildings. Framing has occurred on walls and roofs.
- g. Construction on project continues. Roughing on various areas of the project continue.
- h. Project construction is in final stages with finishing touches being put in place.
- i. Certificate of Occupancy was issued on 12/29/2020 for property.
- j. Management company has been secured and has started advertisement for tenants.
- k. Complex has been fully rented by the management company and tenants have moved in during January and February.
- l. Complex continues to be occupied.

Performance Metrics

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution – N/A
 - o Average number of days from fund distribution to project commencement – N/A
 - o Average number of days from project commencement to project completion – N/A
- b. Amount and % spent/obligated on administrative activities by Program.
 - o Amount Spent Administrative - \$82,618.93, 1.652%
 - o Amount Obligated Administrative - \$0.00, 0.000%
 - o Total Spent/Obligated Administrative - \$82,618.93. 1.652%
- c. Amount and % spent/obligated on behalf of recipients by Program.
 - o Amount Spent Program - \$4,917,381.07, 98.348%
 - o Amount Obligated Program - \$0.00, 0.000%
 - o Total Spent/Obligated Program - \$4,917,381.07, 98.348%

Recent Activities for Current Reporting Period (October - December 2021)

The units continue to be occupied and the management company is currently overseeing the property. No new activity this quarter.

Contact

David Richardson, Executive Director, Lumber River Council of Governments, 910-775-9752

North Carolina Community College System

2. Stabilization Reserve to Offset Impact of Enrollment Declines at Community Colleges

SL 2017-119, Subsection 1.4

The NC Community College System received \$2.7 million to distribute to community colleges suffering enrollment declines related to Hurricane Matthew. These funds will allow the community colleges to continue to offer the same level of services to students, when they return to community colleges. The NC Community College System's 2018-19 enrollment growth budget request shall include any permanent declines in enrollment resulting from Hurricane Matthew.

Responsible Department and Agency

NC Community College System, with funds allocated to the community colleges by the State Board of Community Colleges.

Funding Allocation Update

Appropriated	\$2,700,000.00
Expended	\$2,699,829.73
Obligated	\$0.00
Unobligated Balance	\$170.27

Summary of Activities

- a. The State Board of Community Colleges allocated funds (August 2017, FC-12) to eleven community colleges who documented Matthew-related enrollment declines.
- b. To continue their ability to address student needs post-Hurricane Matthew, community colleges received an additional \$1.8 million nonrecurring in 2018-19.

Performance Metrics

100% of these funds were spent on behalf of the community colleges (0% kept for administrative activities).

Recent Activities for Current Reporting Period (October - December 2021)

No activities for the current reporting period. Project was completed during FY2017-18.

Contact

Alexander Fagg, Director of Government Relations, NCCCS
fagg@nccommunitycolleges.edu 919-807-7077

3. Budget Stabilization Funds for the NC Community College System

SL 2018-136, Subsection 6.1(9)

The North Carolina Community College System received funding to offset an anticipated tuition receipts shortfall at affected community colleges due to enrollment declines caused by Hurricane Florence.

Responsible Department and Agency

NC Community College System, with funds allocated to the community colleges by the State Board of Community Colleges.

Funding Allocation Update

Appropriated	\$8,500,000.00
Expended	\$8,021,644.00
Obligated	\$0.00
Unobligated Balance	\$478,356.00

Summary of Activities

Through December 2019, NCCCS has expended \$7.9 million to offset lower receipt collections at community colleges due to Hurricane Florence. The remaining funds were drawn in the period from April to June 2020. Due to higher than expected FY2019-20 final receipts, NCCCS refunded \$478,356 in September 2020.

Performance Metrics

100% of the funds spent went directly to the colleges (0% spent on administrative activities by the System Office).

Recent Activities for Current Reporting Period (October - December 2021)

There are no activities for the current reporting period. The unobligated balance was returned to DPS in September 2020.

Contact

Alexander Fagg, Director of Government Relations, NCCCS
fagg@nccommunitycolleges.edu 919-807-7077

4. Emergency Grants for Postsecondary Students

SL 2018-136, Subsection 6.1(10) – Appropriation

SL 2018-136, Subsection 5.3(f) – Eligibility

Emergency scholarship grants in an amount up to \$1,250 per student are available to

eligible postsecondary students who have suffered financial hardship due to the damage and destruction from Hurricane Florence. Students must reside in a county covered under a federal disaster declaration. An emergency grant shall be used to mitigate the impact of Hurricane Florence on a student so that his or her postsecondary education in a North Carolina community college continues uninterrupted. These funds may be used to cover any expenses that support a student's continued enrollment, including costs related to transportation, textbooks, tuition, fees, and living expenses.

Responsible Department and Agency

NC Community College System, with funds allocated to community colleges by the State Board of Community Colleges and then distributed to students continuing their enrollment.

Funding Allocation Update

Appropriated	\$5,000,000.00
Expended	\$4,998,772.21
Obligated	\$0
Unobligated Balance	\$1,227.79

Summary of Activities

- a. Through June 2020, nearly \$5 million has been awarded to 5,241 eligible students at 22 colleges.
- b. Students used the funds for food, housing, clothing, and supplies to continue their education. Many students who finished their education during this time have reported that they could not have graduated without the assistance of these scholarship grants.

Performance Metrics

1. Average size of award (system wide average) = \$953.83 per student
2. Range of students served = 1,209 students served at Cape Fear Community College; to five students served at Central Carolina Community College.
3. 100% of the funds were spent on behalf of the students (0% on administrative activities).

Recent Activities for Current Reporting Period (October – December 2021)

The community colleges awarded its final Hurricane Florence Emergency Grants to affected students in spring semester 2020. These remaining balance in the program is due to refunds from two students who did not use the aid. These funds were returned to DPS in September 2020.

Contact

Alexander Fagg, Director of Government Relations, NCCCS
fagga@ncccommunitycolleges.edu 919-807-7077

5. Capital Recovery Funds

SL 2018-136, 6.1(8)

Community colleges received funds to repair local community college facilities damaged by Hurricane Florence. These funds were appropriated to the North Carolina Community College System Office, who distributes these funds to the colleges as reimbursement for actual expenses.

Responsible Department and Agency

NC Community College System, with funds distributed to the community colleges on a reimbursement basis.

Funding Allocation Update

Appropriated	\$5,000,000.00
Expended	\$1,748,987.11
Obligated	\$1,749,922.89
Reduction	(\$1,500,000.00)*
Unobligated Balance	\$1,090.00

*Amount reduced in SL 2019-224, Sec 1.3.

Summary of Activities

- a. Through September 2021, nine colleges have requested reimbursements for 23 Hurricane Florence-related projects. Examples of these projects include repairs to instructional spaces and campus-wide safety protection (at Carteret Community College).
- b. The overall appropriation was reduced by \$1.5 million in the 2019 Disaster Recovery Response bill. These funds were re-directed to help those colleges whose enrollment services were directly impacted by Hurricane Florence. (SL 2019-224)

Performance Metrics

- a. Thirteen projects (of 24, or 54%) have been closed out.
- b. Projects were closed and state funds were refunded if the college received reimbursement from insurance settlements or federal funding.
- c. 100% of the funds were spent directly on capital projects at the community colleges (0% was retained for administrative expenses).

Recent Activities for Current Reporting Period (October - December 2021)

In the fourth quarter 2021 (October-December) three colleges requested funds for three Hurricane Florence-related projects, totaling \$14,009.82.

Alexander Fagg, Director of Government Relations, NCCCS
fagg@nccommunitycolleges.edu 919-807-7077

6. Hurricane Florence Disaster Assistance for FTE Losses

SL 2019-224, Section 2.1(1)

The North Carolina Community College System Office received \$6.4 million to offset the full-time equivalent (FTE) losses at affected community colleges due to enrollment declines caused by Hurricane Florence. When calculating the enrollment growth budget request for the 2020-2021 fiscal year, the North Carolina Community College System Office shall adjust the FTE to reflect the FTE lost due to Hurricane Florence.

Responsible Department and Agency

The NC Community College System, with funds to be distributed to affected community colleges.

Funding Allocation Update

Appropriated	\$6,400,000.00
Expended	\$6,399,997.79
Obligated	\$ 0.00
Unobligated Balance	\$ 2.21

Summary of Activities

- Funds were distributed in October 2019 to 19 colleges who suffered enrollment declines due to Hurricane Florence.
- These funds were used by colleges to continue to offer the same level of student services and instruction that were offered prior to Hurricane Florence.
- All these funds have been expended by the colleges, as of June 29, 2021.

Performance Metrics

100% was spent/obligated directly on behalf of the community colleges (0% retained for administrative activities)

Recent Activities for Current Reporting Period (October - December 2021)

The final expenditures for Hurricane Florence Disaster Assistance for FTE Losses were recorded in June 2021, leaving a residual balance. No activity occurred during the current reporting period.

Contact

Alexander Fagg, Director of Government Relations, NCCCS

fagga@ncccommunitycolleges.edu 919-807-7077

Department of Natural and Cultural Resources

1. Supplemental Funds for Aquarium at Fort Fisher

SL 2019-224 and Subsection 2.1 (6)

\$5,000,000 to the Department of Natural and Cultural Resources to support the aquarium at Fort Fisher.

SL 2020-97, Section 3.8

SECTION 3.8. Notwithstanding Section 3.1(b) of S.L. 2018-134 or any other provision of law restricting the purposes for which funds drawn from the Hurricane Florence Disaster Recovery Fund may be used, funds appropriated from that Fund in S.L. 2019-224 and allocated to the Department of Natural and Cultural Resources for the aquarium at Fort Fisher may be used for the renovation or expansion of the aquarium.

These funds will be used to supplement an existing project that is in the very early phases of design. The \$5M was received from DPS and coded to the Capital Improvement Project Fund Code 42014 4G02.

Responsible Department and Agency

Department of Natural and Cultural Resources, NC Aquariums Division

Funding Allocation Update

Appropriated	\$5,000,000.00
Expended	\$403,038.30
Remaining Balance	\$4,596,961.70
Obligated	\$909,608.00
Unobligated Balance	\$3,687,353.70

Summary of Activities

All the funds will be used for Fort Fisher Renovations and Expansion project. It's a \$25M-30M project. This \$5M will be used towards the design and/or construction of the project. While we work through the design process of the larger project, we are knocking out some high priority smaller repairs/renovations now with this funding that we feel cannot wait until the larger project is approved. We have approximately \$909,608 of this fund obligated to three small projects (HVAC repair, Electrical repair, and roof repair projects).

HVAC Repair Project

Replacement of AHU 1-96, AHU-10 & CU 1-96 - The Aquarium at Fort Fisher needs to replace

two Air Handler Units and associated Condenser. All units are over 10 years old, heavily corroded and are beginning to fail. Repair is not a feasible option at this point.

Electrical Repair Project

The Automatic Transfer Switch has aged and is operating intermittently causing the generator to remain active when normal power is restored. This is a potential life safety issue.

Performance Metrics

These funds will be used to supplement an existing project that is in the very early phases of design. This \$5M will be used towards the design and/or construction of the project. We are easily at least two years out before starting construction.

Recent Activities for Current Reporting Period (October – December 2021)

We have approximately \$909,608 obligated to three small projects (HVAC repair, Electrical repair, and roof repair projects).

HVAC Repair Project

Replacement of AHU 1-96, AHU-10 & CU 1-96 - The Aquarium at Fort Fisher needs to replace two Air Handler Units and associated Condenser. All units are over 10 years old, heavily corroded and are beginning to fail. Repair is not a feasible option at this point.

Electrical Repair Project

The Automatic Transfer Switch has aged and is operating intermittently causing the generator to remain active when normal power is restored. This is a potential life safety issue.

Contact

Sharon Peters
Budget Officer
919 814 6725 Office
919 733 6993 Fax
Sharon.peters@ncaquariums.com

North Carolina Housing Finance Agency

1. Housing Rehabilitation Loan Pool Disaster Recovery

SL 2016-124, 4.1(1)

Through the Disaster Recovery Act of 2016, the General Assembly authorized an allocation of \$20 million to the North Carolina Housing Finance Agency (the Agency) through the North Carolina Housing Trust Fund for eligible projects under Chapter 122 of the General Statutes. Notwithstanding G.S. 122E-6, these funds shall directly benefit persons and families affected by Hurricane Matthew, the western wildfires, or Tropical Storms Julia and Hermine whose incomes do not exceed one hundred percent (100%) of the area's median income, with adjustments for family size, according to the latest figures available from the US Department of Housing and Urban Development.

Responsible Department and Agency

North Carolina Housing Finance Agency

Funding Allocation Update

Appropriated	\$20 million (DRA16)
Expended	\$16,174,318
Obligated	\$3,825,682
Unobligated Balance	\$0

Summary of Activities

- a. 477 Single-family homes in the ESFRLP-DR Portal with funds encumbered
- b. 136 Single-family homes under construction
- c. 337 Single-family homes complete
- d. 48 Multi-family homes complete

Recent Activities for Current Reporting Period (October - December 2021)

- a. The Covid-19 pandemic continues to impede construction progress.
- b. Supply chain disruptions are causing massive delays while contractors wait in windows, HVAC equipment, flex-duct, fasteners, etc.
- c. Several single-family units have dropped out of the queue because they are being addressed by RebuildNC.
- d. After consulting partners, we are considering opening the queue to Florence Survivors

Contact

Will Parry-Hill, wphill@nchfa.com, (919) 877-5605

2. Rental Production Program-Disaster Recovery

SL 2018-136, 6.1(28)

Through the Disaster Recovery Act of 2018, the General Assembly authorized an allocation of \$10 million to the North Carolina Housing Finance Agency (the Agency). These funds have been allocated to the Rental Production Program-Disaster Recovery (RPP-DR) to promote new production of affordable rental homes in the federally declared disaster counties. RPP-DR is to be used as subordinate financing on qualified developments receiving federal Low-Income Housing Tax Credits under section 42 of the federal Internal Revenue Code.

Responsible Department and Agency

North Carolina Housing Finance Agency

Funding Allocation Update

Appropriated	\$10 million (DRA18)
Expended	\$5,518,000
Obligated	\$4,482,000
Unobligated Balance	\$0

Summary of Activities

Awards were made and announced on August 9, 2019. Awards were made to eleven developments in eleven counties with a total of 790 new apartment homes affordable for working families. These investments will leverage \$112 million of private and other public funds.

Recent Activities for Current Reporting Period (October - December, 2021)

- a. Farrington Trace apartments in Pitt County, Meadow Branch apartments in Robeson County, Harbor Meadows apartments in Brunswick County, 703 Carolina Avenue apartments in Craven County, Springfield Park in Onslow County, and Madison Grove in Duplin County have drawn funds.
- b. Many of these developments received a one year placed-in-service deadline extension due to the Covid-19 federal disaster declaration.

Contact

Will Parry-Hill, wphill@nchfa.com, (919) 877-5605

Office of State Budget and Management

1. State Match for Federal Assistance Programs

SL 2016-124; Section 4.1 (4)

The purpose of this program is to provide funds to state agencies from the State Emergency and Disaster Relief Fund (SERDF) related to Hurricane Matthew for the required state match for various federal programs that administer disaster recovery assistance programs.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$66,228,370.00
Expended	\$58,119,147.00
Obligated	\$ 8,109,223.00
Unobligated Balance	\$.00

Summary of Activities

State match funds requested from the SERDF by state agencies were transferred to the appropriate agency to facilitate continued funding for administration of federal disaster recovery programs.

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October – December 2021)

Funds were transferred from the SERDF as requested by state agencies during the quarter.

Contact

Mercidee W. Benton

(984) 236-0672

Mercidee.Benton@osbm.nc.gov

2. State Match for Federal Assistance Programs

SL 2017-119; Section 1 (5)

The purpose of this program is to provide funds to state agencies from the State Emergency and Disaster Relief Fund (SERDF) related to Hurricane Matthew for the required state match for various federal programs that administer disaster recovery assistance programs.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$22,300,000.00
Expended	\$20,012,100.00
Obligated	\$ 2,287,900.00
Unobligated Balance	\$.00

Summary of Activities

State match funds requested from the SERDF by state agencies were transferred to the appropriate agency to facilitate continued funding for administration of federal disaster recovery programs.

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October - December 2021)

Funds were transferred from the SERDF as requested by state agencies during the quarter.

Contact

Mercidee W. Benton

(984) 236-0672

Mercidee.Benton@osbm.nc.gov

3. State Match for Federal Assistance Programs

SL 2018-5; Section 5.6(b)(1)

The purpose of this program is to provide funds to state agencies from the State Emergency and Disaster Relief Fund (SERDF) related to Hurricane Matthew for the required state match for various federal programs that administer disaster recovery assistance programs.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$14,500,000.00
Expended	\$ 5,349,427.00
Obligated	\$ 9,150,573.00
Unobligated Balance	\$.00

Summary of Activities

N/A

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October - December 2021)

Funds were transferred from the SERDF as requested by state agencies during the quarter.

Contact

Mercidee W. Benton

(984) 236-0672

Mercidee.Benton@osbm.nc.gov

4. Grants-In-Aid

SL 2018-5; Section 5.6(b)(4)

The purpose of this program is to provide pass through grant-in-aid funds appropriated by the NC General Assembly to the towns of Princeville and Fair Bluff for contractual services related to management and use of disaster recovery funds for Hurricane Matthew.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$	700,000.00
Expended	\$	656,250.00
Obligated	\$	43,750.00
Unobligated Balance	\$	0.00

Summary of Activities

Grant-in-aid funds requested from the towns for which funds were appropriated for were processed to facilitate continued funding for administration of disaster recovery programs.

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October - December 2021)

Grant-in-aid funds from the towns were processed as requested during the quarter.

Contact

Nels Roseland, OSBM Deputy Director

(984) 236-0731

Nels.roseland@osbm.nc.gov

5. Grants-In-Aid

SL 2019-224; Section 2.1 (2)

The purpose of this program is to provide pass through grant-in-aid funds appropriated by the NC General Assembly to the directed units of local governments outlined in the legislation for varied projects and purposes related to the use of disaster recovery funds for Hurricane Florence.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$ 27,868,000.00
Expended	\$ 12,735,307.00
Obligated	\$ 15,132,983.00
Unobligated Balance	\$ 0.00

Summary of Activities

Grant-in-aid funds requested from the local government units for which funds were appropriated for were processed to facilitate continued funding for administration of disaster recovery programs.

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October - December 2021)

Grant-in-aid funds from the local government units were processed as requested during the quarter.

Contact

Nels Roseland, OSBM Deputy Director
(984) 236-0731
Nels.roseland@osbm.nc.gov

6. State Match for Federal Assistance Programs

SL 2019-250; Section 1.1 (2) a

The purpose of this program is to provide funds to state agencies from the State Emergency and Disaster Relief Fund (SERDF) related to Hurricane Matthew for the required state match for various federal programs that administer disaster recovery assistance programs.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$11,197,013.00
Expended	\$.00
Obligated	\$11,197,013.00
Unobligated Balance	\$.00

Summary of Activities

N/A

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October - December 2021)

N/A

Contact

Mercidee W. Benton
(984) 236-0672
Mercidee.Benton@osbm.nc.gov

7. State Match for Federal Assistance Programs

SL 2019-250; Section 1.1 (2) b

The purpose of this program is to provide funds to state agencies from the State Emergency and Disaster Relief Fund (SERDF) related to Hurricane Michael for the required state match for various federal programs that administer disaster recovery assistance programs.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$ 4,176,245.00
Expended	\$ 1,183,352.00
Obligated	\$ 2,992,893.00
Unobligated Balance	\$.00

Summary of Activities

State match funds requested from the SERDF by state agencies were transferred to the appropriate agency to facilitate continued funding for administration of federal disaster recovery programs.

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October - December 2021)

Funds were transferred from the SERDF as requested by state agencies during the quarter.

Contact

Mercidee W. Benton

(984) 236-0672

Mercidee.Benton@osbm.nc.gov

8. State Match for Federal Assistance Programs

SL 2019-250; Section 1.1 (2) c

The purpose of this program is to provide funds to state agencies from the State Emergency and Disaster Relief Fund (SERDF) related to Hurricane Dorian for the required

state match for various federal programs that administer disaster recovery assistance programs.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

	Total	SL 2019-250
Appropriated	\$17,800,000.00	
Expended	\$10,229,535.00	
Obligated	\$ 7,570,465.00	
Unobligated Balance	\$.00

Summary of Activities

State match funds requested from the SERDF by state agencies were transferred to the appropriate agency to facilitate continued funding for administration of federal disaster recovery programs.

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October - December 2021)

Funds were transferred from the SERDF as requested by state agencies during the quarter.

Contact

Mercidee W. Benton

(984) 236-0672

Mercidee.Benton@osbm.nc.gov

9. State Match for Federal Assistance Programs

SL 2019-250; Section 1.2 (1)

The purpose of this program is to provide funds to state agencies from the State Emergency and Disaster Relief Fund (SERDF) related to Hurricane Dorian, recent storms, and future emergencies, as authorized by G.S 166-A;19.42 for the required state match for various federal programs that administer disaster recovery assistance programs.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$ 5,000,000.00
Expended	\$.00
Obligated	\$ 5,000,000.00
Unobligated Balance	\$.00

Summary of Activities

N/A

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October - December 2021)

N/A

Contact

Mercidee W. Benton

(984) 236-0672

Mercidee.Benton@osbm.nc.gov

10.Grants-In-Aid

SL 2019-250; Section 1.2 (8)

The purpose of this program is to provide pass through grant-in-aid funds appropriated by the NC General Assembly to Hyde County for construction of a pump station and related watershed restoration for the Lake Mattamuskeet watershed.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$ 1,800,000.00
Expended	\$ 100,000.00
Obligated	\$ 1,700,000.00
Unobligated Balance	\$.00

Summary of Activities

Grant-in-aid funds requested from Hyde County were processed to facilitate continued funding for the specific project that funds were appropriated for.

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October – December 2021)

Grant-in-aid funds from Hyde County were processed as requested during the quarter.

Contact

Nels Roseland, OSBM Deputy Director

(984) 236-0731

Nels.roseland@osbm.nc.gov

11. Disaster Housing Recovery Support

SL 2018-136, Subsection 6.1(24)

The purpose of this program is to provide funds for the following housing related matters:

a) Housing elevation, acquisition, and mitigation reconstruction for homes not covered by the Hazard Mitigation Grant Program, b) State Acquisition Relocation funds, which enable low-to-moderate-income homeowners to purchase homes, and c) Flood insurance subsidies.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$	23,000,000
Expended	\$	14,983,140
Obligated	\$	8,016,860
Unobligated Balance	\$	0

Summary of Activities

Where a total of \$23 million in grant awards have been committed or obligated to assist 10 severely impacted counties or communities to provide them with critical and pressing needs grants. These first phase grants would assist Brunswick, Craven, Duplin, Jones, New Hanover, Onslow, Pender, Robeson and Scotland Counties, and the City of Lumberton, to address the most severe hardship cases involving low to moderate income, elderly and/or disabled homeowners who are living in unsafe, unsanitary housing that pose urgent safety

or public health risk due to mold or potential structural failure. These grants can also be used for mitigation reconstruction and acquisition activities. A total of \$5.8 million in non-profit grant awards have been provided to Habitat for Humanity affiliates in eastern North Carolina, Wilmington Area Rebuilding Mission (WARM) (\$1 million grant), Baptists on Mission (\$1 million grant), and United Methodists (\$1 million grant) to support emergency housing repairs, mitigation reconstruction and acquisition activities that will benefit hurricane displaced families. The remaining funds are programmed to support housing recovery expenses associated with repairs, acquisitions and reconstruction of storm impacted homes.

Performance Metrics

- a. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution **153**
 - o Average number of days from fund distribution to project commencement **16**
 - o Average number of days from project commencement to project completion **122**
- b. Amount and % spent/obligated on administrative activities by Program.
823,903/5%
- c. Amount and % spent/obligated on behalf of recipients by Program.
\$14,159,237/95%

Recent Activities for Current Reporting Period (October – December 2021)

- Twenty-nine (29) owners had their home repairs completed or had their homes reconstructed or had been bought out of flood prone areas this quarter
- Thirty-one (31) owner projects were 80% complete by the end of this quarter

Contact

Nels Roseland, OSBM Deputy Director

(984) 236-0731

Nels.roseland@osbm.nc.gov

12. Housing Needs

SL 2017-119, Subsection 1.1(a)

The purpose of this program is to provide funds for the following: 1) Repair of owner-occupied low-to-moderate-income housing not covered by CDBG-DR Program funding 2) Repair of low-to-moderate-income rental housing not covered by CDBG-DR Program funding 3) Housing elevation, acquisitions, and mitigation reconstruction for homes not covered by the Hazard Mitigation Grant Program 4) State Acquisition Relocation funds,

which enable low-to-moderate-income homeowners to purchase homes 5) Flood insurance subsidies and 6) Temporary housing for storm victims.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$ 20,000,000
Expended	\$ 10,812,728
Obligated	\$ 9,805,110
Unobligated Balance	\$ 0

Summary of Activities

Where a total of 13 counties have entered into housing recovery grant contracts with the State. Of these, a total of 190 homeowners have been approved for assistance. One hundred thirty (130) owners have completed their homes repairs or have had their homes reconstructed or have been bought out of flood prone areas. Forty-nine (49) owner projects are in process.

Performance Metrics

- d. Average Time for Project Delivery by Program
 - o Average number of days from application to fund distribution **153**
 - o Average number of days from fund distribution to project commencement **16**
 - o Average number of days from project commencement to project completion **122**
- e. Amount and % spent/obligated on administrative activities by Program.
\$1,085,489/10%
- f. Amount and % spent/obligated on behalf of recipients by Program.
\$10,812,728/90%

Recent Activities for Current Reporting Period (October – December 2021)

- Ten (10) owners had their home repairs completed or had their homes reconstructed or had been bought out of flood prone areas this quarter
- Eleven (11) owner projects were 80% complete by the end of this quarter

Contact

Nels Roseland, OSBM Deputy Director
(984) 236-0731

Nels.roseland@osbm.nc.gov

13.State Match for Federal Assistance Programs

SL 2020-97; Section 2.6.(d)(1)

The purpose of this program is to provide funds to state agencies from the State Emergency and Disaster Relief Fund (SERDRF) related to Hurricane Matthew for the required state match for various federal programs that administer disaster recovery assistance programs.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$ 10,423,729.00
Expended	\$.00
Obligated	\$ 10,423,729.00
Unobligated Balance	\$.00

Summary of Activities

N/A

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October - December 2021)

N/A

Contact

Mercidee W. Benton

(984) 236-0672

Mercidee.Benton@osbm.nc.gov

14.State Match for Federal Assistance Programs

SL 2020-97; Section 2.6.(d)(2)

The purpose of this program is to provide funds to state agencies from the State Emergency and Disaster Relief Fund (SERDRF) related to Hurricane Dorian for the required state match for various federal programs that administer disaster recovery assistance

programs.

Responsible Department and Agency

NC Office of State Budget and Management

Funding Allocation Update

Appropriated	\$	2,779,661.00
Expended	\$.00
Obligated	\$	2,779,661.00
Unobligated Balance	\$.00

Summary of Activities

N/A

Performance Metrics

N/A

Recent Activities for Current Reporting Period (October – December 2021)

N/A

Contact

Mercidee W. Benton

(984) 236-0672

Mercidee.Benton@osbm.nc.gov

North Carolina State Education Assistance Authority

1. Emergency Grant for Affected Postsecondary Students (NCICU)

SL2018-136, Section 6.1 (12)

The Emergency Scholarship Grant Funds are provided to mitigate the impact for postsecondary students who have suffered financial hardship due to damage and destruction from Hurricane Florence. An emergency scholarship in the amount of up to one thousand two hundred fifty dollars (\$1,250) per student will be used so that his or her postsecondary education continues uninterrupted. The students are required to reside in or attend an institution located in a county designated under a major disaster declaration as a result of Hurricane Florence.

Responsible Department and Agency

North Carolina State Education Assistance Authority - NCSEAA

Funding Allocation Update

	Total	SL here
Appropriated	\$1,000,000.00	
Expended	\$ 862,623	
Obligated		
Unobligated Balance	\$ 137,377	

Summary of Activities

- Assisted students with grants for tuition and fees.
- Assisted students with grants for housing and living expenses.
- Assisted students with grants for transportation.
- Provided assistance over a period of three semesters.

Performance Metrics

- Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution **N/A**
 - Average number of days from fund distribution to project commencement **N/A**
 - Average number of days from project commencement to project completion **N/A**
- Amount and % spent/obligated on administrative activities by Program. **None**
- Amount and % spent/obligated on behalf of recipients by Program. **None**

Recent Activities for Current Reporting Period (October - December 2021)

No new awards were made during this period. No refunds were received during this period.

Contact

Kevin J. Lineberry | Associate Director for Higher Education Programs

North Carolina State Education Assistance Authority - NCSEAA

2 UNC-TV Drive | Research Triangle Park, NC 27709

Office: 919.248.4679 | Fax: 919.248.6679 | Cell: 919.937.7884

UNC Pembroke

1. Emergency Grants for Affected Postsecondary Students

SL 2018-136 6.1(11)

In an October special legislative session, the 2018 General Assembly appropriated \$2,000,000 from the statewide Hurricane Florence Disaster Recovery Fund to the Board of Governors to establish the Hurricane Florence Emergency Grant Program for Postsecondary Students. Funding from this program will provide emergency scholarship grants in an amount up to one thousand two hundred fifty dollars (\$1,250) for each eligible UNC System student who has suffered financial hardship due to the damage and destruction from Hurricane Florence. These funds may be used to cover any expenses that support a student's continued enrollment, including costs related to transportation, textbooks, tuition, fees and living expenses.

Responsible Department and Agency

UNC-Pembroke, Financial Aid

Funding Allocation Update

Appropriated	\$250,000
Expended	\$ 97,000
Obligated	\$0.00
Unobligated Balance	\$153,000

Summary of Activities

UNCP awarded \$ 97,000 in grants to students during the Fall and Spring semesters for the 18/19 school year.

Performance Metrics

- a. Average time for Project Delivery by Program
 - Average number of days from application to fund distribution – 4 days
 - Average number of days from fund distribution to project commencement – N/A
 - Average number of days from project commencement to project completion – N/A
- b. Amount and % spent/obligated on administrative activities by Program – 0%
- c. Amount and % spent/obligated on behalf of recipients by Program – 38.8% (97,000/250,000)

Recent Activities for Current Reporting Period (October - December 2021)

UNCP did not award any new grants during this period. This program is finished, and unobligated monies have been returned previously.

Contact

Michelle Donegain

Controller

Michelle.donegain@UNCP.edu

910-521-6583

2. Capital Recovery Fund

SL 2018-136 6.1(7)

In an October special legislative session, the 2018 General Assembly appropriated \$30,000,000 from the statewide Hurricane Florence Disaster Recovery Fund to the Board of Governors for repair and renovation of capital facilities at three campuses that sustained the heaviest damage from Hurricane Florence. Allocations are to be made to Fayetteville State University, UNC Pembroke, and UNC Wilmington.

Under the provisions of the law, institutions will diligently seek alternative funds to cover the needs for which state funds are being provided and, if funds are provided from these alternative sources, return the state funds.

Responsible Department and Agency

Please include the Department, Agency and Division responsible here.

Funding Allocation Update

Appropriated	\$829,499
Expended	\$800,000
Obligated	\$0
Unobligated Balance	\$29,499

Summary of Activities

- a. Foundation work required for soil conditions degraded by flooding and “hardening” finishes, doors, etc. to increase building system resilience for West Hall not covered by FEMA or insurance.

- b. Identified areas of mitigation to reduce future risk and damages

Performance Metrics

- a. Average time for Project Delivery by Program
- Average number of days from application to fund distribution – N/A
 - Average number of days from fund distribution to project commencement – N/A
 - Average number of days from project commencement to project completion Approximately 638 days (October 2018 – July 2020)
- b. Amount and % spent/obligated on administrative activities by Program – 0%
- c. Amount and % spent/obligated on behalf of recipients by Program – 100%

Recent Activities for Current Reporting Period (October - December 2021)

This program is finished and unobligated monies were returned during the current reporting period.

Contact

Michelle Donegain

Controller

Michelle.donegain@UNCP.edu

910-521-6583

UNC Wilmington

1. Repairs and Renovations to Dobo Hall – Hurricane Florence

SL 2019-224 and Subsection 2.1.(8)c.

The intended purpose of this program is to provide funding for repairs and renovations for damages sustained from Hurricane Florence. Hurricane Florence caused extensive damage to Dobo Hall, the primary lab research facility on the main campus. A complete remediation and renovation to Dobo Hall was required, and temporary lab and classroom facilities were necessary in the interim to provide teaching and research space and continue the mission of the University.

Responsible Department and Agency

Architectural and Construction Services, UNC-Wilmington

Funding Allocation Update

	Total	SL here
Appropriated	\$8,000,000.00	
Expended	\$8,000,000.00	
Obligated		
Unobligated Balance	\$0.00	

Summary of Activities

- Short-term space was provided via the re-construction and upfit of modular buildings that could be immediately positioned on the UNCW campus and Infrastructure work was included in this scope of work.
- Mid-term space better suited to our research and teaching needs was planned through the procurement and placement of modular classroom teaching and research laboratory units. The scope included the pre-engineered structures and supporting parking and infrastructure, and will remain operational until Dobo Hall is complete and suitable for re-use.
- The project required the remediation of hazardous materials and conditions to enable full building access, including mold and chemical contaminants that were verified with testing along with removal of all equipment, chemicals, glassware, furniture, etc. The project scope also includes repair of nearly 500 incomplete structural connections resident from the original construction, replacement of the roof and supporting deck, all exterior windows, interior finishes and permanent furnishings, all building mechanical and electrical systems, life safety and controls that were destroyed by several days of water intrusion during the storm.

Performance Metrics

- Average Time for Project Delivery by Program
- Amount and % spent/obligated on administrative activities by Program.
- Amount and % spent/obligated on behalf of recipients by Program.

Recent Activities for Current Reporting Period (October - December 2021)

Although work is still underway to replace equipment, labware and furniture destroyed in the storm, faculty and staff began setting up department offices and labs in August of 2020 and Dobo Hall reopened for fall 2020 semester. No recent activity to report.

Contact

Joe Stewart, Architectural and Construction Services, UNCW
910-962-3599
stewartw@uncw.edu

North Carolina Wildlife Resources Commission

1. Water Vessels (Abandoned and Derelict Vessels)

SL 2019 224 2.1 (10), SL 2020-74 HB 308

SL and Subsection SL 2019 224 2.1 (10), SESSION LAW 2020-74 HB 308

The North Carolina Wildlife Resources Commission received a General Fund appropriation of \$1,000,000 to inspect, investigate, and remove derelict and abandoned water vessels which were a result of Hurricane Florence and other past storms.

Responsible Department and Agency

North Carolina Wildlife Resources Commission

Funding Allocation Update

	Total	SL here
Appropriated	\$1,000,000.00	
Expended	\$942,280.28	
Obligated	\$1,000,000.00	
Unobligated Balance	\$0.00	

Summary of Activities

NC Wildlife Resources Commission (NCWRC) has defined the Abandoned and Derelict Vessel project plan to ensure efficient use of the funding. NCWRC has also requested and was granted revisions to the Abandoned and Derelict Vessel legislation, SESSION LAW 2020-74 HOUSE BILL 308 contains the revisions. A project lead has been named and work on the project plan is underway. NCWRC has removed 40 abandoned vessels and plans to remove 50 total with remaining appropriated funds.

Performance Metrics

- Average Time for Project Delivery by Program
 - Average number of days from application to fund distribution **TBD**
 - Average number of days from fund distribution to project commencement **TBD**
 - Average number of days from project commencement to project completion: **60 days**
- Amount and % spent/obligated on administrative activities by Program.
 - **Amount Spent: \$24,624.52**
 - **% spent on Administrative Activities: 2.46%**
- Amount and % spent/obligated on behalf of recipients by Program.
 - **Amount Spent: \$891,080.28**
 - **% spent on behalf of recipients of by Program: 86.64%**

Recent Activities for Current Reporting Period (October – December 2021)

NCWRC's Abandoned and Derelict Vessel Removal Program has continued to implement a removal plan and strategy for removing abandoned and derelict vessels caused by Hurricane Florence and other past storms. In total 40 vessels have been removed with the \$1 million dollar appropriation. We are forecasted to remove approximately ten more vessels with our remaining funds. Removal projects under this funding should conclude by the 2nd quarter of this calendar year.

Contact

Ashton Godwin
Legislative Liaison
NC Wildlife Commission
919.616.6507

Appendices

1. Comprehensive State and Federal Funding Workbooks for Hurricanes Matthew, Florence, Michael, Dorian, and other smaller recent events.
